

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल, डुमरांव ।

Email ID – ee.dumraon.rwd@gmail.com

पत्रांक 1500/17/20

दिनांक 13/10/25

प्रेषक,

ई0 संजय कुमार
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, डुमरांव ।

सेवा में,

नोडल पदाधिकारी,
मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (MMGSUY (RRSMP GEN)
ग्रामीण कार्य विभाग, बिहार, पटना ।

विषय:— शीर्ष MMGSUY (RRSMP GEN) में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष MMGSUY (RRSMP GEN) योजना अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक का भुगतान किया जा सके।

अनु०:—

1. अधियाचना प्रमाण पत्र 1 पृष्ठ में।
2. उपयोगिता प्रमाण पत्र एक प्रति ।

विश्वासभाजन




कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्यप्रमंडल, डुमरांव ।

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

- (1) Certified that out of the Loan of Rs.2833.01505, Sanctioned under MMGSUY(RRSMP GEN), Vide Letter No.62 dated.27.07.2025, in favour of **Executive Engineer, Rural Works Department, Works Division, Dumraon**, during the year **2025-26**, an amount of Rs.2833.01505, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.0.000, remaining unutilized at the end of the year..... has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.
- (2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.


13/10/25
Divisional Accounts Officer
Rural Works Department,
Works Division, Dumraon.


13/10/25
Executive Engineer
Rural Works Department
Works Division, Dumraon.

Regulation Format for Scheme - MMGSUY (RRSMP General/SCST)

Name of the Works Division :- **Dumraon**


Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work status (WMM/ WMA/ BM/ SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bottom Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/25-26 Dumraon/01	1040200350184	Raghunathpur Station Road to Silariya Green	4.670	43.149680	260.43212	17 CMBD 2025-26	03.10.2026	ongoing	WMM/ SDBC	-	-	-	0.00000	0.00000	48.220	40.220	WMM/ SDBC in progress
2	RRSMP/25-26 Dumraon/01	1040200350185	Durga Mandir to Dharali Road	1.400	77.13700	48.10311	17 CMBD 2025-26	03.10.2026	ongoing	WMM/ BM/ SDBC	-	-	-	0.00000	0.00000	23.600	25.600	WMM/ SDBC in progress
3	RRSMP/25-26 Dumraon/01	1040200350186	Bhadrav PMGSY to Block Boundary	3.450	105.25100	185.30760	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	59.440	50.440	WMM in progress
4	RRSMP/25-26 Dumraon/01	1040200350187	Sakulpura Road to Chaugai Phadidar Road	1.200	70.90800	40.15842	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	28.107	28.107	WMM in progress
5	RRSMP/25-26 Dumraon/01	1040200350188	Atarasi path to Phadidar via sakulpura path/pura path	2.000	119.21400	65.76657	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	40.23	40.23	WMM in progress
6	RRSMP/25-26 Dumraon/01	1040200350189	Badrangar Bagan Path to Akoni Green	3.000	180.25000	99.54085	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	57.715	57.715	WMM in progress
7	RRSMP/25-26 Dumraon/01	1040200350190	Dharali Hilt to Dhuruli Green Tak Path. (Reserve person unemployed Engineer)	1.050	81.55300	47.64130	17 CMBD 2025-26	03.10.2026	ongoing	WMM/ BM	-	-	-	0.00000	0.00000	23.056	23.056	WMM/ BM in progress
8	RRSMP/24-25 Dumraon/02	1040200350118	East Shopar Men Road to Ex. Samad Late Seng Prasad	0.950	67.28662	48.74690	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	-	-	-	0.00000	0.00000	37.940	37.940	Pat Patch Completed, PCC in progress
9	RRSMP/24-25 Dumraon/02	1040200350119	L429-Chaugai to Baidi (L029)	0.780	47.72452	30.60742	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	2564	25	5.01	13.36434	13.56434	13.06400	1.500	Physically Completed
10	RRSMP/24-25 Dumraon/02	1040200350120	Repair of road from Karamsany Main road to Padar (Baidi village)	1.500	87.92543	58.30997	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	2819	25	5.01	35.12712	35.12712	37.22700	2.100	Physically Completed
11	RRSMP/24-25 Dumraon/02	1040200350121	Atyong Chaugai PMGSY Road to Thon Pandeypur dahi busi gate tak	0.700	48.99925	33.80210	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3406	25	5.01	3.26315	3.26315	31.26300	28.000	PCC 400m Completed
12	RRSMP/24-25 Dumraon/02	1040200350122	Karamsany Chaugai Path Se Rampur Nohar Tak Banjarwa Kuchi Busi Tak	2.200	139.84836	91.60380	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3163	25	5.01	56.27225	56.27225	58.37200	2.100	Physically Completed
13	RRSMP/24-25 Dumraon/02	1040200350123	Chaugai Bagan path se Chaugai Mashar tole tak sadak nirman	1.000	64.00400	41.28570	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3275	25	5.01	26.49879	26.49879	27.69800	1.200	Physically Completed
14	RRSMP/24-25 Dumraon/02	1040200350124	Mandraya Nachp PMGSY Road Se Vapur Harijan Tola Tak	2.500	162.90830	104.32790	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	2724	25	5.01	63.33230	63.33230	68.56200	5.280	Physically completed
15	RRSMP/24-25 Dumraon/02	1040200350125	AMSARI NAHAR ROAD SE to DUSADH TOLA KAMKAR TOLA	1.950	122.54129	79.90886	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3246	25	5.01	20.12075	20.12075	56.12100	36.000	Pat Patch Completed & BT 1050m Completed, PCC in progress
16	RRSMP/24-25 Dumraon/02	1040200350126	PHADIDAR APPROACH PATH SE to KOHRI TOLA MASARIYA	2.100	127.99630	82.12206	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3190	25	5.01	47.85808	47.85808	50.25800	2.300	Physically Completed
17	RRSMP/24-25 Dumraon/02	1040200350127	Chaugai Keshari road se Banatpur Shri Mandir tole	1.800	116.04227	72.74437	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3290	25	5.01	35.18106	35.18106	36.48100	1.300	Physically Completed
18	RRSMP/24-25 Dumraon/02	1040200350128	Chaugai Parab gate to Harizon tole	1.250	80.98115	54.96039	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	2637	25	5.01	16.16676	16.16676	46.16700	30.000	PCC in progress
19	RRSMP/24-25 Dumraon/02	1040200350129	Koran Sani Padar Path To Korri Tola	0.400	22.22036	14.53638	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3167	25	5.01	10.90060	10.90060	22.85100	11.550	Physically completed
20	RRSMP/24-25 Dumraon/02	1040200350130	Main Post Office To Choudhary Tola	0.450	28.11512	19.26401	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3010	25	5.01	0.00000	0.00000	18.000	16.000	Pat Patch Completed, PCC in progress
21	RRSMP/24-25 Dumraon/02	1040200350131	Quamrati Chauran Path to Pawan Tola	0.260	17.09777	11.20285	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	2877	25	5.01	0.00000	0.00000	9.380	9.280	Pat in progress
22	RRSMP/24-25 Dumraon/02	1040200350132	Marga pul Bithari path se Nachap	1.600	176.98478	127.00800	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3608	25	5.01	71.85696	71.85696	73.05700	2.000	Surface Completed
23	RRSMP/24-25 Dumraon/02	1040200350133	Marga pul se Bithari	1.200	138.54881	105.29527	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	3380	25	5.01	72.31663	72.31663	74.31700	2.000	Surface Completed
24	RRSMP/24-25 Dumraon/02	1040200350134	Bispar to Chhokri Doh Nachap	1.300	83.18060	54.93108	01 CMBD 2025-26	04/05/2026	ongoing	BM/ SDBC	-	-	-	11.74398	11.74398	33.74000	22.000	BT 450m Completed, PCC in progress


25	RRSMP-24-25 Damraon-04	1040200350100	Repair of road from Bhatpur to Nainjar	14.000	2463.74906	1824.66967	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	317.31166	317.31166	317.31166	200.00000	BM/SDBC in progress
26	RRSMP-24-25 Damraon-04	1040200350094	NH-04 To Kisinga Tola	0.500	33.328	23.16197	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	0.00000	0.00000	20.00000	20.00000	BM/SDBC in progress
27	RRSMP-24-25 Damraon-04	1040200350004	GARATHA KHURD - YOGA	2.400	182.93333	95.04834	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	8.51804	8.51804	84.51804	76.00000	BM/SDBC in progress
28	RRSMP-24-25 Damraon-04	1040200350093	NH-04 Maharaigunj to Karaman Gama	1.95	155.41734	110.31933	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	6.38803	6.38803	86.38803	80.00000	BM/SDBC in progress
29	RRSMP-24-25 Damraon-04	1040200350095	NH-04 To Karaman Tola	0.950	53.79172	34.41250	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	0.00000	0.00000	23.00000	23.00000	BM/SDBC in progress
30	RRSMP-24-25 Damraon-05	1040200350072	Alodhi (Piprah) to Tihar gram tal path nitum	2.630	256.78911	156.56191	08 CMBD 2025-26	04/06/2026	ongoing	BM/SDBC	-	-	-	13.30439	13.10459	118.65400	105.550	SDBC in progress
31	RRSMP-24-25 Damraon-05	1040200350073	BAGEN DEVILAH PATH BHADWAR MAHADEV STHAN SE to BABUHA GRAM CHANDRMA VADAV TOLA	3.900	197.62531	134.78158	08 CMBD 2025-26	04/06/2026	ongoing	BM/SDBC	-	-	-	6.13119	6.13119	73.72100	67.590	SDBC in progress
32	RRSMP-24-25 Damraon-05	1040200350079	Bhatpur Bagen Path to Dhamadi Via Kaithe Road	8.400	730.76600	594.02491	08 CMBD 2025-26	04/06/2026	ongoing	SDBC	-	-	-	46.41600	46.41600	197.78900	351.383	GSS in progress
33	RRSMP-24-25 Damraon-05	1040200350002	BRAHMPUR PEAKINAD SE to BRAHMPUR PASCHEM TOLA MAHADEV STHAN	1.500	84.56050	52.88710	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	3.34215	3.34215	27.98100	24.635	WBM Completed,SDBC in progress
34	RRSMP-24-25 Damraon-05	1040200350087	Kaithe road to Murchi tola	1.250	102.09700	70.99653	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	0.00000	0.00000	43.100	43.100	SDBC in progress
35	RRSMP-24-25 Damraon-05	1040200350090	MAIHIYA NABAR PULL SE to NIYALPUR DERA KAITHE EYM BHAGELU DERA HOTE HUE KAITHE GAUN	1.500	97.83177	66.42109	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	0.00000	0.00000	59.500	59.500	SDBC in progress
36	RRSMP-24-25 Damraon-05	1040200350091	NH10 to Piprah Village	1.350	81.78780	53.22160	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	4.08400	4.08400	40.50100	36.317	SDBC Completed,PCC in progress
37	RRSMP-24-25 Damraon-05	1040200350097	Piprah Bhatpur begun road to Piprah Via Rajpur	2.300	243.97811	136.74258	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	16.39314	16.39314	123.66700	107.214	SDBC in progress
38	RRSMP-24-25 Damraon-05	1040200350098	Bahadurpur Bagen Path to Kaithe to Nachup Gama Tola	1.550	97.10921	61.32194	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	9.15116	9.15116	31.15100	22.000	SDBC in progress
39	RRSMP-24-25 Damraon-03	1040200350060	Kowah Bhata Pool - Arhar Mahave Arhan Path via Jairampur, Rampur	3.950	468.24000	375.87101	09 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	-	-	-	62.29811	62.29811	232.29800	140.000	SDBC in progress
40	RRSMP-24-25 Damraon-03	1040200350063	Kowah Bantand to Soveran NIS-30 Mar	7.90000	844.76261	640.36687	09 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	-	-	-	76.72748	76.72748	318.72700	240.000	SDBC in progress
41	RRSMP-24-25 Damraon-03	1040200350066	KESATH BATHULI PATH MORIAN SINGH KE DERA to NONIYA BABA BATHULI	3.400	212.27907	131.77441	09 CMBD 2025-26	04/03/2026	ongoing	BM/SDBC	-	-	-	15.35083	15.35093	63.35100	48.000	SDBC in progress
42	RRSMP-24-25 Damraon-01	1040200350114	NH04 Naman To Bhariyar Road	3.800	549.98200	398.71231	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	96.47227	96.47227	216.47227	120.00000	SDBC in progress
43	RRSMP-24-25 Damraon-01	1040200350107	Ank Bus Stand To Ank Smith Tola	0.765	53.88800	35.51522	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	3.64047	3.64047	19.64047	16.000	SDBC in progress
44	RRSMP-24-25 Damraon-01	1040200350116	NH 04 Krishnabahan To Ank PMGSY Road Via Kaithe Road	4.300	337.90600	377.45163	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	108.75146	108.75146	248.75100	140.000	SDBC in progress
45	RRSMP-24-25 Damraon-01	1040200350117	Bhatpur Nainjar Mukhya Path to Bandh To Jwahi Tosari Dem	6.950	689.54900	482.18670	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	48.36902	48.16902	302.16900	254.000	SDBC in progress
46	RRSMP-24-25 Damraon-01	1040200350110	Chakki Bagen Road Via Floor ME To PWD Road	0.950	111.18100	60.48129	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	17.76699	17.76699	89.76700	32.000	SDBC in progress
47	RRSMP-24-25 Damraon-08	1040200350137	Damraon Vikarungaj Road To Vardaha Sath Tola	0.500	39.14191	27.17143	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	0.77361	0.77361	20.77361	20.0000	SDBC in progress
48	RRSMP-24-25 Damraon-08	1040200350139	Repair of road from Nawangan Block to Kakar Bhakka	3.320	251.42906	136.86871	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	10.04185	10.04185	100.0419	90.0000	SDBC in progress
49	RRSMP-24-25 Damraon-08	1040200350141	Girdhar Barwan - Sath Nahan Pool	2.625	180.70965	19.96755	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	7.88752	7.88752	92.88752	85.0000	SDBC in progress
50	RRSMP-24-25 Damraon-08	1040200350152	BASUDEWA KESHATH ROAD - GOBINDPUR	0.910	70.25351	54.55622	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	2.63581	2.63581	27.63581	25.0000	SDBC in progress
51	RRSMP-24-25 Damraon-08	1040200350153	Repair of road from Nawangan Thakurhan P.W.D. road to Bhatali via Ratnagar	1.800	122.40885	81.73557	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	8.62867	8.62867	28.62867	20.0000	SDBC in progress


अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि RRSMP (GEN) योजनान्तर्गत

1. पथ/ पुल AMSARI NAHAR ROAD SE to DUSADH TOLA KAMKAR TOLA में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा, चौगाई


सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, चौगाई


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, हुमरौंव।

Name of Road :- ANSARI NAHAR ROAD TO DUSHADH TOLA KAMAKAR TOLA . (MACHINE - BUXAR)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	GATEGORY Road	Latitude	Longitude	Event
26/ 6/ 25	16:31:27	86	0.1	290	0	2900	3364	G	25.386978	84.16372	Normal
26/ 6/ 25	16:31:43	86	0.1	300	30.5	3000	3462	G	25.386818	84.163687	Speed Breaker
26/ 6/ 25	16:32:0	86	0.1	270	31.2	2700	3167	G	25.387697	84.163988	Normal
26/ 6/ 25	16:32:18	86	0.1	290	32.5	2900	3364	G	25.388513	84.164225	Normal
26/ 6/ 25	16:32:18	86	0.1	310	31.2	3100	3561	G	25.389182	84.164175	Normal
26/ 6/ 25	16:32:53	86	0.1	270	30.3	2700	3167	G	25.389523	84.163232	Normal
26/ 6/ 25	16:33:0	86	0.1	290	32.5	2900	3364	G	25.390388	84.16276	Curve
26/ 6/ 25	16:33:0	86	0.1	280	31.2	2800	3265	G	25.390953	84.162222	Normal
26/ 6/ 25	16:33:28	86	0.1	260	30.5	2600	3069	G	25.39151	84.16143	Normal
26/ 6/ 25	16:34:4	86	0.1	250	31.2	2500	2970	G	25.39243	84.161262	Normal
26/ 6/ 25	16:35:0	86	0.1	240	32.5	2400	2872	G	25.393272	84.161565	Normal
26/ 6/ 25	16:35:50	86	0.1	290	30.5	2900	3364	G	25.394075	84.16173	Speed Breaker
26/ 6/ 25	16:36:25	86	0.1	300	31.2	3000	3462	G	25.394775	84.162288	Normal
26/ 6/ 25	16:36:25	86	0.1	280	32.5	2800	3265	G	25.39563	84.16249	Normal
26/ 6/ 25	16:37:0	86	0.1	270	30.5	2700	3167	G	25.396558	84.16244	Normal
26/ 6/ 25	16:37:0	86	0.1	290	30.3	2900	3364	G	25.39747	84.162423	Normal
26/ 6/ 25	16:37:0	86	0.1	270	31.2	2700	3167	G	25.398307	84.162642	Normal
26/ 6/ 25	16:37:35	86	0.1	300	32.5	3000	3462	G	25.399112	84.162945	Normal
26/ 6/ 25	16:37:35	86	0.1	220	31.2	2200	2675	G	25.400052	84.162978	Normal
26/ 6/ 25	16:38:0	86	0.1	290	32.5	2900	3364	G	25.400968	84.163232	Normal
CUMULATIVE							64915				
AVERAGE IRI							3246				

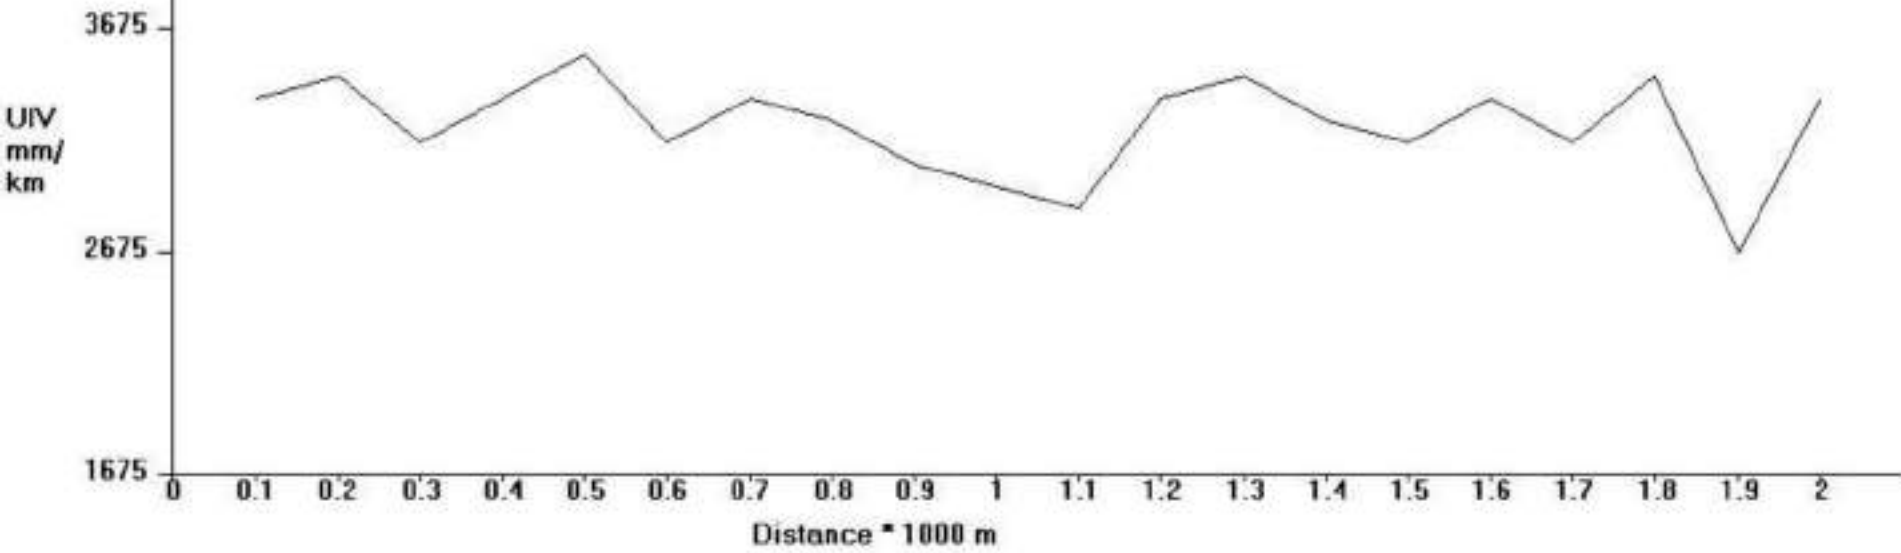
M/na-016
9/10/25

9/10/25

9/10/25

File : C:\Users\Del\Downloads\25021006.Xls, Section No. : 86, Eqn : $Y = 0 \cdot X^2 + 1.047 \cdot X - 63.36$

Name of Customer : M/S DEVTA PROJECT BUILDERS, Name of Work/ Road : ANSARI NAHAR ROAD TO DUSHADH



M/mao/b
9/10/25

9/10/25

9/10/25
