

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल, डुमरांव ।

Email ID – ee.dumraon.rwd@gmail.com

पत्रांक 1500/17/10

दिनांक 13/10/25

प्रेषक,

ई0 संजय कुमार
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, डुमरांव ।

सेवा में,

नोडल पदाधिकारी,
मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (MMGSUY (RRSMP GEN)
ग्रामीण कार्य विभाग, बिहार, पटना ।

विषय:— शीर्ष MMGSUY (RRSMP GEN) में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष MMGSUY (RRSMP GEN) योजना अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक का भुगतान किया जा सके।

अनु०:—

1. अधियाचना प्रमाण पत्र 1 पृष्ठ में।
2. उपयोगिता प्रमाण पत्र एक प्रति ।

विश्वासभाजन




कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्यप्रमंडल, डुमरांव ।

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

- (1) Certified that out of the Loan of Rs.2833.01505, Sanctioned under MMGSUY(RRSMP GEN), Vide Letter No.62 dated.27.07.2025, in favour of **Executive Engineer, Rural Works Department, Works Division, Dumraon**, during the year **2025-26**, an amount of Rs.2833.01505, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.0.000, remaining unutilized at the end of the year..... has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.
- (2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.


13/10/25
Divisional Accounts Officer
Rural Works Department,
Works Division, Dumraon.


13/10/25
Executive Engineer
Rural Works Department
Works Division, Dumraon.

Regulation Format for Scheme - MMGSUY (RRSMP General/SCST)


Name of the Works Division :- **Dumraon**

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work status (WMM/ WMA/ BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bottom Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/25-26 Dumraon/01	1040200350184	Raghunathpur Station Road to Silariya Green	4.670	43.149680	260.43212	17 CMBD 2025-26	03.10.2026	ongoing	WMM/SDBC	-	-	-	0.00000	0.00000	48.220	60.220	WMM/SDBC in progress
2	RRSMP/25-26 Dumraon/01	1040200350185	Draga Mandir to Dharali Road	1.400	77.13700	48.10311	17 CMBD 2025-26	03.10.2026	ongoing	WMM/BM/SDBC	-	-	-	0.00000	0.00000	23.600	25.600	WMM/SDBC in progress
3	RRSMP/25-26 Dumraon/01	1040200350186	Bhadrav PMGSY to Block Boundry	3.450	105.25100	185.30760	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	59.440	90.440	WMM in progress
4	RRSMP/25-26 Dumraon/01	1040200350187	Sakulpura Road to Chaugai Phudidar Road	1.200	70.90800	40.15842	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	28.107	28.107	WMM in progress
5	RRSMP/25-26 Dumraon/01	1040200350188	Atarasi path to Phafidar via sakulpura path/pura path	2.000	119.21400	65.76657	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	40.23	40.23	WMM in progress
6	RRSMP/25-26 Dumraon/01	1040200350189	Badagpur Bagan Path to Akoni Green	3.000	180.25000	99.54085	17 CMBD 2025-26	03.10.2026	ongoing	WMM	-	-	-	0.00000	0.00000	57.715	57.715	WMM in progress
7	RRSMP/25-26 Dumraon/01	1040200350190	Dharali Hilt to Dhuruli Green Tak Path. (Reserve person unemployed Engineer)	1.050	81.55300	47.64130	17 CMBD 2025-26	03.10.2026	ongoing	WMM/BM	-	-	-	0.00000	0.00000	23.056	23.056	WMM/BM in progress
8	RRSMP/24-25 Dumraon/02	1040200350118	East Shopar Men Road to Ex. Samad Late Seng Prasad	0.950	67.28662	48.74690	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	-	-	-	0.00000	0.00000	37.940	37.940	Pat Patch Completed, PCC in progress
9	RRSMP/24-25 Dumraon/02	1040200350119	L429-Chaugai to Baidi (L029)	0.780	47.72452	30.60742	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	2564	25	5.01	13.36434	13.56434	13.06400	1.500	Physically Completed
10	RRSMP/24-25 Dumraon/02	1040200350120	Repair of road from Karamsany Main road to Fakhar (Baidi village)	1.500	87.92543	58.30997	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	2819	25	5.01	35.12712	35.12712	37.22700	2.100	Physically Completed
11	RRSMP/24-25 Dumraon/02	1040200350121	Atyong Chaugai PMGSY Road to Thon Pandeypur dahi busi gate tak	0.700	48.99925	33.80210	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3406	25	5.01	3.26315	3.26315	31.26300	28.000	PCC 400m Completed
12	RRSMP/24-25 Dumraon/02	1040200350122	Karamsany Chaugai Path Se Rampur Nohar Tak Banjarwa Kuchi Busi Tak	2.200	139.84836	91.60380	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3163	25	5.01	56.27225	56.27225	58.37200	2.100	Physically Completed
13	RRSMP/24-25 Dumraon/02	1040200350123	Chaugai Bagan path se Chaugai Mashar tole tak sadak nirman	1.000	64.00400	41.28570	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3275	25	5.01	26.49879	26.49879	27.69800	1.200	Physically Completed
14	RRSMP/24-25 Dumraon/02	1040200350124	Mandhya Nachp PMGSY Road Se Vapur Harijan Tola Tak	2.500	162.90830	104.32790	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	2724	25	5.01	63.33230	63.33230	68.56200	5.280	Physically completed
15	RRSMP/24-25 Dumraon/02	1040200350125	AMSARI NAHAR ROAD SE to DUSADH TOLA KAMKAR TOLA	1.950	122.54129	79.90886	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3246	25	5.01	20.12075	20.12075	56.12100	36.000	Pat Patch Completed & BT 1050m Completed, PCC in progress
16	RRSMP/24-25 Dumraon/02	1040200350126	PHAFIDAR APPROACH PATH SE to KORI TOLA MASARIYA	2.100	127.99630	82.12206	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3190	25	5.01	47.85808	47.85808	50.25800	2.300	Physically Completed
17	RRSMP/24-25 Dumraon/02	1040200350127	Chaugai Keshari road se Banatpur Shriy Mandir tole	1.800	116.04227	72.74437	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3290	25	5.01	35.18106	35.18106	36.48100	1.300	Physically Completed
18	RRSMP/24-25 Dumraon/02	1040200350128	Chaugai Parab gate to Harizon tole	1.250	80.98115	54.96039	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	2637	25	5.01	16.16676	16.16676	46.16700	30.000	PCC in progress
19	RRSMP/24-25 Dumraon/02	1040200350129	Koran Sani Fakhar Path To Kori Tola	0.400	22.22036	14.53638	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3167	25	5.01	10.90060	10.90060	22.85100	11.550	Physically completed
20	RRSMP/24-25 Dumraon/02	1040200350130	Main Post Office To Choodbory Tola	0.450	28.11512	19.26401	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3010	25	5.01	0.00000	0.00000	18.000	16.000	Pat Patch Completed, PCC in progress
21	RRSMP/24-25 Dumraon/02	1040200350131	Quamrari Chauran Path to Pawan Tola	0.260	17.09777	11.20285	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	2877	25	5.01	0.00000	0.00000	9.380	9.280	Pat in progress
22	RRSMP/24-25 Dumraon/02	1040200350132	Marga pul Bithari path se Nachap	1.600	176.98478	127.00800	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3608	25	5.01	71.85696	71.85696	73.05700	2.000	Surface Completed
23	RRSMP/24-25 Dumraon/02	1040200350133	Marga pul se Bithari	1.200	138.54881	105.29527	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	3380	25	5.01	72.31663	72.31663	74.31700	2.000	Surface Completed
24	RRSMP/24-25 Dumraon/02	1040200350134	Bispar to Chhori Doh Nachap	1.300	83.18060	54.93108	01 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	-	-	-	11.74398	11.74398	33.74000	22.000	BT 450m Completed, PCC in progress

25	RRSMP-24-25 Damraon-04	1040200350100	Repair of road from Bhatpur to Nainjar	14.000	2463.74906	1824.66967	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	317.31166	317.31166	317.31166	200.00000	BM/SDBC in progress
26	RRSMP-24-25 Damraon-04	1040200350094	NH-04 To Kisinga Tola	0.500	33.328	23.16197	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	0.00000	0.00000	20.00000	20.00000	BM/SDBC in progress
27	RRSMP-24-25 Damraon-04	1040200350004	GARATHA KHURD - YOGA	2.400	182.93333	95.04834	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	8.51804	8.51804	84.51804	76.00000	BM/SDBC in progress
28	RRSMP-24-25 Damraon-04	1040200350093	NH-04 Maharaigunj to Karonan Gana	1.95	155.41734	110.31931	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	6.38803	6.38803	86.38803	80.00000	BM/SDBC in progress
29	RRSMP-24-25 Damraon-04	1040200350095	NH-04 To Karonan Tola	0.950	53.79172	34.41250	05 CMBD 2025-26	22/05/2026	ongoing	BM/SDBC	-	-	-	0.00000	0.00000	23.00000	23.00000	BM/SDBC in progress
30	RRSMP-24-25 Damraon-05	1040200350072	Alodhi (Piprah) to Titar gaura tal path extension	2.630	256.78911	156.56191	08 CMBD 2025-26	04/06/2026	ongoing	BM/SDBC	-	-	-	13.30439	13.10459	118.65400	105.550	SDBC in progress
31	RRSMP-24-25 Damraon-05	1040200350073	BAGEN DEVILAH PATH BHADWAR MAHADEV STHAN SE to BABUHA GRAM CHANDRMA VADAV TOLA	3.900	197.62531	134.78158	08 CMBD 2025-26	04/06/2026	ongoing	BM/SDBC	-	-	-	6.13119	6.13119	73.72100	67.590	SDBC in progress
32	RRSMP-24-25 Damraon-05	1040200350079	Bhatpur Bagen Path to Dhanadi Via Kaithe Road	8.400	730.76600	594.02491	08 CMBD 2025-26	04/06/2026	ongoing	SDBC	-	-	-	46.41600	46.41600	197.78900	351.383	GWB in progress
33	RRSMP-24-25 Damraon-05	1040200350002	BRAHMPUR PEAKINAD SE to BRAHMPUR PASCHEM TOLA MAHADEV STHAN	1.500	84.56050	52.88710	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	3.34215	3.34215	27.98100	24.635	WBM Completed,SDBC in progress
34	RRSMP-24-25 Damraon-05	1040200350087	Kaithe road to Murchi tola	1.250	102.09700	70.59653	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	0.00000	0.00000	43.100	43.100	SDBC in progress
35	RRSMP-24-25 Damraon-05	1040200350090	MAIHIYA NABAR PULL SE to NIYALPUR DERA KAITHE EYM BHAGELU DERA HOTE HUE KAITHE GAUN	1.500	97.83177	66.42109	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	0.00000	0.00000	59.500	59.500	SDBC in progress
36	RRSMP-24-25 Damraon-05	1040200350091	NH10 to Piprah Village	1.350	81.78780	53.22160	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	4.08400	4.08400	40.50100	36.317	SDBC Completed,PCC in progress
37	RRSMP-24-25 Damraon-05	1040200350097	Piprah Bhatpur bagen road to Piprah Via Rajpur	2.300	243.97811	136.74258	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	16.39314	16.39314	123.66700	107.214	SDBC in progress
38	RRSMP-24-25 Damraon-05	1040200350098	Bhagatpur Bagen Path to Kaithe to Nachup Gana Tola	1.550	97.10921	61.32194	08 CMBD 2025-26	04/06/2026	ongoing	WBM/BM	-	-	-	9.15116	9.15116	31.15100	22.000	SDBC in progress
39	RRSMP-24-25 Damraon-03	1040200350060	Kowah Bhata Pool - Arhar Mahave Arhar Path via Jairampur, Rampur	3.950	468.24000	375.87101	09 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	-	-	-	62.29811	62.29811	232.29800	140.000	SDBC in progress
40	RRSMP-24-25 Damraon-03	1040200350063	Kowah Bantand to Soveraha NH-30 Mar	7.90000	844.76261	640.36087	09 CMBD 2025-26	04/05/2026	ongoing	BM/SDBC	-	-	-	76.72748	76.72748	318.72700	240.000	SDBC in progress
41	RRSMP-24-25 Damraon-03	1040200350066	KESATH BATHULI PATH MORIAN SINGH KE DERA to NONIYA BABA BATHULI	3.400	212.27907	131.77441	09 CMBD 2025-26	04/03/2026	ongoing	BM/SDBC	-	-	-	15.35083	15.35093	63.35100	48.000	SDBC in progress
42	RRSMP-24-25 Damraon-01	1040200350114	NH04 Naman To Bhariyar Road	3.800	549.96200	398.71231	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	96.47227	96.47227	216.47227	120.00000	SDBC in progress
43	RRSMP-24-25 Damraon-01	1040200350107	Ank Bus Stand To Ank Smith Tola	0.765	53.88800	35.51522	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	3.64047	3.64047	19.64047	16.000	SDBC in progress
44	RRSMP-24-25 Damraon-01	1040200350116	NH 04 Krishnabahan To Ank PMGSY Road Via Kaithe Road	4.300	337.90500	377.45163	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	108.75146	108.75146	248.75100	140.000	SDBC in progress
45	RRSMP-24-25 Damraon-01	1040200350117	Bhatpur Nainjar Mukhya Path to Bandh To Jwahi Tawan Dem	6.950	689.54900	482.18670	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	48.16902	48.16902	302.16900	254.000	SDBC in progress
46	RRSMP-24-25 Damraon-01	1040200350110	Chakki Bagen Road Via Floor ME To PWD Road	0.950	111.18100	60.48129	04 CMBD 2025-26	11/06/2026	ongoing	BM/SDBC	-	-	-	17.76699	17.76699	89.76700	32.000	SDBC in progress
47	RRSMP-24-25 Damraon-08	1040200350137	Damraon Vikarungaj Road To Vandeve Sach Tola	0.500	39.14191	27.17143	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	0.77361	0.77361	20.77361	20.0000	SDBC in progress
48	RRSMP-24-25 Damraon-08	1040200350139	Repair of road from Nawangan Block to Kakar Bhakka	3.320	251.42906	136.86871	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	10.04185	10.04185	100.0419	90.0000	SDBC in progress
49	RRSMP-24-25 Damraon-08	1040200350141	Girdhar Barwan - Sam Nahan Pool	2.625	180.70965	19.96755	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	7.88752	7.88752	92.88752	85.0000	SDBC in progress
50	RRSMP-24-25 Damraon-08	1040200350152	BASUDEWA KESHATH ROAD - GOBINDPUR	0.910	70.25351	54.55622	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	2.63581	2.63581	27.63581	25.0000	SDBC in progress
51	RRSMP-24-25 Damraon-08	1040200350153	Repair of road from Nawangan Thakurhan P.W.D. road to Bhatali via Ratnagar	1.800	122.40885	81.73557	02 CMBD 2025-26	07/05/2026	ongoing	BM/SDBC	-	-	-	8.62867	8.62867	28.62867	20.0000	SDBC in progress

52	RRSMP-24-25 Damron-08	1040200350161	N.H-30 Vaina Sadik Se Wali Tak	1.850	64.19438	44.09958	02 CMBD 2025-26	07/05/2026	origin g	BM/SDBC	-	-	-	0.89783	0.89783	35.89783	25,0000	SDBC in progress
53	RRSMP-24-25 Damron-08	1040200350164	Titarhat Link Road Se Pakhiyo Mahavir Shiva Pooner Tola Tak	0.900	64.61417	44.26161	02 CMBD 2025-26	07/05/2026	origin g	BM/SDBC	-	-	-	2.39800	2.39800	37.398	25,0000	SDBC in progress
54	RRSMP-24-25 Damron-08	1040200350170	Kancha N.H-30 se Shiv tola tak	0.800	54.54991	36.75455	02 CMBD 2025-26	07/05/2026	origin g	BM/SDBC	-	-	-	2.50589	2.50589	32.50589	30,0000	SDBC in progress
55	RRSMP-24-25 Damron-08	1040200350171	Budhat PMSY Shiv Gopal Pandey ka Guchki to Tutaha Village	1.230	83.02806	54.49621	02 CMBD 2025-26	07/05/2026	origin g	BM/SDBC	-	-	-	8.66183	8.66183	53.66183	45,0000	SDBC in progress
56	RRSMP-24-25 Damron-08	1040200350183	NH120 to Kouspur	1.850	62.40526	41.54917	02 CMBD 2025-26	07/05/2026	origin g	BM/SDBC	-	-	-	1.77030	1.77030	39.7703	28,0000	SDBC in progress
57	RRSMP-24-25 Damron-09	1040200350136	Damron Vikramgarh Road To Ahar Vindola	0.300	21.48366	15.27827	03 CMBD 2025-26	07/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	10.0000	10,0000	WBM/BM in progress
58	RRSMP-24-25 Damron-09	1040200350147	NAWANAGAR SIKRARAUL ROAD - ATIANI	0.950	110.91022	82.93316	03 CMBD 2025-26	07/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	50.0000	50,0000	WBM/BM in progress
59	RRSMP-24-25 Damron-09	1040200350159	Sakraal Banar path se Akotara gaon tak sadak niman	1.200	73.88024	48.83414	03 CMBD 2025-26	07/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	24.0000	24,0000	WBM/BM in progress
60	RRSMP-24-25 Damron-09	1040200350174	Kancha PMSY to Vikramgarh	1.120	81.83507	49.34265	03 CMBD 2025-26	07/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	25.0000	25,0000	WBM/BM in progress
61	RRSMP-24-25 Damron-09	1040200350178	Ahar-Bhawa road to kanchi	0.900	52.93026	22.99440	03 CMBD 2025-26	07/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	17.0000	17,0000	WBM/BM in progress
62	RRSMP-24-25 Damron-06	1040200350010	Kopra to Kariya	2.030	130.87908	84.32672	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	50.0000	50,0000	WBM/BM in progress
63	RRSMP-24-25 Damron-06	1040200350013	L846-NH-84 NAWADERA (L846)	1.700	114.37140	76.28813	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	3.00916	3.00916	40.0094	25,0000	WBM/BM in progress
64	RRSMP-24-25 Damron-06	1040200350017	L850-Damron Koton Sami to Samandha (L850)	1.000	67.35873	40.89041	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	4.11196	4.11196	24.1120	20,0000	WBM/BM in progress
65	RRSMP-24-25 Damron-06	1040200350018	Ayazpur Brahmadaha to Bagin Path	9.800	881.98853	635.37200	07 CMBD 2025-26	04/05/2026	origin g	WBM/BM	-	-	-	86.27483	86.27483	256.2748	200,0000	WBM/BM in progress
66	RRSMP-24-25 Damron-06	1040200350019	NH-84 Bhakich to Anandpur Hota har Karamal Paluk	13.500	1578.96503	1171.70898	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	11.76649	11.76649	211.7665	200,0000	WBM/BM in progress
67	RRSMP-24-25 Damron-06	1040200350021	Bahari to Sewa	6.420	571.52117	412.32106	07 CMBD 2025-26	04/05/2026	origin g	WBM/BM	-	-	-	30.15430	30.15430	188.8543	150,0000	WBM/BM in progress
68	RRSMP-24-25 Damron-06	1040200350024	Repair of Road from Mathila to Kariya	1.950	251.46809	144.89671	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	128.0000	120,0000	WBM/BM in progress
69	RRSMP-24-25 Damron-06	1040200350025	Kidharbaha to Garidharbaha	19.200	1711.62506	1277.42469	07 CMBD 2025-26	04/05/2026	origin g	WBM/BM	-	-	-	111.09811	111.09811	361.0981	250,0000	WBM/BM in progress
70	RRSMP-24-25 Damron-06	1040200350026	Repair of Road from S.H-79 Damron Barampur to Magan	2.000	133.70764	87.85225	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	6.55182	6.55182	50.5518	44,0000	WBM/BM in progress
71	RRSMP-24-25 Damron-06	1040200350029	Magan Nakar Pal to Damron Via Fagi Tola Nahara Road	6.450	829.12407	578.33374	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	248.0000	240,0000	WBM/BM in progress
72	RRSMP-24-25 Damron-06	1040200350046	Kotmora Reika Path to Najiganj	2.000	132.39980	86.86249	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	4.95899	4.95899	59.7290	54,7800	WBM/BM in progress
73	RRSMP-24-25 Damron-06	1040200350052	KUSHALPUR RAILWAY GUMTI MUKHYA PATH to BARNALIA	1.450	94.69105	63.34440	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	35.8000	35,0000	WBM/BM in progress
74	RRSMP-24-25 Damron-06	1040200350053	BUKAR AKA N.H-84 to RAILWAY GUMTI KOTE HUE KUSHALPUR	2.010	193.69941	121.85115	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	5.14819	5.14819	65.1482	60,0000	WBM/BM in progress
75	RRSMP-24-25 Damron-06	1040200350054	NH 84 Bihal Bagat Shivalya se Banauli via Biharpurva	1.800	194.54608	138.07972	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	80.0000	80,0000	WBM/BM in progress
76	RRSMP-24-25 Damron-06	1040200350056	Sarka Pal se Kharochia	4.000	372.29948	239.86224	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	158.0000	150,0000	WBM/BM in progress
77	RRSMP-24-25 Damron-06	1040200350058	Aharwa to Oatigana	1.900	198.63753	135.04641	07 CMBD 2025-26	22/05/2026	origin g	WBM/BM	-	-	-	0.00000	0.00000	58.0000	58,0000	WBM/BM in progress

It is certified that Physical & Financial Progress has been updated in MIS.


Senior S.D.O. J.S.
RWD, Works Division, Damron


Senior S.D.O. J.S.
RWD, Works Division, Damron

1. Above Signed Copy along with Forwarding Letter & Utilization Certificate must be uploaded in MIS.
2. Signed Hard Copy and Soft Copy (in excel) of forwarded IRI is enclosed (As Applicable).

अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि RRSMP (GEN) योजनान्तर्गत

1. पथ/ पुल PHAFDAR APPROACH PATH SE to KOIRI TOLA MASARIYA में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।

mp. ucc 014
21/10/25

कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा, चौगाई

21/10/25

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, चौगाई

09/10/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, डुमराँव।

Name of Road :- PHAFDAR APPROACH PATH TO KOIRI TOLA MASARIYA . (MACHINE - BUXAR)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	GATEGORY Road	Latitude	Longitude	Event
20/ 6/ 25	13: 19: 41	40	0.1	230	0	2300	2773	G	25.433072	84.267322	Normal
20/ 6/ 25	13: 20: 0	40	0.1	250	30.3	2500	2970	G	25.432188	84.267255	Normal
20/ 6/ 25	13: 20: 0	40	0.1	260	31.2	2600	3069	G	25.431235	84.267053	Curve
20/ 6/ 25	13: 20: 0	40	0.1	250	32.5	2500	2970	G	25.43089	84.267827	Normal
20/ 6/ 25	13: 21: 0	40	0.1	320	31.2	3200	3659	G	25.42997	84.267558	Normal
20/ 6/ 25	13: 21: 28	40	0.1	280	32.5	2800	3265	G	25.42929	84.267153	Speed Breaker
20/ 6/ 25	13: 21: 28	40	0.1	320	31.2	3200	3659	G	25.428422	84.266918	Speed Breaker
20/ 6/ 25	13: 22: 2	40	0.1	330	32.5	3300	3757	G	25.42758	84.266918	Normal
20/ 6/ 25	13: 22: 2	40	0.1	320	30.3	3200	3659	G	25.42673	84.27	Normal
20/ 6/ 25	13: 22: 2	40	0.1	260	30.3	2600	3069	G	25.425828	84.266548	Normal
20/ 6/ 25	13: 22: 38	40	0.1	300	31.2	3000	3462	G	25.42491	84.266328	Normal
20/ 6/ 25	13: 23: 0	40	0.1	260	32.5	2600	3069	G	25.424035	84.266245	Normal
20/ 6/ 25	13: 23: 13	40	0.1	200	31.2	2000	2478	G	25.423775	84.265487	Normal
20/ 6/ 25	13: 23: 13	40	0.1	330	32.5	3300	3757	G	25.424007	84.264512	Normal
20/ 6/ 25	13: 24: 0	40	0.1	310	31.2	3100	3561	G	25.424107	84.26347	Normal
20/ 6/ 25	13: 24: 24	40	0.1	290	32.5	2900	3364	G	25.424708	84.262827	Normal
20/ 6/ 25	13: 25: 0	40	0.1	270	31.2	2700	3167	G	25.425257	84.26207	Curve
20/ 6/ 25	13: 25: 34	40	0.1	240	32.5	2400	2872	G	25.426078	84.261885	Curve
20/ 6/ 25	13: 26: 0	40	0.1	220	31.2	2200	2675	G	25.4264	84.260975	Curve
20/ 6/ 25	13: 26: 9	40	0.1	230	32.5	2300	2773	G	25.425703	84.26042	Normal
20/ 6/ 25	13: 26: 9	40	0.1	250	30.3	2500	2970	G	25.425158	84.25973	Normal
CUMULATIVE							66998				
AVERAGE IRI							3190				

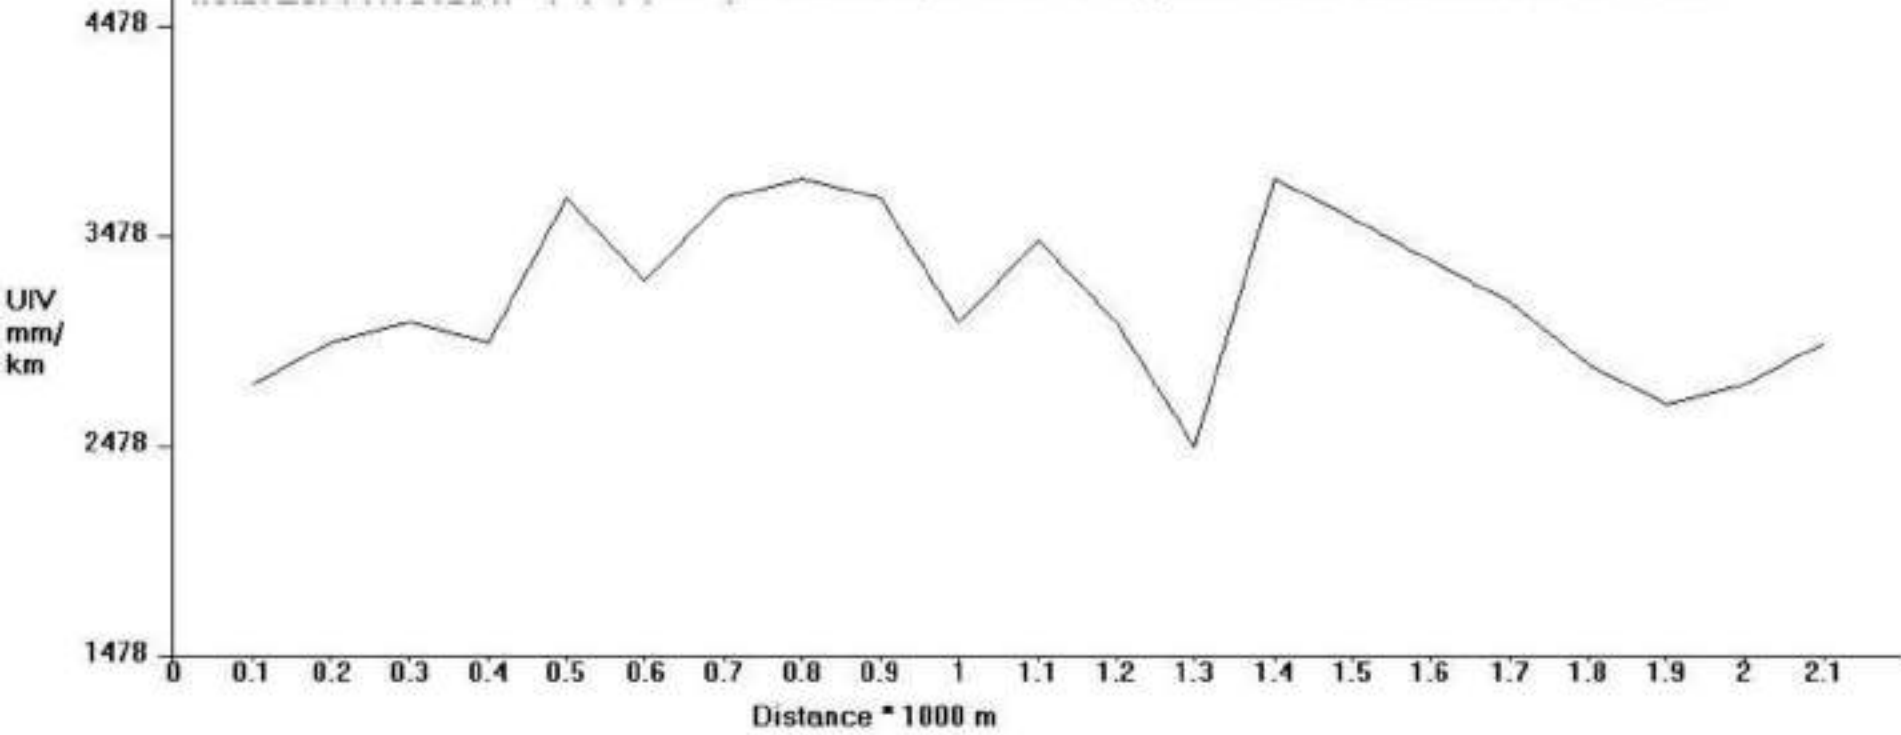
M/ma-016
9/10/25

9/10/25

9/10/25

File : C:\Users\Del\Downloads\250210061.xls, Section No. : 40, Eqn : $Y = 0 \cdot X^2 + 1.047 \cdot X - 63.36$

Name of Customer : M/S DEVTA PROJECT BUILDERS, Name of Work/ Road : PHAFDAR APPROACH PATH TO



M. M. C. 16
9/10/25

9/10/25

9/10/25
