

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

पत्रांक :- 1950(अ७०)

/कटिहार, दिनांक- 02/09/25

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

नोडल पदाधिकारी,
3054 एम.आर. कोषांग,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- MMGSUY(SC) (मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना) के क्रियान्वित पथों के भुगतान हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि ग्रा०का०वि०, कार्य प्रमंडल, कटिहार अन्तर्गत MMGSUY(SC) (मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना) के पथ में पूर्ण कराये गये कार्यों के भुगतान हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु०:-यथोक्त।

विश्वासभाजन,


21/9/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।


21/9/25

ज्ञापांक:- 1950

/कटिहार, दिनांक:- 02/09/25

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।


21/9/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।


21/9/25

GFR 12-B

[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(3) Certified that out of the Loan of Rs. 127300000.00, Sanctioned under MMGSUY(SC), dated 23.03.2025, in favour of EE, RWD, Katihar, during the year 2024-25, an amount of Rs.98419732.00, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.28880268.00, remaining unutilized at the end of the year 2024-25 has been surrendered to the Government (vide No....., dated.....) will be adjusted towards the loan payable during the next financial year.

(4) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Works have been supervised by Executive Engineer/Superintending Engineer.
2. Periodical inspection has been conducted by E.E./S.E.
3. Construction materials have been tested.
4. Measurements have been recorded in the MBs and test check conducted by the Assistant.
5. All other codal formalities have been observed.


Divisional Accounts Officer Gr-I
RWD, Works Division, Katihar


Executive Engineer,
RWD (W) Division, Katihar.


Assistant Engineer,
RWD (W) Division, Katihar.

RWD, Works Division, Katihar

MMGSUY(SC) Allotment Requisition Format


Name of Division : Katihar


Sl No	Package no	Project ID as per MIS	Name of Road	Administrative Approval (AA)		Agreement Construction Work Amount (in Lac)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work status (WBM/ WMM/MB)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Alloted Amount (In Lac)	Upto date expenditure as per MIS (In Lac)	Value of Work Done (In lac)	Current Demand (In lac)	Remarks	
				Length (In Km)	Construction Work Amount (in Lac)														
1	MMGSUY/23-24 KATIHAR/05	4110550300002	L022-L035 MAHAMADIA TO DHERUA (TRACK22)	3.940	301.59900	243.37394	09MBD/24-25, 15.09.2024	14.09.2025	01.07.2025	Completed	2893.33	75mm	5.00%	223.00000	221.02876	242.46610	19.46610		
2		4110550300003	Bharidih To Pipra Tola	1.995	140.95800	114.82278	09MBD/24-25, 15.09.2024	14.09.2025	01.07.2025	Completed	3205.21	75mm	5.01%	101.00000	96.00000	108.90505	7.90505		
3		4110550300001	Hasanganj RCD road Thana chowk se jagarnath pur tola tak	1.700	183.01500	150.70854	09MBD/24-25, 15.09.2024	14.09.2025	17.07.2025	Completed	2724.76	75mm	5.01%	90.00000	60.00000	130.08895	40.08895		
			Total												414.00000	377.02876	481.46010	67.46010	

It is certified that physical and financial progress has been updated in MIS

NOTE:-

- 1 Above signed copy along with forwarding letter and Utilization Certificate must be uploaded in MIS
- 2 Signer Hard copy and soft copy (in excel sheet) of recorded IRI is enclosed (As Applicable)


02.09.25
Divisional Accounts Officer Gr-I
RWD, Works Division, Katihar


21/9/25
Executive Engineer
RWD, Works Division, Katihar

Name of Road-Hasanganj RCD road Thana chowk se jagarnath pur tola tak Length

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/ 8/ 25	11: 46: 0	34	0.1	200	0	2000	2404	G	25.652281	87.580489	Normal
24/ 8/ 25	11: 46: 0	34	0.1	210	20.2	2100	2518	G	25.652128	87.581443	Culvert
24/ 8/ 25	11: 46: 27	34	0.1	270	20.2	2700	3199	G	25.652096	87.582456	Normal
24/ 8/ 25	11: 46: 27	34	0.1	230	30.3	2300	2745	G	25.652487	87.583054	Normal
24/ 8/ 25	11: 46: 27	34	0.1	200	30.3	2000	2404	G	25.652634	87.584085	Normal
24/ 8/ 25	11: 47: 3	34	0.1	210	30.3	2100	2518	G	25.652732	87.58537	Normal
24/ 8/ 25	11: 47: 3	34	0.1	310	30.3	3100	3654	G	25.652502	87.586368	Normal
24/ 8/ 25	11: 47: 3	34	0.1	280	30.3	2800	3313	G	25.652246	87.587137	Normal
24/ 8/ 25	11: 47: 3	34	0.1	280	30.3	2800	2177	G	25.653319	87.587161	Normal
24/ 8/ 25	11: 47: 38	34	0.1	180	30.3	1800	2177	G	25.654363	87.587376	Normal
24/ 8/ 25	11: 47: 38	34	0.1	270	30.3	2700	3199	G	25.654363	87.587376	Normal
24/ 8/ 25	11: 47: 38	34	0.1	270	30.3	2700	3199	G	25.655325	87.587425	Normal
24/ 8/ 25	11: 48: 0	34	0.1	190	30.3	1900	2290	G	25.656684	87.587969	Normal
24/ 8/ 25	11: 48: 13	34	0.1	210	30.3	2100	2518	G	25.656684	87.587969	Normal
24/ 8/ 25	11: 48: 13	34	0.1	190	30.3	1900	2290	G	25.656482	87.588148	Normal
24/ 8/ 25	11: 48: 13	34	0.1	190	30.3	1900	2290	G	25.657364	87.588463	Normal
24/ 8/ 25	11: 48: 13	34	0.1	240	30.3	2400	2858	G	25.658149	87.588231	Curve
24/ 8/ 25	11: 48: 48	34	0.1	270	30.3	2700	3199	G	25.658149	87.588231	Normal
24/ 8/ 25	11: 48: 48	34	0.1	270	30.3	2700	3199	G	25.658865	87.588319	Normal
24/ 8/ 25	11: 49: 0	34	0.1	180	30.3	1800	2177	G	25.658865	87.588319	Normal
24/ 8/ 25	11: 49: 0	34	0.1	240	30.3	2400	2858	G	25.658735	87.589425	Normal
24/ 8/ 25	11: 49: 0	34	0.1	240	30.3	2400	2858	G	25.658735	87.589425	Normal
			1.7								

Bilal
02/09/25
O.E

Bilal
02/09/25
A.E

Bilal
02/09/25
Executive Engineer
R.W.D. (W) Division
Katihar

Name of Customer : MS BALAJI CONSTRUCTION
 Name of Work/ Road : Hasanganj RCD road Thana ch
 Lab Job number :
 Date : 24-08-2025
 Section No. : 34

Test Date : 24-08-2025 Road Name : se jagamath pur tola tak Length
 Machine No : 404 Road Type : (R) RURAL ROAD
 Start S No : 34 Side : Interval
 Start E No :
 Weather :
 UV Range : 1177 To 5000 1000 mm/km
 Dist Range : 0 To 1.8 0.1 * 1000 m
 Start Location :
 End Location :
 Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

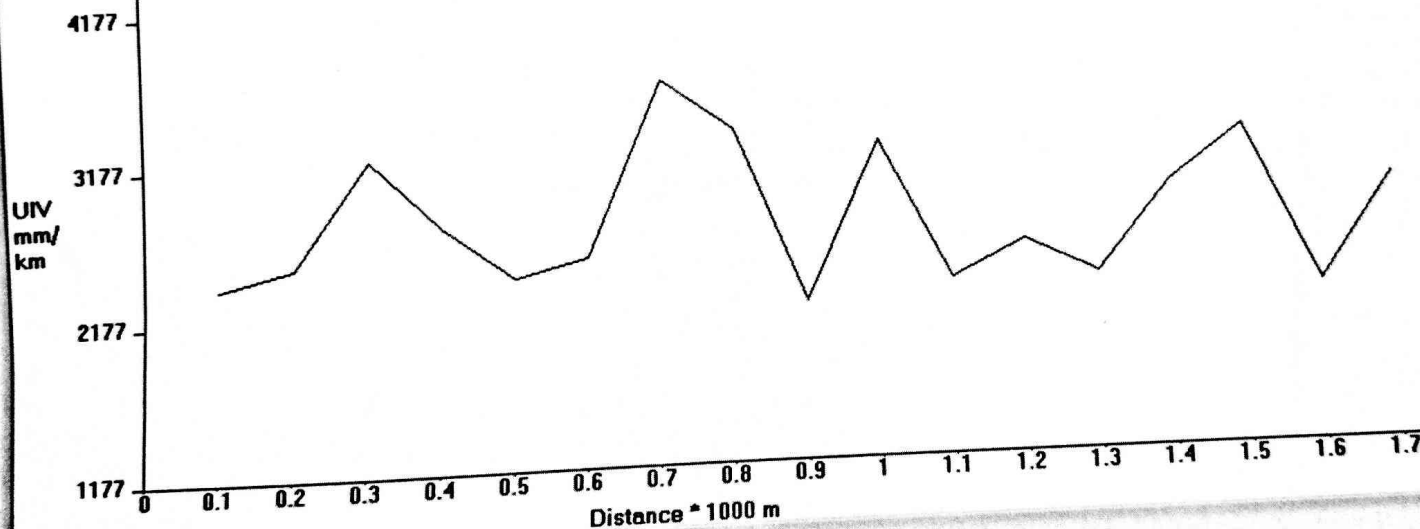
Print

Generate Report and Graph

Redraw Graph

Map View

File : E:\RAM KUMAR\MISC Files\Bump integrator\MMGSUY\Hasanganj RCD road Thana chowk se jagamath pur
 Name of Customer : MS BALAJI CONSTRUCTION. Name of Work/ Road : Hasanganj RCD road Thana chowk se



By 02/09/25
 S.E.

By 02/09/25
 A.E.

Executive Engineer
 R.W.D. (W) Division
 Katihar

अधियाचना हेतु प्रमाण पत्र

प्रमाणित किया जाता है कि MMGSUY(Sc) योजनान्तर्गत:-

1. पथ / पुल Hasanganj RCD road Thana chowk se jagarnath pur tola tak में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक / विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


कनीय अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रशाखा, हसनगंज


सहायक अभियंता
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, हसनगंज


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल कटिहार।

M/S BALAJI CONSTRUCTION

09MBD/2024-25- MMH50Y (SC)

Schedule XLV-Form No. 134

HASANGANJ RCD ROAD THANA CHOUK
SE JAGARNATH PUR. TOLA TAK.

R. W. D. KATHAR - DIVISION

HASANGANJ - SUB-DIVISION

(NO-2441)

MEASUREMENT BOOK

3rd on 74/c Bill

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Abstract of cost.</u>					
1. Providing and fixing of working benchmark pillars	01 Nos.				
alt. vide T. M. B.					
Page (8) = 2 Nos.					
Rs 4452.39 / No.					Rs 8905.00
2. Providing and fixing of working reference pillars	04 Nos.				
alt. vide T. M. B.					
Page (8) = 6 Nos.					
Rs 2072.82 / No.					Rs 12,437.00
3. Clearing and grubbing Road land					
alt. vide T. M. B.					
Page (8) = 0.68 Ha					
Rs 76926.08 / Ha					Rs 52,310.00
4. Box cutting excavation					

Continuation

Continuation

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Qty. vide T.M.B.					
Pay (21) =					77.764 ²
at 137.55/m ²					10,696.00
					Rs. 1,33,32,993.00
Add Labour (C.P.) 1%					Rs. 1,33,330.00
Add seigniorage Fee					Rs. 1,39,116.00
					Rs. 1,36,05,439.00
Add G.S.T. 18%					Rs. 24,48,979.00
					Rs. 1,60,54,418.00
Less 18.97% Below					Rs. 30,45,523.00
					Rs. 1,30,08,895.00

Total Rs. 70,08,895.00

Bilal

28/07/25

J.E

28/07/25

28/07/25

A.E
