

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, जहानाबाद।**

पत्रांक: 1367 / जहानाबाद ,
प्रेषक,

दिनांक: 14/9/20

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

सेवा में,


अधीक्षण अभियंता
ग्रामीण कार्य विभाग
कार्य अंचल, औरंगाबाद।

विषय :- प्रधानमंत्री ग्राम सड़क योजना अन्तर्गत एल150- टेहटा बाईपास रोड से पुरना बिगहा निर्माण कार्य की समयवृद्धि के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि प्रधानमंत्री ग्राम सड़क योजना अन्तर्गत एल150- टेहटा बाईपास रोड से पुरना बिगहा (पैकेज संख्या- बीआर-14आर-377) पथ निर्माण का कार्य पूर्ण कर लिया गया है, जिसका एकरारनामा संख्या-23एसबीडी/18-19 है एवं कार्य समाप्ति की निर्धारित तिथि 11.01.2020 है। पुनरीक्षित एकरारनामा एवं जमीन विवाद हो जाने के कारण संवेदक द्वारा समय पर कार्य पूर्ण नहीं कराया गया जिसके कारण दिनांक 31.08.2020 तक समयवृद्धि हेतु विहित प्रपत्र में भरकर अनुशंसा के साथ समर्पित की जाती है। आवंटन की अधियचना से संबंधित प्रतिवेदन संलग्न कर समर्पित किया जा रहा है।
अनु0 - यथोक्त।

विश्वासभाजन


14.9.2020

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

AK
14/9/20

APPLICATION FOR EXTENSION OF TIME :-

1. Name Of Contractor: Sai Ventures
2. Name Of Work:- Construction of road from L150 Telita
(Head Of Expenditure) Bypass to Purnabigha.
3. Agreement Number:- 23(SBD)/2018-19
4. Agreement Value:-
5. Date Of Commencement Of Work:- 12/01/2019
6. Date Of Completion Stipulated In The Agreement:- 11/01/2020
7. Period For Which Extension Has Been Given Previously:- NO
8. Work Done In %:- 100%.
9. Period For Which Extension Now Applied For:- 31/08/2020
10. Reason For Extension Of Time:- Land Dispute, Revise Estimate, Covid-19
11. Recommendation By J.E.:- Time extension maybe granted Pratik Kr.
12. Whether Programme Of Work Approved:- JE
13. Whether Fund Available:- Yes
14. If Spill Over From Previous Financial Year Whether Included In The
Current Work Programme or not:-
15. Recommendation Of SDO:-

Recommended for Extension

File P.S. 7/9/20

16. Recommendation Of Executive Eng:- अग्रिम



7/9/20
10-9-2020
Executive Engineer
R. W. D. (W) Division
Jehanabad

17. Recommendation Of S.E.



Kanti K.
 2020
 JE

P. S. / 2020
 AB

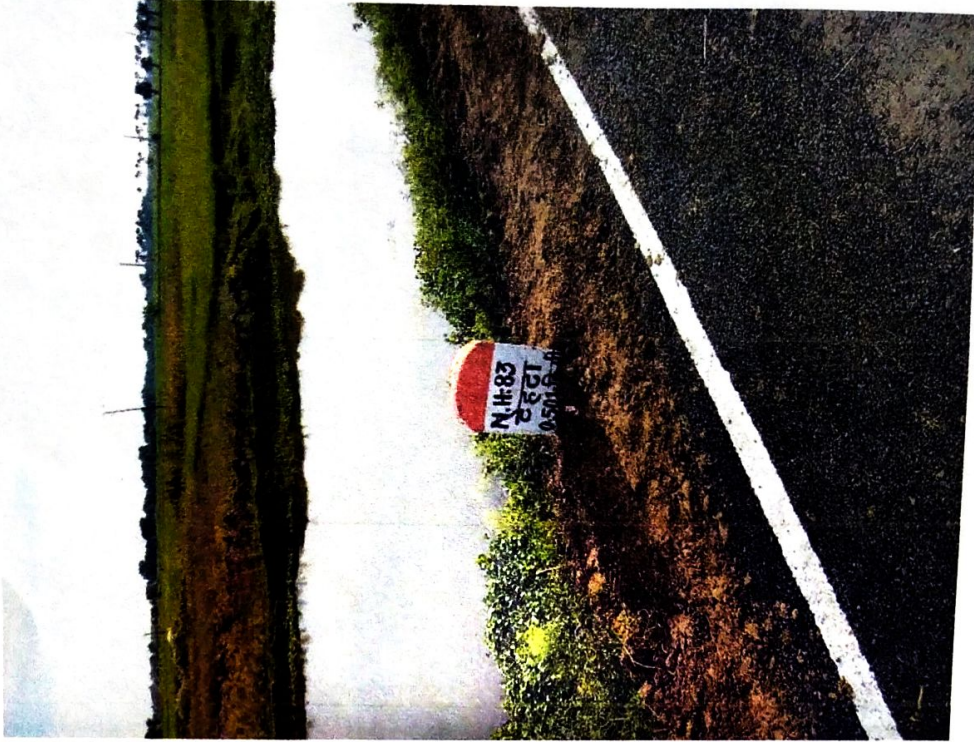

Permit R5.
JE

Permit R5
7/19/70
JB



Hamid K.
JE

Proh
7/11/20
JTB



Pan 4 Ko.
TE

Resh
7/9/20
AE
