

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, जहानाबाद।**

पत्रांक: 1366 / जहानाबाद ,
प्रेषक,

दिनांक: 14/9/20

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

सेवा में,

अधीक्षण अभियंता
ग्रामीण कार्य विभाग
कार्य अंचल, औरंगाबाद।

विषय :- प्रधानमंत्री ग्राम सड़क योजना अन्तर्गत एल150- पाई बिगहा धनकी रोड से नरहनपर निर्माण कार्य की समयवृद्धि के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि प्रधानमंत्री ग्राम सड़क योजना अन्तर्गत एल150- पाई बिगहा धनकी रोड से नरहनपर (पैकेज संख्या- बीआर-14आर-380) पथ निर्माण का कार्य पूर्ण कर लिया गया है, जिसका एकरारनामा संख्या-16एसबीडी/18-19 है एवं कार्य समाप्ति की निर्धारित तिथि 17.12.2019 है। पुनरीक्षित एकरारनामा एवं जमीन विवाद हो जाने के कारण संवेदक द्वारा समय पर कार्य पूर्ण नहीं कराया गया जिसके कारण दिनांक 18.08.2020 तक समयवृद्धि हेतु विहित प्रपत्र में भरकर अनुशंसा के साथ समर्पित की जाती है। आवंटन की अधियचना से संबंधित प्रतिवेदन संलग्न कर समर्पित किया जा रहा है।

अनु0 - यथोक्त।

विश्वासभाजन



14.9.2020

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जहानाबाद।

14/9/20


APPLICATION FOR EXTENSION OF TIME :-

1. Name Of Contractor: Sai Ventures
2. Name Of Work:- Construction of road from Paibigha
(Head Of Expenditure) Dhanki Road to Natchoupar.
3. Agreement Number:- 16 SBD/2018-19
4. Agreement Value:-
5. Date Of Commencement Of Work:- 18/12/2018
6. Date Of Completion Stipulated In The Agreement:- 17/12/2019
7. Period For Which Extension Has Been Given Previously:- No
8. Work Done In %:- 100%
9. Period For Which Extension Now Applied For:- 18/08/2020
10. Reason For Extension Of Time:- Land Dispute, Revise Estimate, Covid-19
11. Recommendation By J.E.:- Time extension may be granted Land Ko
12. Whether Programme Of Work Approved:- Je
13. Whether Fund Available:- Yes
14. If Spill Over From Previous Financial Year Whether Included In The
Current Work Programme or not:-
15. Recommendation Of SDO:- Recommended for Extension of Time
Revised 7/9/20
AE
16. Recommendation Of Executive Eng:- अक्षय 7/9/20
10.9.2020
Executive Engineer
R. W. D. (W) Division
Jehanabad
17. Recommendation Of S.E.

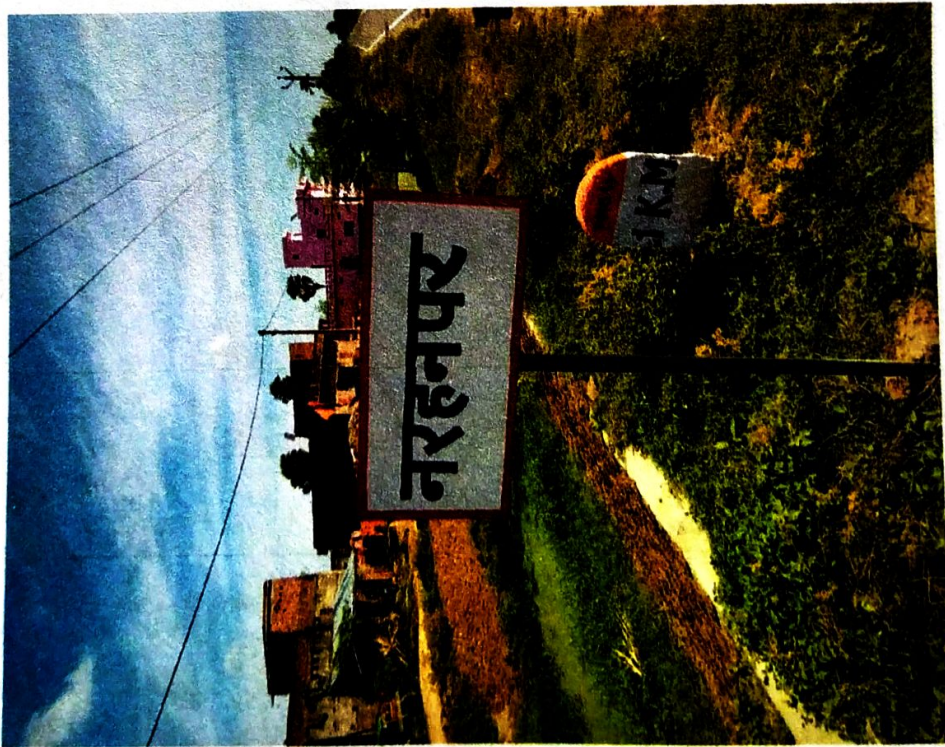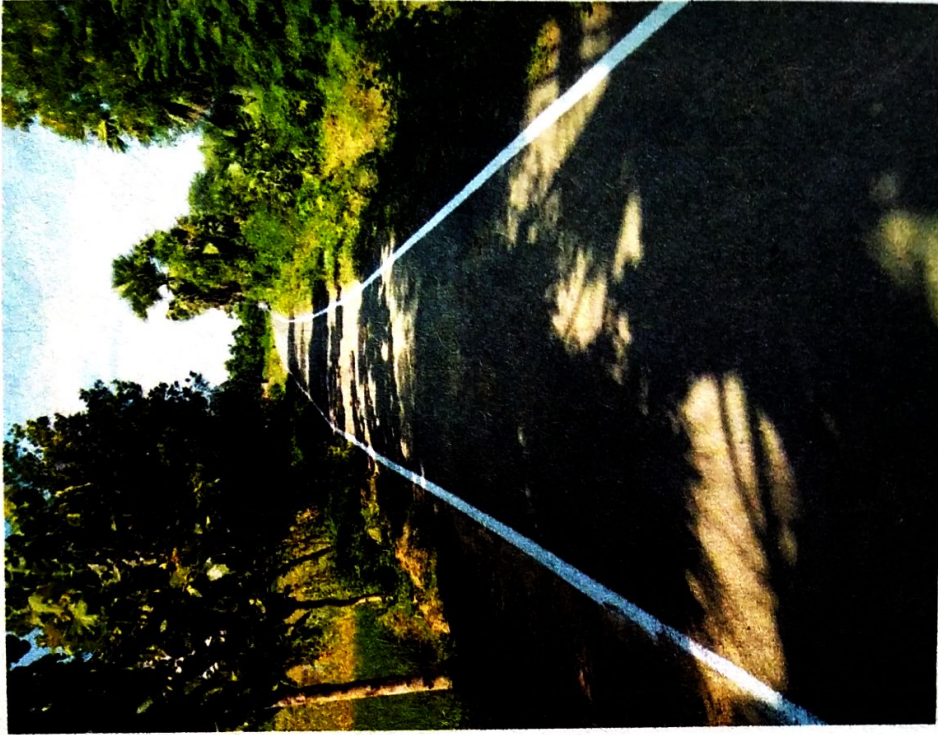


Pranil R.
JE

Pranil R.
7/9/20
JE

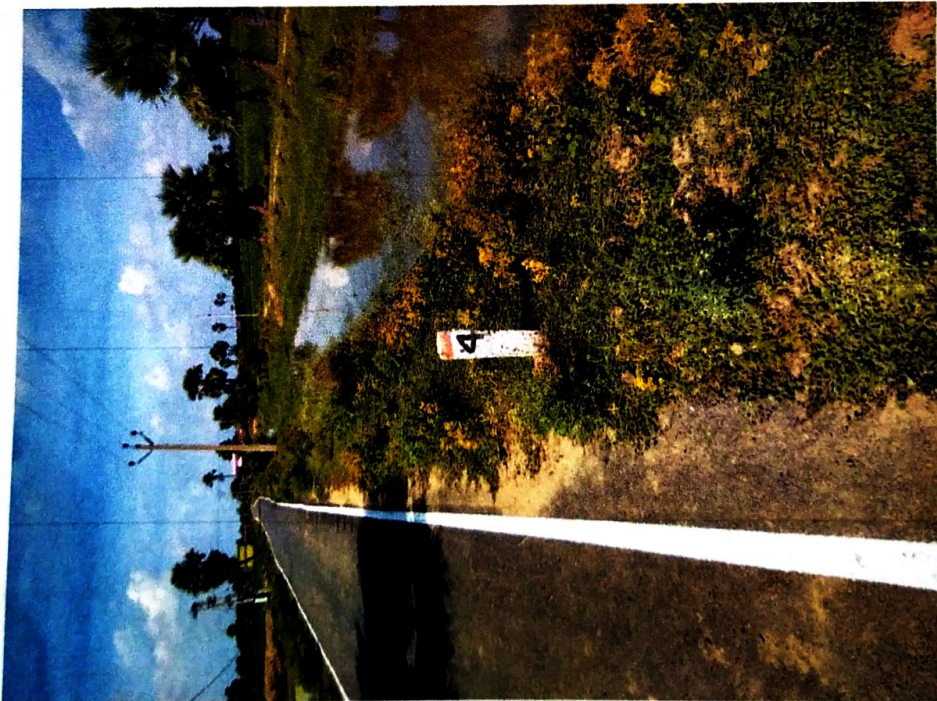

Pramit K.
JE

Redi
7/9/20
AE

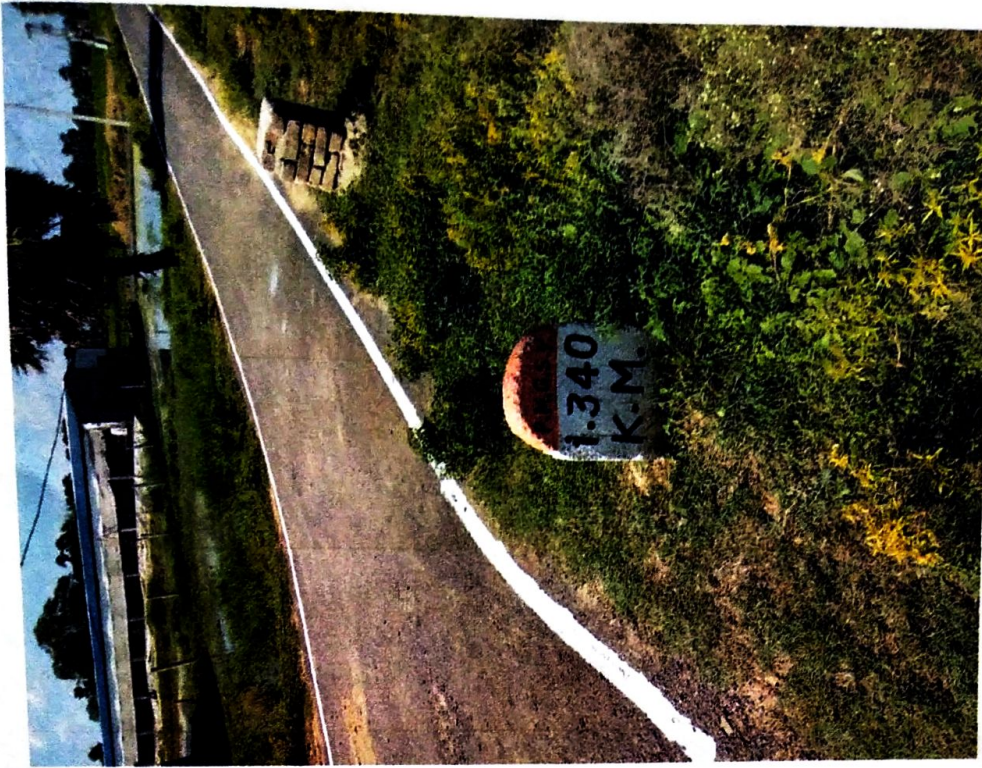

Paint K.M.

JE

Ref. in
7/9/20
AB

