

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, महनार (वैशाली)

पत्रांक
प्रेषक ,

१०८

/महनार/दिनांक :- १८/११/२०२०

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, महनार

नोडल पदाधिकारी, MR (3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- **MR (3054)** नई अनुरक्षण निति-2018 के तहत निर्माणाधीन/निर्मित पथ की राशि की अधियाचना पत्र समर्पित करने के संबंध में।


महाशय,

उपरोक्त विषय के संदर्भ में **MR (3054)** नई अनुरक्षण निति-2018 निर्माणाधीन/निर्मित पथ के लिए राशि की अधियाचना विहित प्रपत्र में समर्पित की जा रही है।

विदित है कि अधियाचित पथ का कार्य संतोषप्रद है। अधियाचित पथ में आवंटन देने की कृपा की जाये।

अनु०:-1. अधियाचना विहित प्रपत्र।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, महनार


Katharia Braham asthan - Andhwara

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event
12/11/20	14:14:13	No.	0.1	240	0	2400	2360	ROAD	3.25	25.664825	85.31867	Normal
12/11/20	14:14:13	99	0.1	220	20.2	2200	2162	G	3	25.665752	85.319107	Normal
12/11/20	14:18:0	99	0.1	240	0	2400	2360	G	3.25	25.66366	85.317928	Normal
12/11/20	14:18:20	99	0.1	220	10.1	2200	2162	G	3	25.663935	85.31682	Normal
12/11/20	14:19:0	99	0.1	180	10.1	1800	1766	G	2.51	25.662882	85.316363	Normal
12/11/20	14:19:0	99	0.1	230	10.1	2300	2261	G	3.13	25.661947	85.31601	Normal
12/11/20	14:19:30	99	0.1	160	20.2	1600	1568	G	2.26	25.661007	85.31569	Normal
12/11/20	14:19:30	99	0.1	200	20.2	2000	1964	G	2.76	25.659898	85.315318	Normal
12/11/20	14:20:6	99	0.1	250	20.2	2500	2458	G	3.37	25.658872	85.314982	Curve
12/11/20	14:20:6	99	0.1	200	10.1	2000	1964	G	2.76	25.658297	85.31579	Normal
12/11/20	14:21:0	99	0.1	170	10.1	1700	1667	G	2.38	25.657247	85.31547	Normal
12/11/20	14:21:16	99	0.1	190	20.2	1900	1865	G	2.63	25.65661	85.316312	Normal
12/11/20	14:21:16	99	0.1	230	20.2	2300	2261	G	3.13	25.656015	85.31682	Normal
12/11/20	14:21:51	99	0.1	180	20.2	1800	1766	G	2.51	25.65512	85.31638	Normal
12/11/20	14:22:0	99	0.1	190	20.2	1900	1865	G	2.63	25.654095	85.315858	Normal
12/11/20	14:23:2	99	0.1	190	0	1900	1865	G	2.63	25.65297	85.315318	Normal
12/11/20	14:23:2	99	0.1	120	10.1	1200	1173	G	1.74	25.652048	85.314747	Normal
12/11/20	14:24:0	99	0.1	190	10.1	1900	1865	G	2.63	25.65105	85.31409	Normal
12/11/20	14:24:12	99	0.1	180	10.1	1800	1766	G	2.51	25.649913	85.313502	Normal
12/11/20	14:24:48	99	0.1	150	10.1	1500	1469	G	2.13	25.6489	85.313047	Normal
12/11/20	14:25:0	99	0.1	170	20.2	1700	1667	G	2.38	25.647947	85.312473	Normal
12/11/20	14:25:23	99	0.1	170	20.2	1700	1667	G	2.38	25.646805	85.31202	Normal
12/11/20	14:42:0	99	0.1	160	0	1600	1568	G	2.26	25.64719	85.312103	Normal
12/11/20	14:42:26	99	0.1	150	20.2	1500	1469	G	2.13	25.648107	85.312542	Normal
12/11/20	14:42:26	99	0.1	180	20.2	1800	1766	G	2.51	25.649062	85.313113	Normal
12/11/20	14:43:1	99	0.1	200	10.1	2000	1964	G	2.76	25.650292	85.313618	Normal
12/11/20	14:43:37	99	0.1	150	10.1	1500	1469	G	2.13	25.65118	85.314157	Normal
12/11/20	14:44:0	99	0.1	180	10.1	1800	1766	G	2.51	25.65208	85.314763	Normal

$$Y = 0 * X^2 + 0.989 * X - 13.58$$

$$X = 1400$$

$$Y = 1371$$

(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

Handwritten signature

1854.3929


Bidupur to Majhauri NH-103

12/11/20	15:3:18	38	0.1	220	0	2200	2162 G	3	25.652007	85.32512	Normal
12/11/20	15:4:0	38	0.1	200	0	2000	1964 G	2.76	25.653192	85.325522	Normal
12/11/20	15:4:27	38	0.1	300	10.1	3000	2953 G	3.97	25.65422	85.325942	Normal
12/11/20	15:5:2	38	0.1	190	10.1	1900	1865 G	2.63	25.654968	85.32542	Normal
12/11/20	15:5:38	38	0.1	250	10.1	2500	2458 G	3.37	25.655207	85.324157	Normal
12/11/20	15:6:0	38	0.1	150	20.2	1500	1469 G	2.13	25.65605	85.324175	Normal
12/11/20	15:6:13	38	0.1	150	20.2	1500	1469 G	2.13	25.657192	85.32468	Culvert
12/11/20	15:6:48	38	0.1	150	20.2	1500	1469 G	2.13	25.658182	85.32513	Normal
12/11/20	15:7:0	38	0.1	120	20.2	1200	1173 G	1.74	25.659215	85.325757	Normal
12/11/20	15:7:23	38	0.1	180	20.2	1800	1766 G	2.51	25.66027	85.326363	Normal
12/11/20	15:7:23	38	0.1	160	10.1	1600	1568 G	2.26	25.661432	85.325622	Normal
12/11/20	15:7:23	38	0.1	120	20.2	1200	1173 G	1.74	25.662715	85.324865	Normal
12/11/20	15:8:34	38	0.1	210	0	2100	2063 G	2.88	25.664062	85.32512	Normal
12/11/20	15:8:34	38	0.1	190	10.1	1900	1865 G	2.63	25.665135	85.325588	Normal
12/11/20	15:9:9	38	0.1	120	10.1	1200	1173 G	1.74	25.666235	85.325975	Normal
12/11/20	15:9:45	38	0.1	160	10.1	1600	1568 G	2.26	25.66747	85.32616	Normal
12/11/20	15:10:0	38	0.1	230	10.1	2300	2261 G	3.13	25.66865	85.326363	Normal
12/11/20	15:10:20	38	0.1	190	10.1	1900	1865 G	2.63	25.66962	85.3268	Culvert
12/11/20	15:12:6	38	0.1	260	0	2600	2557 G	3.49	25.670992	85.327222	Normal
12/11/20	15:12:41	38	0.1	270	0	2700	2656 G	3.61	25.67207	85.32776	Speed Breaker
12/11/20	15:13:16	38	0.1	210	10.1	2100	2063 G	2.88	25.673005	85.328163	Normal
12/11/20	15:13:16	38	0.1	220	20.2	2200	2162 G	3	25.673955	85.328618	Normal
12/11/20	15:14:0	38	0.1	210	10.1	2100	2063 G	2.88	25.675215	85.32941	Normal
12/11/20	15:14:27	38	0.1	160	10.1	1600	1568 G	2.26	25.676492	85.329443	Normal
12/11/20	15:15:2	38	0.1	240	0	2400	2360 G	3.25	25.677673	85.329545	Normal
12/11/20	15:16:0	38	0.1	280	0	2800	2755 G	3.73	25.679077	85.330353	Speed Breaker
12/11/20	15:16:13	38	0.1	250	10.1	2500	2458 G	3.37	25.680102	85.330823	Normal
12/11/20	15:17:0	38	0.1	270	10.1	2700	2656 G	3.61	25.681088	85.331397	Normal
12/11/20	15:19:9	38	0.1	260	0	2600	2557 G	3.49	25.682265	85.331127	Normal
12/11/20	15:19:44	38	0.1	160	10.1	1600	1568 G	2.26	25.682405	85.33007	Normal
12/11/20	15:20:0	38	0.1	150	10.1	1500	1469 G	2.13	25.682588	85.328955	Normal
12/11/20	15:20:20	38	0.1	200	20.2	2000	1964 G	2.76	25.682777	85.327827	Normal
12/11/20	15:20:20	38	0.1	150	20.2	1500	1469 G	2.13	25.683025	85.32668	Normal
12/11/20	15:20:55	38	0.1	180	20.2	1800	1766 G	2.51	25.68327	85.325655	Normal
12/11/20	15:21:0	38	0.1	160	10.1	1600	1568 G	2.26	25.68337	85.32446	Normal
12/11/20	15:21:30	38	0.1	140	20.2	1400	1371 G	2	25.683423	85.323298	Normal
12/11/20	15:21:30	38	0.1	110	10.1	1100	1074 G	1.61	25.683482	85.322222	Normal
12/11/20	15:22:0	38	0.1	140	20.2	1400	1371 G	2	25.68372	85.321077	Normal
12/11/20	15:22:5	38	0.1	140	20.2	1400	1371 G	2	25.684098	85.32002	Normal
12/11/20	15:22:5	38	0.1	140	20.2	1400	1371 G	2	25.684552	85.319023	Normal

[Signature]


File : D:\Bump Indicator Report\17.11.2020\12111527.Xls, Section No. : 99, Eqn : $Y = 0 * X^2 + 0.989 * X - 13.58$

Name of Customer : , Name of Work/ Road : , Lab Job number :

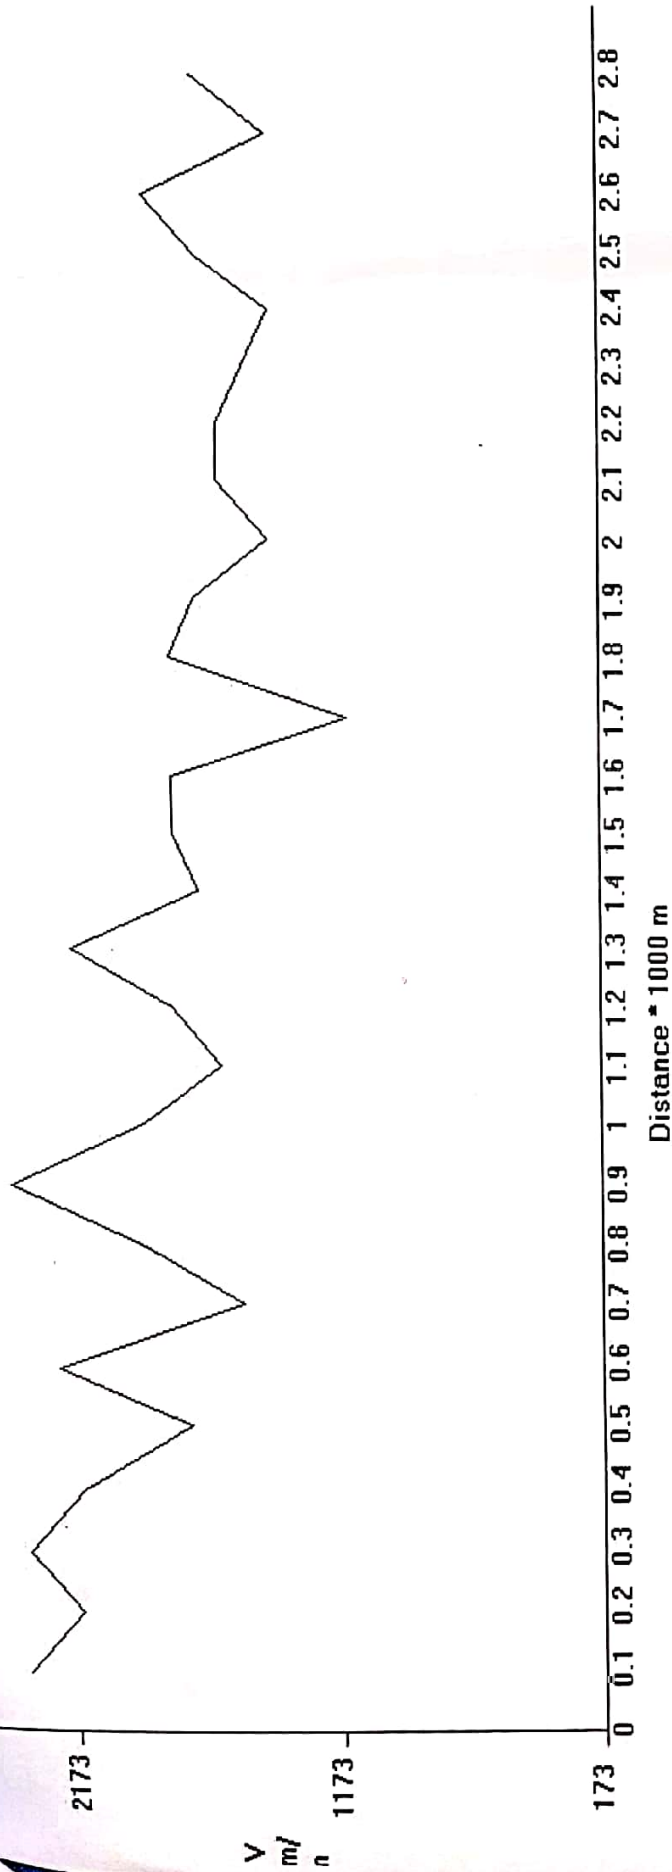

Handwritten signature

File : D:\Bump Indicator Report\17.11.2020\12111527.Xls, Section No. : 38, Eqn : $Y = 0 * X^2 + 0.989 * X - 13.58$
 Name of Customer : Name of Work/ Road : Lab Job number :

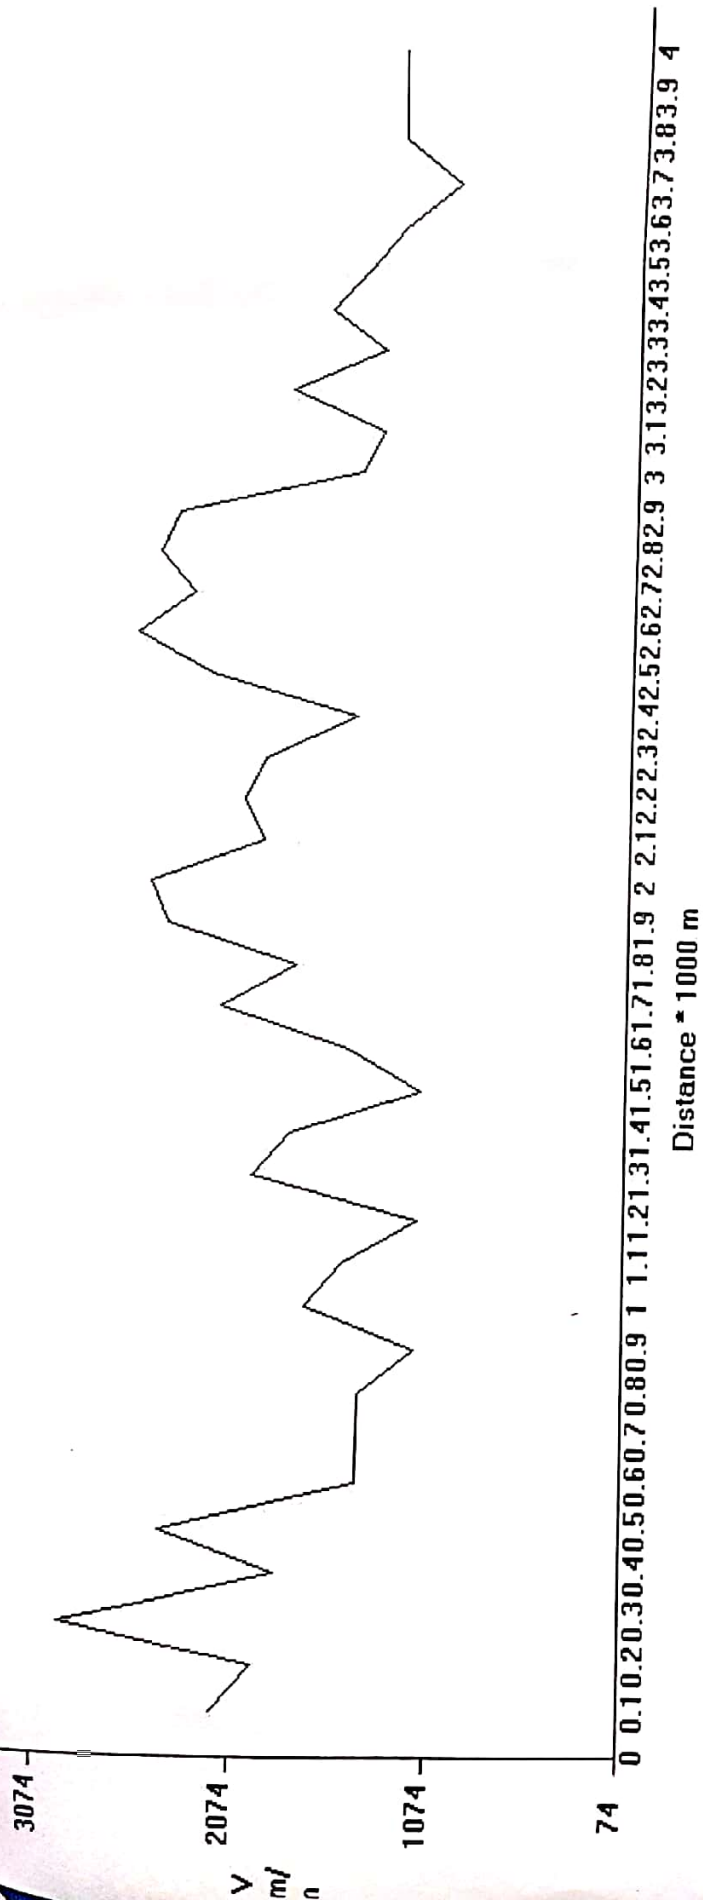

Handwritten signature

MIR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division: Mahanar

Sl No	Package No	Name of the Road (English)	Project ID as per AES	Adolescence Approval (AA) Letter Date	Administrative Approval (AA)		Agreement Amount (Rs Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Bidding (Rs Lakhs)	Thickness of Bituminous Layer (mm)	Value of Bituminous Content in percentage	Previous Total Aerial Survey (Rs Lakh)	Up to Date Expense (Rs per MTS)	Requestion against work done (Rs Lakh)	Remarks
					Length (in KM)	Amount of work (in Lakh)	Level Rectification and Surface Renewal (in Lakh)	Free Yearly Repair Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	ADP-2019-20 Mahanar-403	Highway to Majhuli Post-103	21507360012	Letter-2178 Dt-26.07.19	4.00	125.74286	72.12260	31.74880	01/04/HD/19-20 dt-26.03.2020	05.12.2020	-	1897.25	25 mm	5.05%	0.00	0.00	60.63382	
2	ADP-2019-20 Mahanar-403	Kantari Bhabari Kotari - Andhawa	MCA720000033	Letter-2178 Dt-26.07.19	3.00	87.20380	49.64336	22.81235	01/04/HD/19-20 dt-05.03.2020	05.12.2020	-	1854.39	25 mm	5.05%	0.00	0.00	41.38839	

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRJ is enclosed.
2 Up-to-date Physical Progress has been updated in MIS

RWD, Works Division, Mahanar

Executive Engineer
RWD, Works Division, Mahanar
