

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल ढाका

पत्रांक—1606 / दिनांक—19.10.2020

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल ढाका।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार पटना।
विश्वशरैया भवन पाचवां तल्ला, पटना।

विषय :- MR(3054) under Bihar Rural Road Maintenance Policy-2018 योजना हेतु आवंटन
अधियाचना पत्र के संबंध में।

महाशय,

उपर्युक्त विषय ग्रामीण कार्य विभाग, कार्य प्रमंडल ढाका के अधीन MR(3054)
under Bihar Rural Road Maintenance Policy-2018 में कराये गये कार्य के विरुद्ध भुगतान हेतु
आवंटन अधियाचना विहित-प्रपत्र में संलग्न कर समर्पित किया जाता है।

अनु0—यथोक्त।

Signed Hard Copy of recorded IRI is enclosed.

Up-to-date Physical Progress has been uploaded in MIS.

विश्वासभाजन


19/10/2020

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल ढाका।
19/10/20

Same of Works Division : Dhaka, East Champaran

Sl No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Administrative Approval (AA)				Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1		REO ROAD KATHMALIYA CHOWK TO KAPOOR PAKRI PATH ROAD	NEA22000193	Latter No.-1873 & Date-24.06.2019	3.600	150.29200	91.25289	32.44030	Agreement No-38 MBD/28.01.2020	27.10.2020	Work in Progress	2878.561	25	5.00	91.25000	75.71340		
2		Motihari Dhaka Road to Shitalpatti	31708602114	Latter No.-1873 & Date-24.06.2019	3.856	159.867	97.84091	39.57475	Agreement No-38 MBD/2019-20	27.10.2020	Work in Progress	3053.970	25	5.00	97.84090	81.67839		
3		Motihari Dhaka PWD Road to Partapur	31708602173	Latter No.-1873 & Date-24.06.2019	0.660	27.743	13.99197	6.29652	Agreement No-38 MBD 2019-20	27.10.2020	Work in Progress	2938.710	25	5.00	13.99196	0.00000		
4	MR-N/20-21 DHAKA/01	Chiraiya Purnahiya Road At Rampur to Chiraiya Purnahiya REO Road	31708602073	Latter No.-1873 & Date-24.06.2019	3.421	140.7796	83.77209	34.25691	Agreement No-26 MBD/2019-20	27.08.2020	Work in Progress	2405.700	25	5.00	83.77200	80.64446		

EXECUTIVE DIRECTOR
FRYD (W) DIVISION CHAIR

DAO, 1970-10

19/10	2020
-------	------

Scanned by CamScanner

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
 form of Utilisation Certificate Upto the Month of upto 19.10.2020

3054 New Maintenance Policy 2018

:- EE, RWD (W) DIVISION DHAKA

Sl. No.	NAME OF SCHEME	Sanction No. & Date with Amount (in Rs Lacs)	Amount Received (in Rs Lacs)	Particulars
1	Construction of Rural Roads Under 3054 New Maintenance Policy 2018	Allotment received vide Letter No-14 Date.-28-02-2020	31105937.00	Certified that out of Rs-93222420.00 lacs received during the year 2020-21 in favour of Ex. Engineer RWD (W) DIVISION DHAKA a sum of Rs-77376546.33 lacs has been utilized for the Purpose of 3054 to Level-1 PI Schemes as given in the margin for which it was sanctioned of Rs-15845874.33 remaining unutilized at the end of the period under
2		Allotment received vide Letter No-1199 Date.20.03.2020	9125000.00	
3		Allotment received vide Letter No-35 Date.-21.05.2020	8377200.00	
4		Allotment received vide Letter No-37 Date.-27.05.2020	14204687.00	
5		Allotment received vide Letter No-47 Date.-24.06.2020	1399196.00	
6		Allotment received vide Letter No-65 Date.-09.09.2020	18572400.00	
7		Allotment received vide Letter No-77 Date.-14.10.2020	10438000.00	
8				
9				
		Total	93222420.00	

Certified that I have satisfied my self that the condition on which the grants - in -aid was sanctioned have been duly fulfilled are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer .
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD Works.

D.A.O.

WORKS DIVISION DHAKA
 RURAL WORKS DEPARTMENT

19/10/2020

EXECUTIVE ENGINEER
 RWD (W) DIVISION DHAKA
 19/10/20

of
 mer :
 Name of Work/ Road :
 Lab Job number :
 Date :
 Section No. :


Test Date :
 Machine No :
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name :
 Road Type :
 Side :
 UV Range :
 Dist Range :
 Equation :
 Interval :
 mm/km :
 • 1000 m

Print

Generate Report and Graph

Redraw Graph

Map View

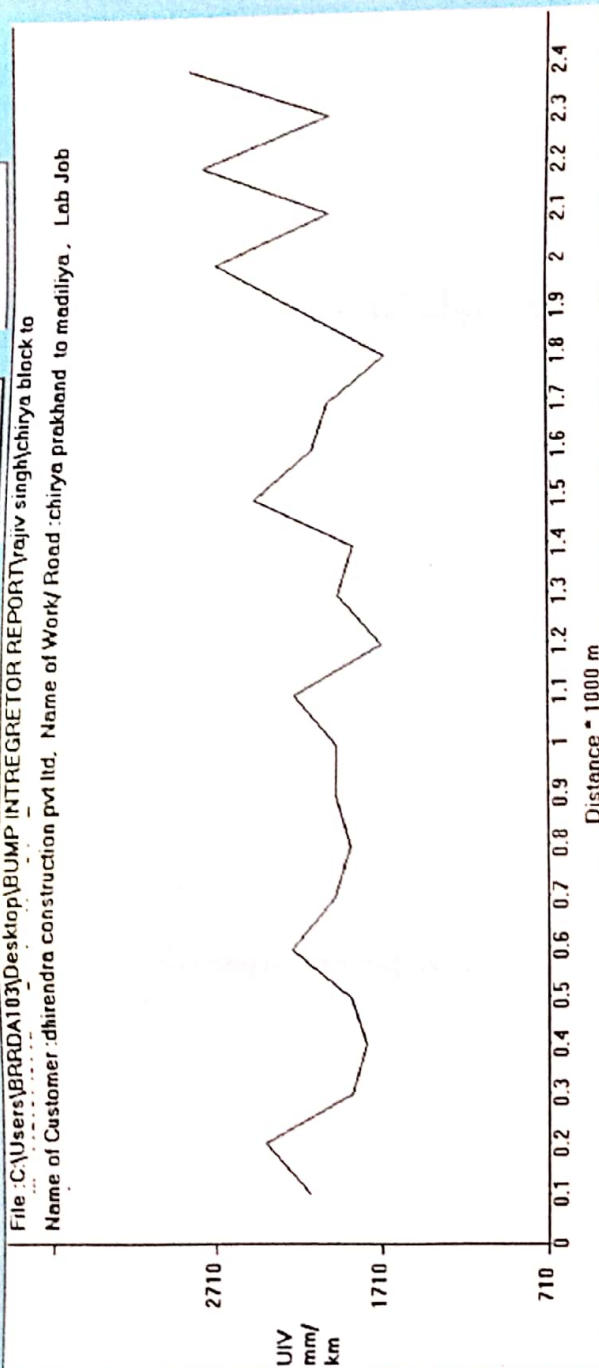

17/10/2020
 J.E

17/10/2020
 R.W.D. Chirya

17/10/2020
 Executive Engineer
 R W. D. Works Division
 Dhaka

e	Time	Section	Length	Bumps	Speed	OR	IRI	ATEGOR	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
17/10/20	13:53:0	24	0.1	220	0	2200	2144	G	26.70132	85.77222	Normal
17/10/20	13:53:4	24	0.1	250	20.2	2500	2405	G	26.70206	85.77777	Normal
17/10/20	13:53:4	24	0.1	190	30.3	1900	1883	G	26.7028	85.7843	Normal
17/10/20	13:53:39	24	0.1	180	20.2	1800	1797	G	26.70352	85.78972	Normal
17/10/20	13:54:0	24	0.1	190	30.3	1900	1883	G	26.7044	85.7936	Normal
17/10/20	13:54:0	24	0.1	230	30.3	2300	2231	G	26.70524	85.7973	Normal
17/10/20	13:54:14	24	0.1	200	30.3	2000	1970	G	26.70598	85.80218	Normal
17/10/20	13:54:14	24	0.1	190	30.3	1900	1883	G	26.70649	85.81143	Normal
17/10/20	13:54:14	24	0.1	200	30.3	2000	1970	G	26.70685	85.8202	Normal
17/10/20	13:54:49	24	0.1	230	30.3	2300	2231	G	26.70671	85.83013	Normal
17/10/20	13:55:0	24	0.1	170	30.3	1700	1710	G	26.70654	85.84007	Normal
17/10/20	13:55:0	24	0.1	200	30.3	2000	1970	G	26.70679	85.84965	Normal
17/10/20	13:55:24	24	0.1	190	30.3	1900	1883	G	26.70733	85.8579	Normal
17/10/20	13:55:24	24	0.1	260	30.3	2600	2492	G	26.70775	85.87	Normal
17/10/20	13:55:24	24	0.1	220	30.3	2200	2144	G	26.70794	85.87693	Normal
17/10/20	13:56:0	24	0.1	210	30.3	2100	2057	G	26.70822	85.8872	Normal
17/10/20	13:56:0	24	0.1	170	30.3	1700	1710	G	26.70861	85.89697	Normal
17/10/20	13:56:0	24	0.1	230	30.3	2300	2231	G	26.70891	85.90572	Normal
17/10/20	13:56:35	24	0.1	290	30.3	2900	2752	G	26.70921	85.91582	Normal
17/10/20	13:56:35	24	0.1	210	30.3	2100	2057	G	26.70952	85.9249	Normal
17/10/20	13:57:0	24	0.1	300	20.2	3000	2839	G	26.70985	85.9347	Normal
17/10/20	13:57:10	24	0.1	210	10.1	2100	2057	G	26.70981	85.95387	Normal
17/10/20	13:57:45	24	0.1	310	10.1	3100	2926	G	26.71006	85.96413	Normal
						TOTAL	51195				
						AVERAGE	2133.12				

$$Y = 0 * X^2 + 0.869 * X + 232.9$$

$$X = 2111$$

$$Y = 2067$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

17/10/2020
JE/Chiraiya

17/10/2020
JE/Chiraiya

17/10/2020
Executive Engineer
R. W. D. Works Division
Dhaka
