

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, मोतिहारी।

पत्रांक.....18528/20 / दिनांक 14.9.2020

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल मोतिहारी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव BRRDA,
बिहार, पटना।

विषय — MR-3054(New Maintenance Policy 2018) के अन्तर्गत पथ के
अनुरक्षण के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054(New Maintenance Policy 2018) के अन्तर्गत पथ के अनुरक्षण के निधि के लिए सूची बनाकर इस पत्र में संलग्न कर भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अनु०:— यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, मोतिहारी।

14/9/20

Office of The Executive Engineer, Rural Works Department, Works Division Motihari

Requisition formate for Scheme Head- MR-3054 Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification with Surface Renewal)

S.No	Package No	Name of Road	Project ID As per MIS	A.A Letter No & Date	Administrative Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of RRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-Date Expenditure as per MIS (in lakh)	Requisition amount work done (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	MR-N/19-20 Motihari/16	Dipau to Talwa	Project ID- 317821032387	5583 Dt. 23.10.2019	2.226	95.93450	66.65094	23.35377	36 MBD/2020-21 Dt. 30.06.2020	29.03.2021	08.09.2020	3260.26	25	5.00	0.00000	0.00000	66.60519	

Sr. Divisional Accounts Officer
Rural Works Department,
Works Division, Motihari

14/9/2020
Junior Engineer

14/9/2020
Asst. Engineer

14/9/2020
Executive Engineer,
Rural Works Department,
Works Division, Motihari

R.W.D Work Division Motihari

FORM GFR 19A

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 14.09.2020
MR HEAD-3054 (Initial Rectification with Surface Renewal)

Sl. No.	Name of Scheme	Selection No. of Date with Amount (in Rs. In Lacs)	Amount Received (in Rs. In Lacs)	Particulars
1	Construction of Rural Roads under MR HEAD-3054 (Initial Rectification with Surface Renewal)		880.41725	Certified that out of Rs.880.41725 Lacs received during the years 2020-21 in favour of Executive Engineer, R.W.D. Works Division, Motihari A sum of Rs.863.74723 Lacs has been utilised for the purpose of MR HEAD-3054 (Initial Rectification with Surface Renewal) Scheme as given in the margin or whichever sanctioned and that the balance Rs. 16.67012 Lacs remaining unutilised at the end of the period under.
			880.41725	


- 2 Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilised for the purpose for which it was sanctioned.


Kinds of exercised :-

- (i) Works have been supervised by Executive Engineer/ Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- (iii) Construction Material have been testes.
- (iv) Measurement have been recorded in the MBs and test check conducted by the Assistant.
- (v) All other codal formalities have been observed.

3 Physical Progress achieved : _

- (i) Construction of Road Works.
- (ii) Construction of CD Works.


Sr. Divisional Accounts Officer
Rural Works Department,
Works Division, Motihari


Executive Engineer,
Rural Works Department,
Works Division, Motihari

Name of Road- Dipau to Talwa, Constructor Name- Kshitij Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI in mm/km	CATEGORY ROAD	Latitude	Longitude	Event
12/9/20	14:9:11	50	0.1	320	0	3200	3303 G	26.508603	84.839578	Normal	
12/9/20	14:9:46	50	0.1	340	20.2	3400	3502 G	26.508335	84.840487	Normal	
12/9/20	14:10:0	50	0.1	330	20.2	3300	3402 G	26.508212	84.841515	Normal	
12/9/20	14:10:21	50	0.1	370	10.1	3700	3802 G	26.507828	84.842423	Normal	
12/9/20	14:10:21	50	0.1	360	20.2	3600	3702 G	26.507418	84.843282	Normal	
12/9/20	14:11:0	50	0.1	330	20.2	3300	3402 G	26.507102	84.844208	Normal	
12/9/20	14:11:0	50	0.1	320	20.2	3200	3303 G	26.506418	84.844427	Curve	
12/9/20	14:11:32	50	0.1	320	20.2	3200	3303 G	26.505868	84.845218	Normal	
12/9/20	14:11:32	50	0.1	340	20.2	3400	3502 G	26.50516	84.845757	Curve	
12/9/20	14:12:7	50	0.1	310	20.2	3100	3203 G	26.504525	84.846347	Curve	
12/9/20	14:12:7	50	0.1	350	20.2	3500	3602 G	26.503738	84.8468	Normal	
12/9/20	14:12:7	50	0.1	300	20.2	3000	3103 G	26.503132	84.847525	Normal	
12/9/20	14:12:42	50	0.1	270	20.2	2700	2804 G	26.50263	84.848	Normal	
12/9/20	14:13:0	50	0.1	300	20.2	3000	3103 G	26.502443	84.849242	Normal	
12/9/20	14:13:18	50	0.1	270	20.2	2700	2804 G	26.502395	84.850218	Normal	
12/9/20	14:13:18	50	0.1	340	20.2	3400	3502 G	26.502513	84.851228	Normal	
12/9/20	14:13:18	50	0.1	330	20.2	3300	3402 G	26.50306	84.851952	Normal	
12/9/20	14:13:53	50	0.1	310	20.2	3100	3203 G	26.503588	84.85271	Normal	
12/9/20	14:14:0	50	0.1	290	20.2	2900	3003 G	26.50416	84.85347	Curve	
12/9/20	14:14:28	50	0.1	370	20.2	3700	3802 G	26.5046	84.853602	Normal	
12/9/20	14:14:28	50	0.1	270	20.2	2700	2804 G	26.503903	84.854225	Normal	
12/9/20	14:15:0	50	0.1	300	20.2	3000	3103 G	26.503063	84.854562	Normal	
12/9/20	14:15:3	50	0.018	40	40.4	2222	2327 G	26.502848	84.854595	Normal	
		Total IRI					74986				
		Average IRI					3260.26				

$Y = 0 * X^2 + 0.998 * X + 109.5$
 $X = 2222$
 $Y = 2327$
 (R) RURAL ROAD
 Good Average Poor
 <4000 4001-500C >5001

13.9.2020
 S.E

13/9/20
 ARB

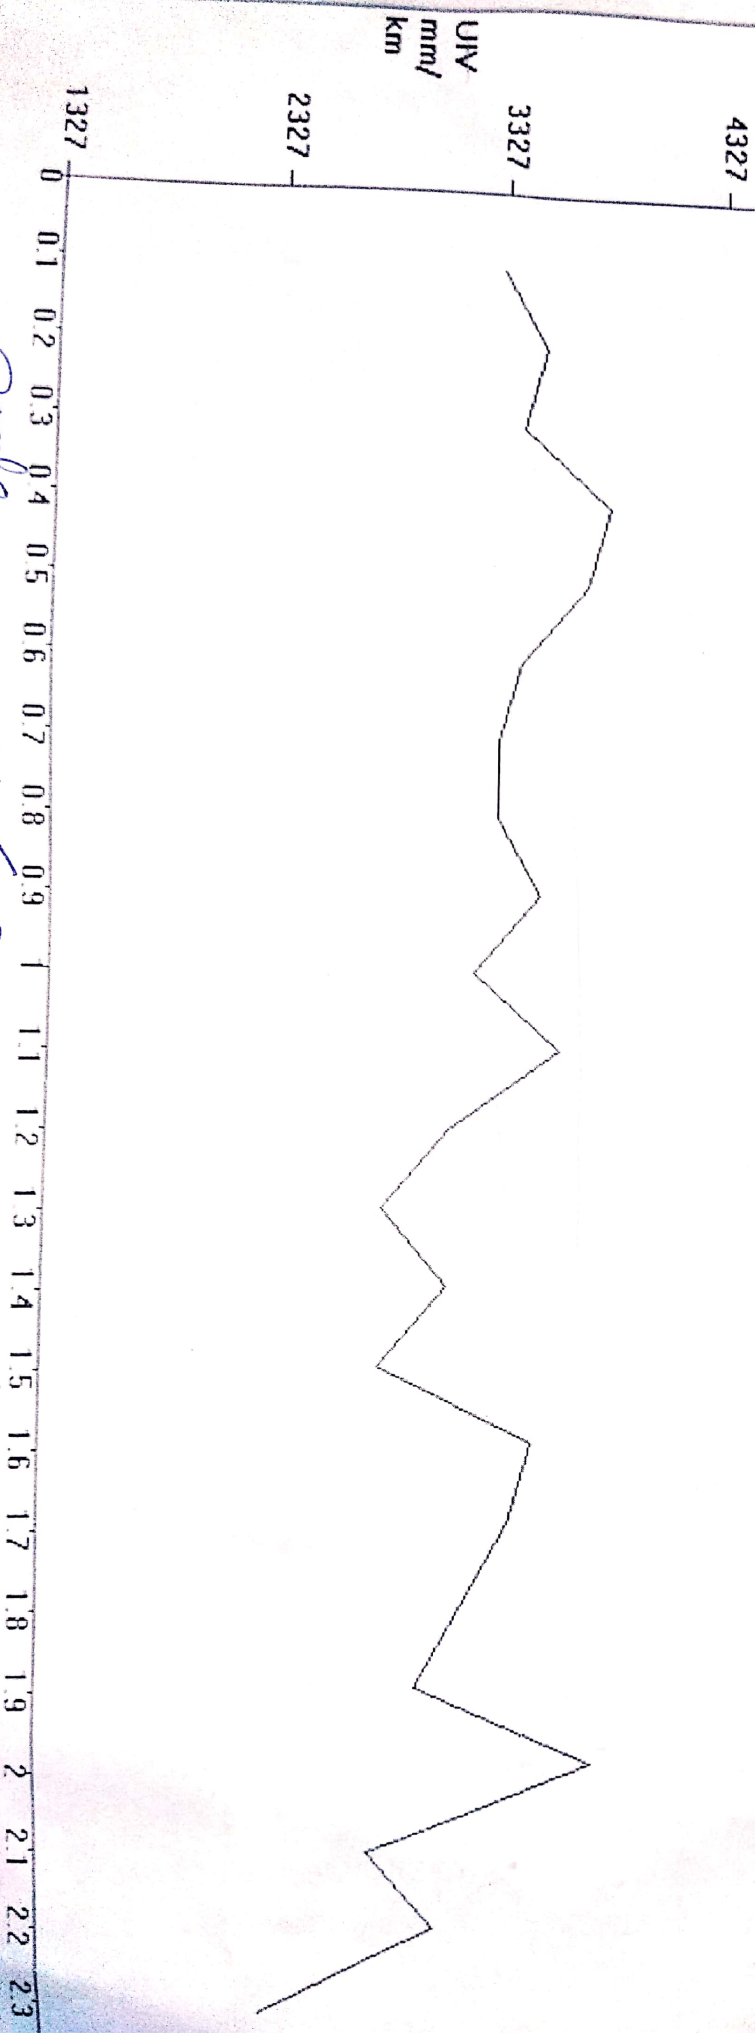
14/9/20
 Executive Engineer
 R.W.D. (W) Division
 Motihari

Name of Customer : Kshrij Construction
 Name of Work/ Road : Dipau to Talwa
 Lab Job number : 317821032387
 Date : 12-09-2020
 Section No. : 50

Test Date : 12-09-2020
 Road Name : Dipau to Talwa
 Machine No : 378
 Road Type : (R) RURAL ROAD
 Start S No : 0.000 KM
 Side :
 Start E No : 2.260 KM
 Weather : Good
 UIV Range : 1327 To 5000
 Dist Range : 0 To 2.4
 Interval : 1000 mm/km
 Start Location : Dipau
 End Location : Talwa
 Equation : $Y = 0 * X^2 + 0.998 * X + 109.5$

File : D:\12091445.Xls, Section No. : 50, Eqn : $Y = 0 * X^2 + 0.998 * X + 109.5$

Name of Customer : Kshrij Construction, Name of Work/ Road : Dipau to Talwa, Lab Job number : 317821032387



Date : 13.9.2020
 S.E.

Distance = 1000 m

Engineer
 R.W.D. (M) Division
