

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

पत्रांक :- 1984

/कटिहार, दिनांक- 26-11-2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, 3रीं मंजिल, भूमि विकास बैंक भवन,
बिहार, पटना।

विषय :- शीर्ष New Maintenance Policy-2018 योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:-यथोक्त।


विश्वासभाजन,


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

ज्ञापांक:- 1984

/कटिहार, दिनांक:- 26-11-2021

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

RWD, Works Division, Katihar

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Katihar

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (In Lac)	up to date expenditure as per MIS (In Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	MR-N/19-20 Kachhar/14	Bari- Bhesh Dira Chowk To Fakir Tola	211551034595	468/ 28.01.20	1.100	44.06890	29.14558	12.65856	09MBD/20-21, 12.09.2020	11.06.2021	20.07.21	2637.45	25mm	5.1%	23.63136	23.63136	4.80697	Completed
Total																		


 Executive Engineer
 RWD, Works Division, Katihar
 22.11.20

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of Nov, 2021

Particulars

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

- i. Works have been supervised by Executive Engineer/Superintending Engineer.
- ii. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- iii. Construction materials have been tested.
- iv. Measurements have been recorded in the MBs and test check conducted by the Assistant.
- v. All other codal formalities have been observed.

- i. Construction of Road Works.
- ii. Construction of CD Works.

Executive Engineer,
WD (W) Division, Katihar.

~~RWD (W)~~ Division, Katihar.

Lab Job number :07

Date :26-07-2021

Name of Customer :Dhananajay Kumar Singh

Name of Work/ Road :Bari- Bhesh Dira Chowk To Fakir Tola

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	1818	G
2	0.200	2206	G
3	0.300	2884	G
4	0.400	2303	G
5	0.500	2400	G
6	0.600	2690	G
7	0.700	3756	G
8	0.800	2690	G
9	0.900	2497	G
10	1.000	2787	G
11	1.100	2981	G
Average IRI value		2637.45	

Handwritten signature
26.7.2021
JE

Handwritten signature
26/7/21
EE
Executive Engineer
R.W.D (W) Division Katihar

Lab Job number :07

Date :26-07-2021

Name of Customer :Dhananajay Kumar Singh

Name of Work/ Road :Bari- Bhesh Dira Chowk To Fakir Tola

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
26/7/21	7:38:19	7	0.1	180	0	1800	1818	G	25.54395	87.38736	Normal
26/7/21	7:39:0	7	0.1	220	10.1	2200	2206	G	25.54350	87.38825	Speed Breaker
26/7/21	7:39:30	7	0.1	290	10.1	2900	2884	G	25.54303	87.38909	Speed Breaker
26/7/21	7:40:0	7	0.1	230	10.1	2300	2303	G	25.54269	87.38998	Normal
26/7/21	7:40:5	7	0.1	240	10.1	2400	2400	G	25.54236	87.39089	Normal
26/7/21	7:40:40	7	0.1	270	10.1	2700	2690	G	25.54196	87.39180	Normal
26/7/21	7:41:0	7	0.1	380	10.1	3800	3756	G	25.54161	87.39273	Normal
26/7/21	7:41:16	7	0.1	270	20.2	2700	2690	G	25.54134	87.39364	Normal
26/7/21	7:41:16	7	0.1	250	20.2	2500	2497	G	25.54090	87.39449	Normal
26/7/21	7:41:51	7	0.1	280	20.2	2800	2787	G	25.54016	87.39510	Normal
26/7/21	7:42:0	7	0.1	300	20.2	3000	2981	G	25.53931	87.39556	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 3333$$

$$Y = 3304$$

(R) RURAL ROAD

Good Average Poor


<4000 4001-5000 >5001

[Signature]

Executive Engineer
R.W.D (N) Division Kathihar

[Signature]
26.7.2021
JE

File : C:\RAM KUMAR\MISC Files\Bump integrator\Barari\Dhananjay Singh\Bhains Diyara to Fakir Tola\26070743.Xls,
Name of Customer : Dhananjay Kumar Singh, Name of Work/ Road : Bari- Bhesh Dira Chowk To Fakir Tola, Lab

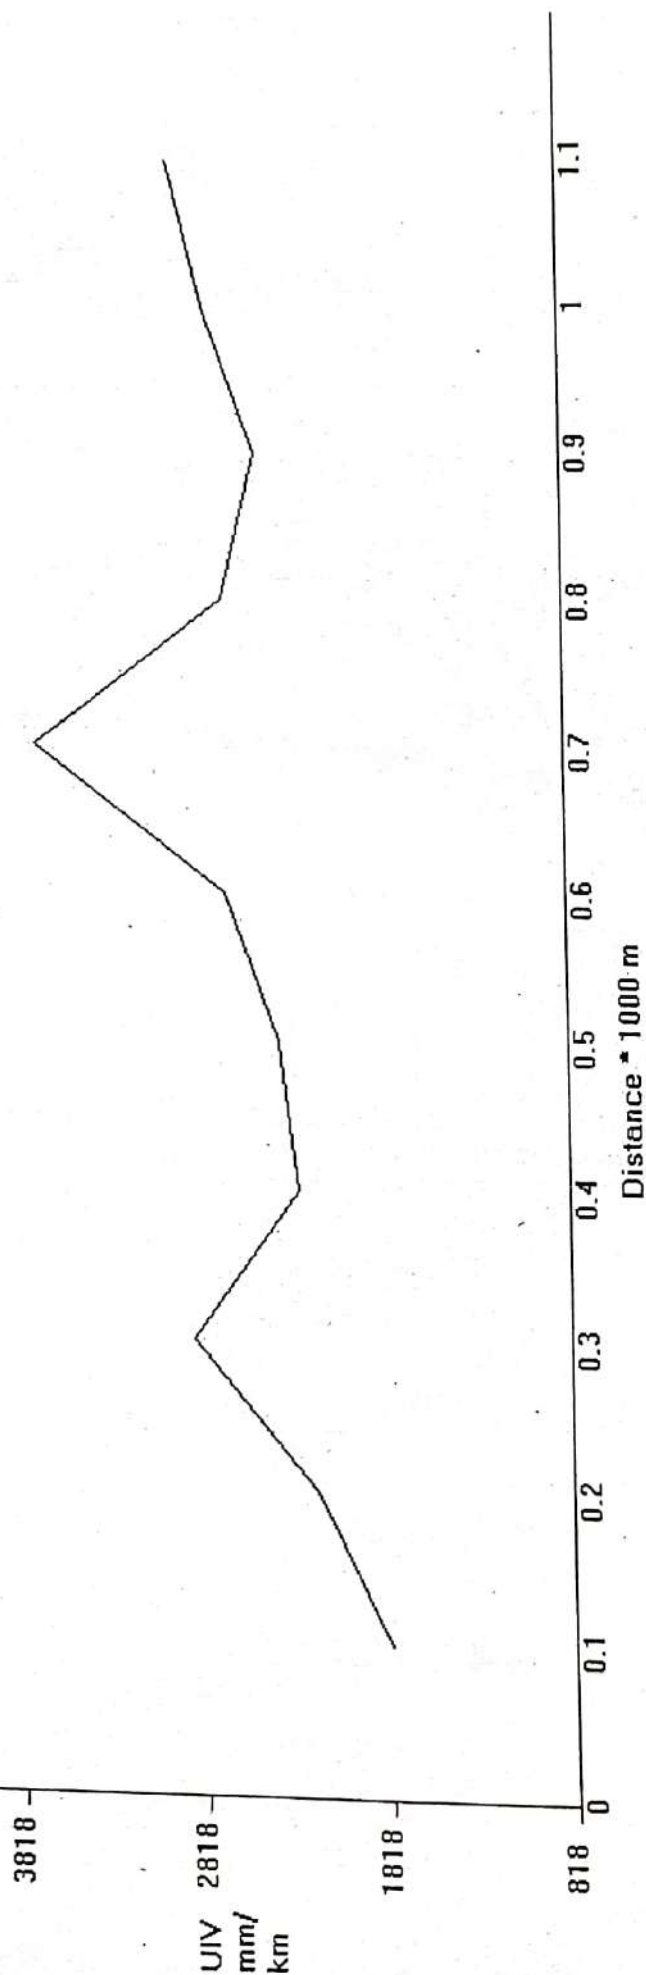

fdg
26.7.2021
JE

R.W.D (W)
Executive Engineer
Executive Engineer
R.W.D (W) Division Kathar
