

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, खगड़िया ।

पत्रांक 960 8430 /
प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, खगड़िया ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना ।

खगड़िया, दिनांक 18-9-2021 /

विषय :- शीर्ष Maintenance Policy-2018 Under MR-3054 योजना अन्तर्गत आवंटन
उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयांकित शीर्ष 3054(MR) के अन्तर्गत कार्यान्वित योजना हेतु माँग
पत्र में अंकित राशि 84.08992 =00 (चौरासी लाख आठ हजार नौ सौ बेरान्वें) रुपये मात्र
आवंटित करने की कृपा की जाय ताकि कार्य की प्रगति सुचारु रूप से चल सके।

अनु० - अधियाचना पत्र।

विश्वासभाजन,

18-9-21
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य
प्रमण्डल, खगड़िया।
14/9/21

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
Name of Works Division :- Khagaria

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount (In		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (In km)	Amount of (In Lakh)	Initial Rectification on with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/KH/KHA/19/0008	N.H-31 - Durgapur Paswan Tola	20904502035	19-Jul-19	0.510	18.96	13.739	4.9388	01/MBD/2019-2024-12-2019	23-Aug-20	work in progress	3606	25	5	0	0	4.95453	
2	RM/KH/KHA/19/0008	Bhadas To Dhusnari Bishanpur Road Part-II	29451032325	19-Jul-19	0.700	36.05	29.417	10.6256	01/MBD/2019-2024-12-2019	23-Aug-20	28-06-21	3606	25	5	0	0	28.10468	
3	RM/KH/KHA/19/0008	Parmannandpur Dhala To Reo Road Via Hardachak	10109663	19-Jul-19	0.800	43.43	36.239	5.8756	01/MBD/2019-2024-12-2019	23-Aug-20	28-05-21	3428	25	5	30.10422	30.10422	5.43071	
4	RM/KH/KHA/19/0011	khagariya jila anataragat haripur panchayat me nista mahaveer asthan se firangi asthan hote hue bairwa mushari tak sarak nirmaan.	20904504001	28-Aug-19	1.68	67.321	45.715	16.33932	05MBD/2020-2116-07-2020	15-Apr-21	14-09-21	3695	25	5	0	0	45.600	

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


 Executive Engineer
 RWD, Works Division
 Khagaria
 14/9/21

FROM GFR 19-A
(See Government of India's Decision (1) below Rule-150)
Form of utilization Certificate up to the Month of 10-09-2021

Executive Engineer,
R.W.D. Works Division,
Khagaria.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Laacs)	Amount Received (in Rs. Laacs)	Particulars
1	MR(3054) under Bihar Rural Road Maintenance Policy - 2018	upto Letter No.17 Date. 26-2-2021 Letter No.20 Date. 19-3-2021 Letter No.22 Date. 24-3-2021 Letter No.30 Date. 21-5-2021	371.93374 155.807660 2.36365 66.07899	Certified that out of Rs.596.18404 Laacs received upto date 10-09-2021 in favour of Executive Engineer, RWD, Bihar Khagaria sum of Rs.593.81905 Laacs has ben utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy - 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 2.36499 remaining unutilized at the end of the period under.
	Total		596.18404	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid wa sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks excrecised :-

- (i) Works have been supervised by Executive Engineer/Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending
- (iii) Construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the
- (v) All other codal formalities have been observed.

- 3 Physical Progress achieved :

- (i) Construction of Road Works.
- (ii) Construction of CD Works.

14/9/21
Executive Engineer,
R.W.D. Works Division,
Khagaria.

14/9/21

14/9

Name of Customer: GIRISH KUMAR
Name of Work/ Road: To Reo Road Via Hardaschak
Lab Job number:
Date: 28-08-21
Section No: 22


Test Date: 28-08-21 Road Name: To Reo Road Via Hardaschak
Machine No: 403 Road Type: (R) RURAL ROAD
Start S No: Side:
Start E No: Interval
Weather: UIV Range: 1628 To 4000 1000 mm/km
Start Location: Dist Range: 0 To 0.9 0.1 * 1000 m
End Location: Equation: $Y = 0 * X^2 + 0.889 * X + 228.2$

Print

Generate Report and Graph

Redraw Graph

Map View

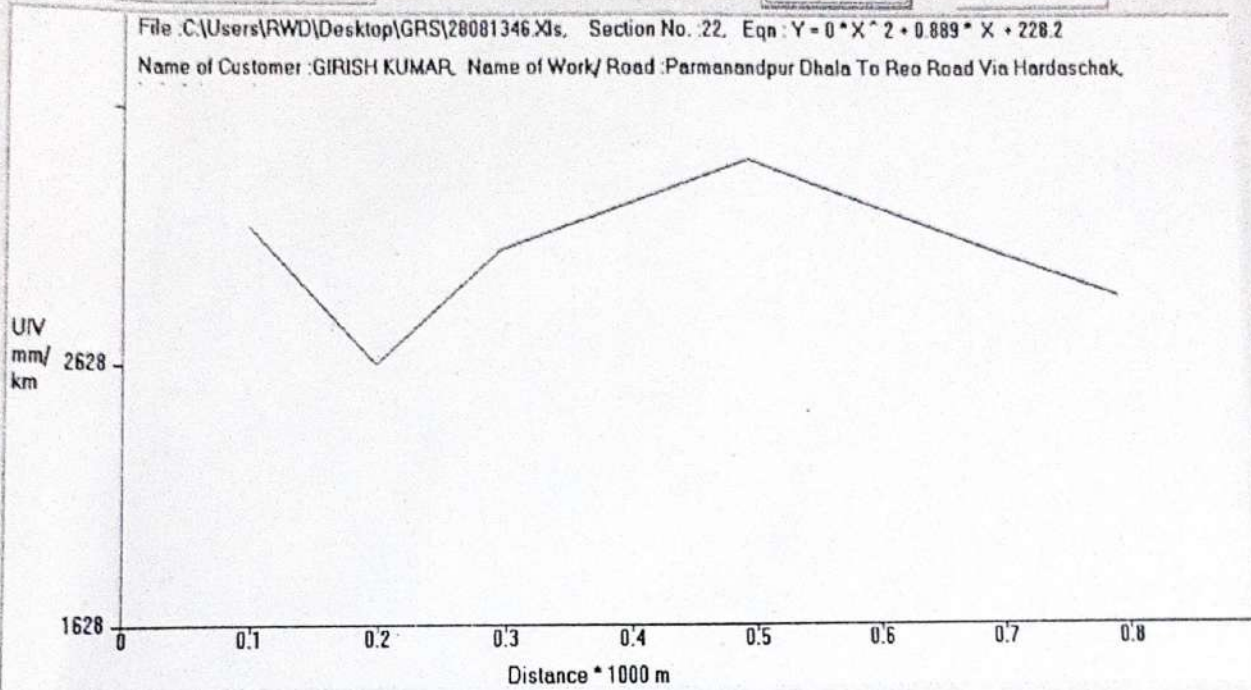

[Signature]
28/08/2021
A.E

[Signature]
28-08-2021
A.E

[Signature]
28-8-21
EE

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
28/8/21	13:36:0	22	0.1	330	10.1	3300	3161	G	25.51327	86.49104	Normal
28/8/21	13:36:9	22	0.1	270	20.2	2700	2628	G	25.51292	86.4914	Normal
28/8/21	13:36:9	22	0.1	320	10.1	3200	3073	G	25.51219	86.492	Normal
28/8/21	13:36:45	22	0.1	340	20.2	3400	3250	G	25.51149	86.49264	Normal
28/8/21	13:37:0	22	0.1	360	10.1	3600	3428	G	25.51111	86.49338	Normal
28/8/21	13:37:20	22	0.1	340	20.2	3400	3250	G	25.5103	86.49394	Normal
28/8/21	13:37:20	22	0.1	320	10.1	3200	3073	G	25.50962	86.49461	Normal
28/8/21	13:37:55	22	0.1	300	20.2	3000	2895	G	25.50904	86.49534	Normal

$$Y = 0 * X^2 + 0.889 * X + 228.2$$

$$X = 3000$$

$$Y = 2895$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

28/08/2021

28-08-2021
A.E

28/8/21
A.E

Name of Work—
 Situation of Work—
 Agency by which work is executed—
 Date of Measurement—
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Road:- Parmanand					
From Dhala To R.E.O Road					
Via Hardaschak (MR)					
Agency:- Gresh Kumar, At:-					
Makahi, Alauli, Kogaria					
Agreement no:- 01MBD					2019-20
Date of start:- 24.12.2019					
Date of completion:-					

(1) clearing and grubbing road land including up rooting wild vegetation.

$$2 \times 8 \times 30.00 \times 1.00 = 480.00 \text{ m}^2$$

$$2 \times 8 \times 30.00 \times 1.00 = 480.00 \text{ m}^2$$

$$2 \times 7 \times 30.00 \times 1.00 = 420.00 \text{ m}^2$$

$$2 \times 1 \times 30.00 \times 1.00 = 60.00 \text{ m}^2$$

$$\underline{720 \text{ M}^2}$$

$$\text{Total} = 1440.00 \text{ m}^2$$

$$= 0.140 \text{ Hec.}$$

(2) Providing and fixing of masonry sign board with legs as per specified
 = 2 Nos.

(3) Construction of granules

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(17) R.C.C. grade m-15 Boundary pillars complete as per plan 16 Nos. vide TMB, P-10 @ 487202/No. ₹ 7792200					
(18) Road marking with hot applied thermoplastic. BT 21.00 m ² vide TMB, P-10 (Limit = 20.0 m) @ 735240/m ² ₹ 14708200					
(19) Road marking with hot applied thermoplastic. BT 3.00 m ² vide TMB, P-10 @ 735240/m ² ₹ 2206200					
(20) Road marking with hot applied thermoplastic. CC 139.40 m ² vide TMB, P-11 @ 82570/m ² ₹ 115103200					
(21) Provisioning and fixing of maintenance project 2 Nos. vide TMB, P-4 + 2 Nos. " " P-11 4 Nos. @ 886127/No. ₹ 85445200					
Total ₹ 316207520					
Add GST @ 12% ₹ 37944920					
Add L.C @ 1% ₹ 31621200					
Total ₹ 357314520					
Less as per agg. 0.55% ₹ 19652200					
Less previous Bill @ 30104220					

Continuation

NET BILL ₹ 5,43,071

28-05-2021
A.C.

28/05/2021
SK
