

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ

पत्रांक 1757 (379) / बिहारशरीफ, दिनांक 24-12-21

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:- नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।


महाशय,


उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अधियाचना पत्र समर्पित की जा रही है।


अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन


24/12/21


24/12/21
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ


24/12/2021

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 24-12-2021

(New Maintenance Policy 2018)

J- BIHARSHARIF

Year-2021-22


Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	latter no. 67 dated 15-12-2021	1318.03290	Certified that out of Rs 1318.03290 received & balance during the years 2021-22 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 1265.71214 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 52.32076 lacs remaining unutilized at the end of the period under 24-12-2021
	Total Rs.		1318.03290	


2 Certified that I have satisfied myself that the conditions on which the grants-in- aid was
Kind of Checks exercised :-


- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works


24/12/21
Divisional Accounts Officer
Rwd, Works Division
Biharsharif


24/12/21
Executive Engineer
Rwd, Works Division
Biharsharif


24/12/2021

Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of BBT (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Increase in Allotment (Demand)	Remarks
				Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	RM/NA/BIH /19/0005	Const. of road from Chandaura Dhamauli Rahui road to Imli Bigha via Chandaura Village & Railway Crossing.	5268 04-10-2019	1.43	28.5834	32.178	15.1598	MBD-07 20-21	07-06-2021		65.87	25.00	5.40	0.00000	0.00000	23.59853	
2	RM/NA/BIH /19/0005	NH-31 Dhamauli More to Deobigha More via Gaganpur, Shivaybigha, Garabidha Dohat.	5268 04-10-2019	1.89	46.439	47.847	19.22609	MBD-07 20-21	07-06-2021		70.98	25.00	5.40	0.00000	0.00000	27.30219	
3	RM/NA/BIH /19/0005	Sonsa Chunnuchak Road to Chandaura Road.	5268 04-10-2019	0.63	13.976	15.574	6.03637	MBD-07 20-21	07-06-2021		23.35	25.00	5.40	0.00000	0.00000	8.71697	
4	RM/NA/BIH /19/0005	Const. of road from Vanda More of Sonsa Path to Village Sondhi via Chand Bathani Chhika.	5268 04-10-2019	2.39	47.546	54.777	23.66314	MBD-07 20-21	07-06-2021		89.95	25.00	5.40	0.00000	0.00000	40.06725	
5	RM/NA/BIH /19/0005	Bind Alpur Road to Sonsikara	5268 04-10-2019	0.63	13.014	13.562	5.90747	MBD-07 20-21	07-06-2021		25.61	25.00	5.40	0.00000	0.00000	8.40134	
6	RM/NA/BIH /19/0005	NH-31 to Amarapur	5268 04-10-2019	0.4	16.94029	20.542	4.7558	MBD-07 20-21	07-06-2021		15.68	25.00	5.40	0.00000	0.00000	17.36700	
7	RM/NA/BIH /19/0005	LO52 - T01 to Bhadwa (VR21)	5268 04-10-2019	0.990	17.22693	19.907	10.55564	MBD-07 20-21	07-06-2021		34.03	25.00	5.40	0.00000	0.00000	18.00000	
TOTAL																	
Total =																	

(43.45328)

1. Signed Hard Copy and Soft Copy (in Excel) of recorded BBT is enclosed.
2. Up-to-date Physical Progress has been uploaded in MIS.

24/12/21
24/12/21
Divisional Accounts Officer
Rwd. works Division Biharsharif

24/12/21
24/12/21
Executive Engineer
Rwd. works Division Biharsharif

Case of Road:-Sonsa Chunchachak Road To Chandwara
Name of Contractor:- M/S Uday Shankar Prasad

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	UTV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
		No.										
5/12/21	10:20:14	61	0.1	220	0	2200	2353	G	3.24	25.280068	85.61094	Normal
5/12/21	10:20:14	61	0.1	240	30.3	2400	2533	G	3.46	25.28002	85.6119	Normal
5/12/21	10:20:49	61	0.1	210	10.1	2100	2263	G	3.13	25.279898	85.61296	Normal
5/12/21	10:21:0	61	0.1	220	10.1	2200	2353	G	3.24	25.27901	85.61293	Normal
5/12/21	10:21:25	61	0.1	230	0	2300	2443	G	3.35	25.278298	85.61268	Normal
5/12/21	10:22:0	61	0.1	200	30.3	2000	2173	G	3.02	25.278345	85.612	Normal
5/12/21	10:22:0	61	0.03	300	30.3	3000	3071	G	4.11	25.278312	85.61066	Normal
Total			0.630	1620.00	111.10	16200.00	17189.00		23.55			

DR
24/12/21
AB

$Y = 0 * X^2 + 0.898 * X + 377.8$		
X = 2471		
Y = 2596		
(R) RURAL ROAD		
Good	Average	Poor
<4000	4001-5000	>5001

Executive Engineer
R.W.D. (W)
Division Biharsharif (Nalanda)

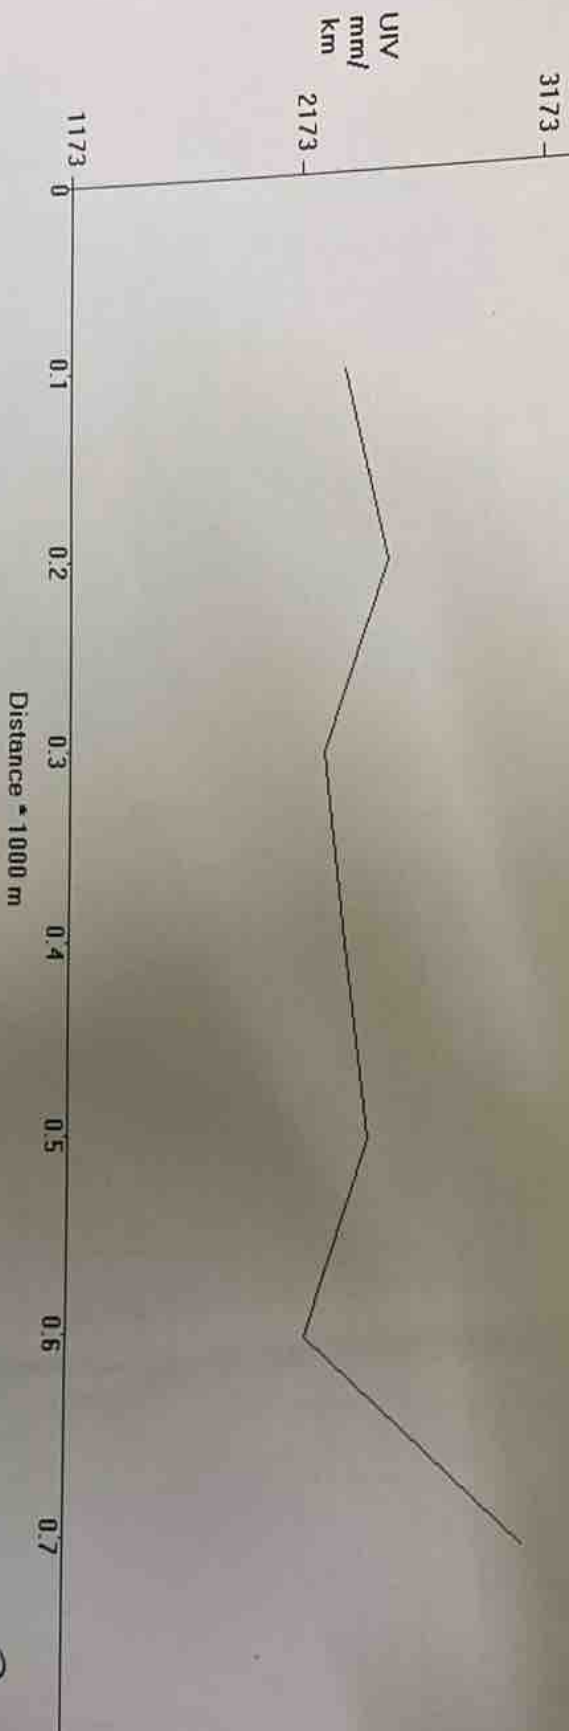
24/12/21

24/12/21

भागप काय विभाग

File : F:\19121130.Xls, Section No. : 61, Eqn : $Y = 0 \cdot X^2 + 0.898 \cdot X + 377.8$

Name of Customer : MS Uday Shankar Prasad, Name of Work/ Road : Sorsa Chunnuchak Road to Chandaure, Lab



[Signature]
24/11/21

[Signature]
24/11/21
AB


[Signature]
24/11/21

Executive Engineer


R.W.D. (V)

Division Biharsharif/Nalanda,


प्रमाणित किया जाता है कि इस साप्ताहिक प्रमाणित
में मशीन से छपे कुल 100 (सौ) पृष्ठ हैं जिनमें
श्री रामरत्नकृष्ण प्रसाद सिंह भादव सहायक
आभियन्ता, ग्रामीण कार्य विभाग कार्य अवर
प्रमंडल, रहुई के गज निर्गत किया जाता है।


30/8/20

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बिहार शरीफ


30/8/20

Re-issued to Sri Binod Kumar Singh,
J.B. Rahuri


20/10/20
AR

Sch, XLV-Form No. 134

बिहार शरीफ DIVISION

रहुई SUB-DIVISION

Measurement Book

No. 2989

Name of Officer

श्री रामरत्नकृष्ण प्रसाद सिंह भादव

सहायक आभियन्ता अवर प्रमंडल, रहुई

Date of first entry 28/10/20

Date of last entry

Name of Work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement -

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	<u>Record entry</u>				
Name of work -	Maintenance of Road				
from	Sukha chunchunchak road				
to	chandwaru				
Heed -	3054				
Agency -	M/S Uday Shankar Prasad				
Agreement No -	MBD-07/2020-21				
Agreement Rate -	0.001 Below of BGR Rate				
Agreement Amount -					
Work start Date -	08/09/2020				
Date of completion -	07/06/2021				
Date of entry -	28/10/20				
(194) Cleaning and grubbing road					
land - -	all complete RB				
	$2 \times 30 \times 30 \times 1 \times 1 =$				180 m^2
	$2 \times 40 \times 30 \times 1 \times 1 =$				240 m^2
	$2 \times 20 \times 30 \times 1 \times 1 =$				120 m^2
	$2 \times 10 \times 23 \times 1 \times 1 =$				46 m^2
	$2 \times 10 \times 28 \times 1 \times 1 =$				56 m^2
	$2 \times 30 \times 30 \times 1 \times 1 =$				180 m^2
	$2 \times 20 \times 30 \times 1 \times 1 =$				120 m^2
	$2 \times 10 \times 24 \times 1 \times 1 =$				48 m^2
					990 m^2
					$= 0.099 \text{ Hec}$
(219) Provisioning and branding					
Informative sign board -	44				
Complete RB					2 Hec

By Sup
28/10/20

By Continuation
21/11/20
AB

Continuation
