

Inspection Report For Flood Damage Work

Date :- 21.11.2021

1. Name of PIUs :- Er Bi'jay Kumar.

2. Name of Block/Road :- Rahui/Rahimpur foot over Bridge To Gobaniya village

A. For Road

1. Damage Location/Chainage :- 0.00 to 175.00 mtr.

2. Damage Length :- 12.50 mtr.

3. Nature of Damage :- Crust and flank.

4. Details of Restoration Works :-

- Material being used in Restoration Works:- Brick Bats.
- Equipments/ Tools being used in Restoration Works:- J.C.B and Tractor.
- Procedure taken up in Restoration Works:- Departmental
- Restored Length:- 12.50 mtr.

B. For Bridge

1. Damage Location/Chainage:-

2. Damage Length:-

3. Nature of Damage:-

4. Details of Restoration Works:-

- Material being used in Restoration Work:-
- Equipments/ Tools being used in Restoration Works:-
- Procedure taken up in Restoration Works:-
- Restored Length:-

NA.


C. Requirement Of New CD/Bridge

- Name of Road:-
- Location Chainage:-
- Type of CD Work/Length Required

Upload one photograph of damage portion if available

Attach minium two photograph (during restoration & after restoration) photographs

Should be Geotags and at least one photo be captured in selfie mode. work is Satisfactory.


21.11.21
Signature of JE/AE/EE


21.11.21
Signature of verifying officer



ग्रामीण कार्य विभाग


Rural Works Department, Govt of Bihar

BIHAR RURAL ROADS PROJECT

Govt. of Bihar

FDR(Motorable)

Estimate for Motorable of Road from Rahimpur foot over Bridge to Gobariya village in Nalanda District.

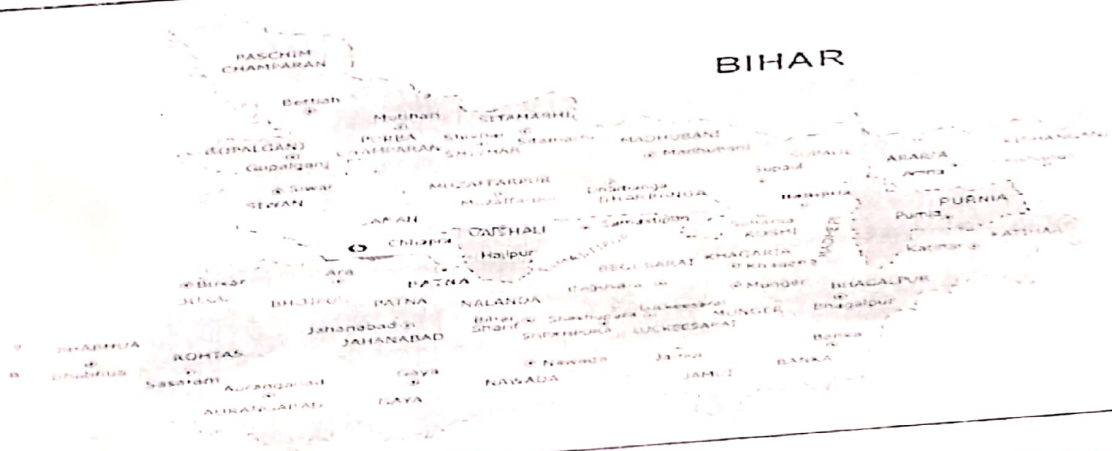

Name of the Road :-

Rahimpur foot over Bridge to Gobariya village

DISTRICT	:	NALANDA	
DIVISION	:	Biharsharif	
BLOCK	:	Rahm' Bind	
TOTAL COST OF CONSTRUCTION	:	0.217	Lac
TOTAL COST OF PROJECT	:	0.217	Lac

SUBMITTED BY
RURAL WORKS DEPARTMENT
WORKS DIVISION-BIHARSHARIF

पथ का नाम :- रहीमपुर फुट ओवर ब्रिज से गोबरिया ग्राम

प्राक्कलित राशि :- 0.217 लाख

प्रतिवेदन

प्रस्तुत प्राक्कलन जिसकी प्राक्कलित राशि 0.217लाख है ग्रामीण कार्य विभाग, कार्य प्रमंडल, बिहारशरीफ अन्तर्गत रहुई प्रखंड में वर्ष-2021 में आयी बाढ़ के कारण क्षतिग्रस्त पथ के मरम्मत हेतु तैयार किया गया है।

उपर्युक्त पथ का निर्माण नाबार्ड योजनान्तर्गत किया गया है। वर्ष-2021 में पंचाने नदी में आई बाढ़ के कारण पथ के उपर से पानी का बहाव शुरू हो गया एवं पानी बहाव के कारण मिट्टी का कटाव हुआ एवं पथ 12.5 मीटर लंबाई में कटाव हो गया फलतः आवागमन बाधित हो गया एवं ग्रामीणों का अन्य जगह से संपर्क टुट गया।

विभागीय निर्देशानुसार कटे हुए भाग को ईट के टुकड़ों से भरने के उपरान्त आवगमन को चालू किया गया। पूर्ण रूप से कटे हुए भाग में ब्रिक बैट द्वारा पथ मरम्मत किया गया। प्रस्तुत प्राक्कलन में कराए गए कार्य में ब्रिक बैट का उपयोग किया गया। कार्य के उपरान्त स्थल निरीक्षण के क्रम में उच्चाधिकारियों द्वारा जाँच करा लिया गया है। प्राक्कलन में लिया गया दर अंचल कार्यालय द्वारा पत्रांक-458 दिनांक-19.06.2021 द्वारा अनुमोदित दर से लिया गया है। सिर्फ ढुलाई का दर नहीं रहने के कारण इसे वर्तमान अनुसूचित दर पर तैयार किया गया है।

इस योजना की राशि FDR (3054) में भारित होगा। यथाशीघ्र प्राक्कलन की स्वीकृति अपेक्षित है।


29.10.21

कनीय अभियंता,
कार्य प्रशाखा, रहुई


29/11/21

सहायक अभियंता
कार्य अवर प्रमंडल, रहुई


11/11/21

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बिहारशरीफ

SUMMARY OF COST ESTIMATE FOR THE PROJECT

NAME OF ROAD : Rahimpur foot over Bridge to Gobariya village

DISTRICT NALANDA

BLOCK Bind

DIVISION Biharsharif

Sl. No.	DESCRIPTION	AMOUNT (LAKHS)
1	BRICK BATS	21713.000
5	GSB & Sand Bag	0.000
	Total	21713.000
	TOTAL COST IN LACS =	0.217
	TOTAL COST OF PROJECT IN LACS =	0.217

Keiser
29.10.21
JE
RWD

By
29/10/21
AE
RWD

Gm
11/11/21
EE
RWD

Technically ^{Sanctioned} approved for Rs. 21,713.000 ..

(Rupees Twenty One Thousand

Seven Hundred only ..)

Condition and direction laid down in attached technical notes with DPR is be followed Strictly

Akshay
2/12/2021
S. E.

RWD

Work Circle Nalanda

9
10/12/2021

g
simpler
C
X
O
ABT
ap
th
ur
y

EE 1/11/21

Name of Road Rahimpur foot over Bridge to Gobariya village
Block Bind
District NALANDA

Calculation of Brick Bats

Sl.No	Lenth (m)		Width(m)		Thickness (m)		Qty. (Cum)
1	$\frac{6.0+5.0}{2}$	x	$\frac{0.6+1.00}{2}$	x	$\frac{1.0+1.5}{2}$	=	5.500
2	$\frac{6.5+5.75}{2}$	x	$\frac{0.8+1.3}{2}$	x	$\frac{1.0+1.2}{2}$	=	7.074
							<u>12.574</u>
						=	10.778

Net Quantity After Deduction of Voids @ 12/14*12.574

Keingl
29.10.21
J E

AA
29/10/21
AA

Name of Road:- Rahimpur foot over Bridge to Gobariya village
District:- NALANDA
Block :- Bind

SI No	Item with Source	Unit	Source Up to	Carriage Cost & Lead in Km										Loading & Unloading Cost	Carriage Cost by Rail Head	Total			
				Pukka / Surface					Katcha										
1	Brick bat	Cum	Local	3.60	x	19.79	x	7.00 Km	=	Rs 221.68	3.60	x	24.73	x	1.00 Km	=	Rs 39.56	186.67	Rs 447.91
				2.25	x					2.25									0.00

Jeinik
29.10.21
JE
RWD

Carriage Including GST and Labour Cess
For Brick Bats

AE
29/10/21
RWD

AE
11/12
RWD
506.1383

Analysis of Rates (FORMAT F8)

4.2	402	PAVEMENT CRUST LAYERS				
		For Grading II Material (Type B)				
		Construction of Gravel/Soil-aggregate base by providing well graded material, spreading in uniform layers with motor on prepared surface, mixing by mix in place method with rotavator at OMC, and compacting with three wheel 80-100 kn static roller to achieve the desired density, complete as per Technical Specification Clause 402.				
	(ii)	For Grading II Material (Type B)				
		Unit = cum				
		Taking output = 300 cum				
	a)	Labour				
		Mate	day	0.48	407.00	195.36
		Mazdoor (Skilled)	day	2.00	407.00	814.00
		Mazdoor (Unskilled)	day	10.00	321.00	3210.00
	b)	Machinery				
		Tractor with Trolley	hour	6.00	630.00	3780.00
		8-10 Ton Smooth Wheeler Roller	hour	30.00	883.00	26490.00
		Tractor with Trolley 25 cum per hour	hour	12.00	630.00	7560.00
	c)	Material				
		Well graded granular sub-base material including GST, Labour Cess and Seignorage Fee with Carriage				
			cum	383.00	1200.00	459600.00
		Cost of GSB for 300 cum				501649.36
			CUM			1,672.16

SDB Sl. No.	MOR D Ref No.	DESCRIPTION	Unit	Quantity	Rate	Amount (In Rs)
1.1 RCD		Loading and Unloading of brick bats with tractor				
		Unit=cum				
		Taking output= 2.25 cum				
		Time required for				
		i) Positioning of tipper at loading point		1 MIN		
		ii) Loading by front end loader 1 cum bucket capacity @ 25 cum per hour		5 Min		
		iii) Maneuvering, reversing, dumping and turning for return		0 Min		
		iv) Waiting time, unforeseen contingencies etc		6 Min		
		Total				
		a) Labour				
		Male	day	0.03	407	12.210
		Mazoor for loading and unloading	day	0.72	268	192.960
		b) Machinery				
		Tractor 3.60 tonne capacity	hour	0.1	630	63.000
		Front end loader 1cum bucket capacity @25 cum/hour	hour	0.083	1543	128.069
		c) Overhead charges @ 0.06 on (a+b)				23.774
		d) contractor profit @ 0.0on (a+b+c)				0.000
		Cost for 2.25 cum= (a+b+c+d)				420.013
		Rate per cum= (a+b+c+d)/2.25				186.673
	Note	Unloading will be done manually				
1.4 RCD		Cost of Haulage Excluding Loading and Unloading				
		Haulage of material by Tractor excluding cost of loading, unloading and stacking.				
		Unit= t.km				
		Taking output 3.60 tonnes load and lead 10 km= 36.0 t.km				
	i)	Surface Road				
		Speed with load : 15 km/hour				
		Speed while Returning empty : 25 km/ hour				
		a) Machinery				
		Tractor 3.6 tonne capacity				
		Time taken for onward haulage with load	hour	0.667	630.00	420.210
		Time taken for empty return trip.	hour	0.4	630.00	252.000
		Total				672.210
		b) Add overhead charges @0.06				40.333
		c) Add contractor profit @0.0				0.000
		cost for 36 t km = a+b+c				712.543
		Rate per t.km = (a+b+c)/36				19.793
	ii)	Unsurface Graveled Road/ Katcha				
		Speed with load : 12 km/ hour				
		Speed for empty return trip: 20 km/ hour				
		a) Machinery				
		Tractor 3.6 tonnes capacity	hour	0.833	630.00	524.790
		Time taken for onward haulage with load	hour	0.5	630.00	315.000
		Time taken for empty return trip				839.790
		Total				50.387
		b) Add overhead charges @0.06				0.000
		c) Add contractor profit @0.0				890.177
		Cost for 36 t.km = a+b+c				24.727
		Rate per t.km = (a+b+c)/36				
