

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक 177 (अनु)

रक्सौल, / दिनांक 03/03/22.

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेन्सी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 के तहत आवंटन
उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषयक गैर योजना शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण
नीति-2018 संलग्न सूची के अनुसार आवंटन अधियाचना विहित प्रपत्र में भरकर आवश्यक
कार्रवाई हेतु समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची


1. पथों का आवंटन अधियाचना प्रपत्र।

विश्वासमाजन,


03/03/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Requisition of Allotment under Head MIR HEAD-3054 Under Bihar Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)


Sl. No.	Package No.	Name of Road	Contractor Name	Project ID as per MIS	Administrative Approval (A/A) Letter No. & Date	A.A.		Agreement Value		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percent	Previous Total Allotted Amount	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
						Length (in Km)	Total (Amount) (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Yrs Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
1	MIR-N-20-21/Raxaul01	Kaurihar Chowk to Naya Tola Laxmipur via KCTC Collage	Paramba Construction Pvt Ltd	317851032674	3054-04-105-2020 3309/2020 Raxaul-08 07 2020	3.900	216.84300	180.309	35.6383	01 MIBD/202 1-22	30-07-2021	-	2361	25mm	5	0	0	180.30902	Work Completed
																		180.30902	


 Executive Engineer,
 Rural Works Department,
 Works Division, Raxaul

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

प्रमाण-पत्र


योजना शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 के तहत Kaurihar Chowk to Naya Tola Laxmipur via KCTC Collage पथ के मापी पुस्त पर इस आशय का प्रमाण-पत्र दर्ज है कि कार्य गुणवत्ता पूर्ण कराया गया है एवं विशिष्टियों के अनुरूप है।


3/3/22

कनीय अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रशाखा, रक्सौल।


03/03/22

सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, रक्सौल।


3/3/2022

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Name of Road:-Kaurihar Chowk To Naya Tola Laxmipur via KCTC Collage
Name of Contractor:-Paramba Construction Private Limited

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	Latitude	Longitude	Event	
3/3/22	11:3:30	31	0.1	300	0	3000	3103 G	26.97769	84.84096	Normal		$Y = 0 * X^2 + 0.998 * X + 109.5$
3/3/22	11:3:55	31	0.1	320	20.2	3200	3303 G	26.97679	84.84099	Normal		$X = 16000$ $Y = 16077$
3/3/22	11:4:23	31	0.1	250	20.2	2500	2604 G	26.9759	84.8412	Normal		
3/3/22	11:5:1	31	0.1	230	20.2	2300	2404 G	26.97505	84.84148	Normal		
3/3/22	11:5:34	31	0.1	210	20.2	2100	2205 G	26.97418	84.84167	Normal	(R) RURAL ROAD	
3/3/22	11:5:58	31	0.1	270	20.2	2700	2804 G	26.9733	84.84189	Normal	Good	
3/3/22	11:6:30	31	0.1	230	20.2	2300	2404 G	26.97245	84.84217	Normal	Average	
3/3/22	11:6:57	31	0.1	240	20.2	2400	2504 G	26.97152	84.84237	Normal	Poor	
3/3/22	11:7:28	31	0.1	190	20.2	1900	2005 G	26.97062	84.84253	Normal	<4000	4001-5000 >5001
3/3/22	11:7:59	31	0.1	170	20.2	1700	1806 G	26.96976	84.84242	Normal		
3/3/22	11:8:25	31	0.1	310	20.2	3100	3203 G	26.96886	84.84239	Normal		
3/3/22	11:8:55	31	0.1	170	30.3	1700	1806 G	26.96798	84.84237	Normal		
3/3/22	11:9:22	31	0.1	260	20.2	2600	2704 G	26.96707	84.84205	Normal		
3/3/22	11:9:53	31	0.1	330	20.2	3300	3402 G	26.96622	84.8419	Normal		
3/3/22	11:10:14	31	0.1	240	20.2	2400	2504 G	26.96535	84.84162	Normal		
3/3/22	11:10:55	31	0.1	320	20.2	3200	3303 G	26.9646	84.8421	Speed Breaker		
3/3/22	11:11:16	31	0.1	230	20.2	2300	2404 G	26.96378	84.84219	Normal		
3/3/22	11:11:57	31	0.1	150	30.3	1500	1606 G	26.96294	84.84185	Culvert		
3/3/22	11:12:28	31	0.1	190	10.3	1900	2005 G	26.96206	84.84162	Normal		
3/3/22	11:12:56	31	0.1	150	10.3	1500	1606 G	26.96123	84.84109	Normal		
3/3/22	11:13:32	31	0.1	170	10.3	1700	1806 G	26.9604	84.84072	Normal		
3/3/22	11:13:51	31	0.1	170	10.4	1700	1806 G	26.95958	84.84045	Normal		
3/3/22	11:14:22	31	0.1	180	10.3	1800	1905 G	26.95868	84.84012	Culvert		
3/3/22	11:14:53	31	0.1	160	30.3	1600	1706 G	26.95791	84.8397	Normal		
3/3/22	11:15:24	31	0.1	170	30.3	1700	1806 G	26.95698	84.83941	Normal		
3/3/22	11:15:55	31	0.1	180	20.2	1800	1905 G	26.95606	84.83929	Normal		
3/3/22	11:16:26	31	0.1	220	20.2	2200	2305 G	26.95533	84.83961	Normal		
3/3/22	11:16:57	31	0.1	170	30.3	1700	1806 G	26.95436	84.83981	Normal		
3/3/22	11:17:28	31	0.1	310	20.2	3100	3203 G	26.95348	84.84	Normal		
3/3/22	11:17:59	31	0.1	290	20.2	2900	3003 G	26.95257	84.84	Normal		
3/3/22	11:18:26	31	0.1	190	20.2	1900	2005 G	26.95167	84.83995	Normal		
3/3/22	11:18:51	31	0.1	210	30.3	2100	2205 G	26.95082	84.83988	Normal		
3/3/22	11:19:22	31	0.1	180	30.3	1800	1905 G	26.9499	84.83997	Normal		
3/3/22	11:19:53	31	0.1	200	20.3	2000	2105 G	26.949	84.83993	Normal		
3/3/22	11:20:24	31	0.1	260	30.3	2600	2704 G	26.94811	84.83976	Culvert		

Done 3/3/22 7.8 1008/10/22

CLM

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	CATEGORY	Latitude	ongitude	Event
3/3/22	11:20:55	31	0.1	180	20.2	1800	ROAD	26.94723	84.83963	Normal
3/3/22	11:21:16	31	0.1	220	20.2	2200		26.94702	84.83963	Normal
3/3/22	11:21:47	31	0.1	350	20.2	3500		26.96460	84.83210	Normal
3/3/22	11:22:18	31	0.1	230	20.2	2300		26.96378	84.83219	Normal

Total IRI	92076
Average IRI	2360.923

$$Y = 0 \cdot X^2 + 0.998 \cdot X + 109.5$$

[Signature]
3/3/22
J.E.

[Signature]
3/3/22
J.E.

[Signature]
3/3/2022

Executive Engineer
Rural Works Department
Works Division, Raichur

[Signature]
3/3/22
J.E.

[Signature]
3/3/22
J.E.

ಈ ದಿ. 27/3/22 ರಂದು 3.90 km ಇ-
ದ್ದರಲ್ಲಿ 20.2 ರಿಂದ 21.4

[Signature]
3/3/22

Executive Engineer
Rural Works Department
Works Division, Raichur

Steco Analyzer

Name of Customer : Paramba Construction Private L
 Name of Work/ Road : Kaurihar Chowk To Naya Tola
 Lab Job number : 08
 Date : 03-03-2022
 Section No. : 31

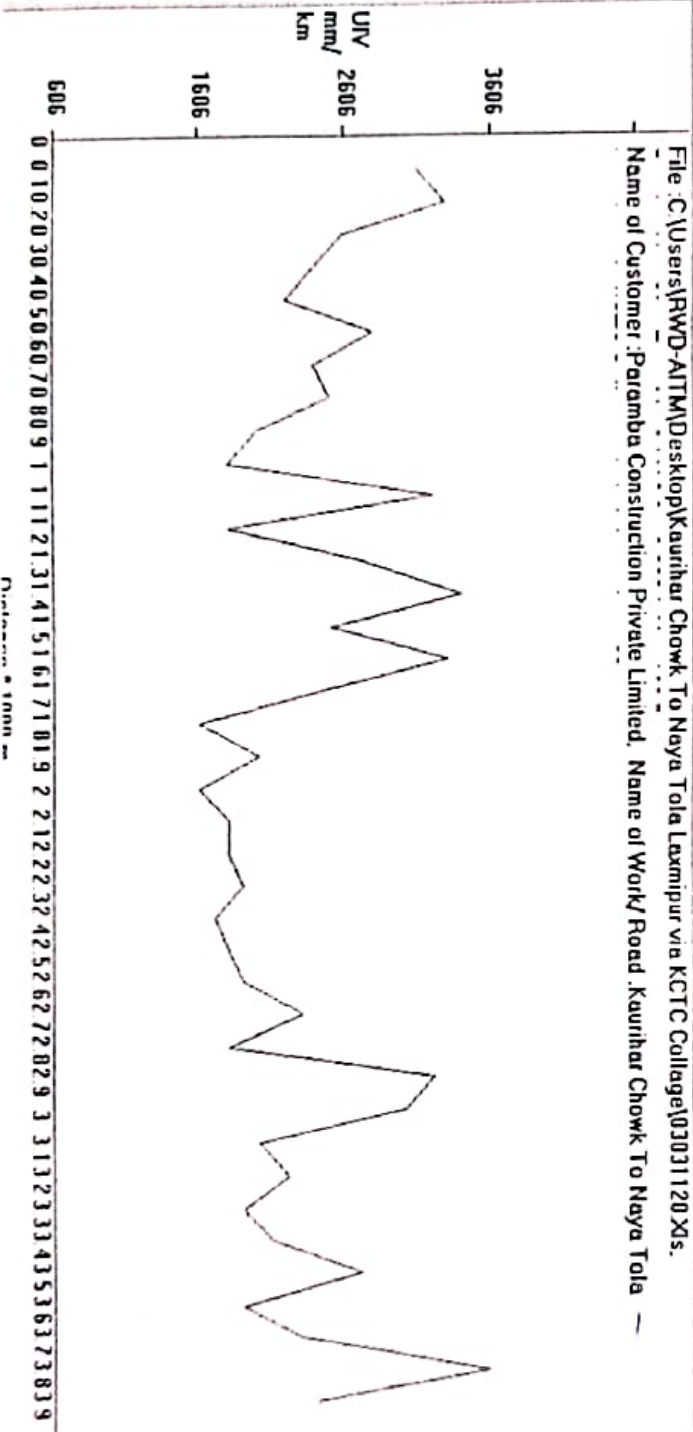
Test Date :	03-03-2022	Road Name :	Kaurihar Chowk To Naya Tola
Machine No :	378	Road Type :	(R) RURAL ROAD
Start S No :	0 0000m	Side :	Interval
Start E No :	3 9000m	Weather :	Normal
Weather :	Normal	UV Range :	605 To 5000 mm/km
Start Location :	Kaurihar Chowk	Dist Range :	0 To 4 01 1000 m
End Location :	Naya Tola Le	Equation :	$Y = 0 \cdot X^2 + 0.998 \cdot X + 1095$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\RWD-ATM\Desktop\Kaurihar Chowk To Naya Tola Luxmipur via KCTC Collage\03031120.Xls.
 Name of Customer : Paramba Construction Private Limited. Name of Work/ Road : Kaurihar Chowk To Naya Tola



Shree

808/5/22
 8/5/22

RWD
