

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

पत्रांक :- 435

/कटिहार, दिनांक- 03-03-22

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, 3री मंजिल, भूमि विकास बैंक भवन,
बिहार, पटना।

विषय :- शीर्ष New Maintenance Policy-2018 योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

ज्ञापांक:- 435

/कटिहार, दिनांक:- 03-03-22

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

12-2-2022.

RWD, Works Division, Katihar

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Katihar

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Alloted Amount (In Lac)	up to date expenditure as per MIS (In Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	MR-N/19-20 Katihar/14	Marpa Balua To Bhandartal	21105602040	468/28.01.20	7.200	242.76700	153.75965	76.57317	09MBD/20-21, 12.09.2020	11.06.2021	18.08.2021	2223.35	25mm	5.1%	150.00000	150.00000	1.11087	Completed
2	MR-N/19-20 Katihar/08	Bharsia Korha Falga PWD road to Mohammad Nagar	21105602012	5129/24.09.19	4.018	135.01800	78.98592	40.39058	03MBD/20-21, 03.07.2020	02.04.2021	-	2060.17	25mm	5.1%	0.00000	0.00000	70.78639	Surface Complete
3		Sarsi-Kursela PWD road to Ramnakhil	21105602059	5129/24.09.19	4.420	170.03500	115.24879	45.27029	03MBD/20-21, 03.07.2020	02.04.2021	-	2365.13	25mm	5.1%	0.00000	0.00000	84.44665	Surface Complete
4		Sarsi-Kursela PWD road to Gobindpur	21105602061	5129/24.09.19	3.840	146.52900	100.34165	39.33973	03MBD/20-21, 03.07.2020	02.04.2021	-	2069.13	25mm	5.1%	0.00000	0.00000	73.16449	Surface Complete
5		Sarsi Kursela PWD road to Simeria	21105602062	5129/24.09.19	3.060	103.21200	63.03863	31.04941	03MBD/20-21, 03.07.2020	02.04.2021	-	1934.81	25mm	5.1%	0.00000	0.00000	55.25606	Surface Complete
6		PWD Road to Lohani to PWD road Amin Chowk	21105501016	5129/24.09.19	2.380	104.05600	57.42817	24.68233	03MBD/20-21, 03.07.2020	02.04.2021	-	2041.21	25mm	5.1%	0.00000	0.00000	32.57384	Surface Complete
															150.00000	150.00000	317.33830	
															Total			

Divisional Accounts Officer-Gr-I
R.W.D (W) Division, Katihar

Executive Engineer
RWD, Works Division, Katihar
12.2.2022

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of Jan, 2022
New Maintenance Policy-2018

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

- i. Works have been supervised by Executive Engineer/Superintending Engineer.
- ii. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- iii. Construction materials have been tested.
- iv. Measurements have been recorded in the MBs and test check conducted by the Assistant.
- v. All other codal formalities have been observed.

- i. Construction of Road Works.
- ii. Construction of CD Works.

- i. Work has been done as per specification and with quality.
- ii. Work done measurement entered in MB has been verified 100 % by JE, 50% by AE and 10% by EE.

Divisional Accounts Officer-Gr-I
R.W.D (W) Division, Katihar

Executive Engineer,
WD (W) Division, Katihar.

MR-N/13-20

Schedule XLV-Form No. 134

SARSI-KURSELA PUJ ROAD TO
GOBINDPUR

R.W.D. KATHAR DIVISION

FAL KA SUB-DIVISION

NO - 2119.

MEASUREMENT BOOK

ASHOK KUMAR

and machine of good
from SSSI Karsela
paid road to
Ground per order
SOSM
Name of contractor -
Sri Anshok Kumar
Kahinor
Agr. No - 311012024
Jat & of work spot -
02.07.2020
Date of completion -
02.04.2021
17704

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					2399640-00
10 11					Plr and paving SD. B. C. P.H. nile 7000. 18
361.616					2399640-12-349578520
11					Road Marking
24					Plr and paving
716					2399640-526546
12					Road Marking
24					Plr and paving
					P. 20
50					2399640-41029
13					Plr and paving Paved. B. C. P.H. Plr and paving
2 Nos					2399640-18870
					1122078820
					12464950
					1220800
					12677490
					648187000
					7778240
					6481900
					732451300
					805700
					731645600

Continuation

Handwritten signature
7/11/2021
A-E

Handwritten signature
7/11/2021

Lab Job number :25

Date :09-01-2022

Name of Customer : Ashok Kumar

Name of Work/ Road : Sarsi-Kursela PWD Road to Gobindpur

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2787	G
2	0.200	2206	G
3	0.300	2400	G
4	0.400	2012	G
5	0.500	2109	G
6	0.600	2012	G
7	0.700	2109	G
8	0.800	1818	G
9	0.900	1721	G
10	1.000	2109	G
11	1.100	2109	G
12	1.200	2206	G
13	1.300	3756	G
14	1.400	2303	G
15	1.500	2303	G
16	1.600	2303	G
17	1.700	1915	G
18	1.800	1818	G
19	1.900	1915	G
20	2.000	2109	G
21	2.100	1915	G
22	2.200	1721	G
23	2.300	1528	G
24	2.400	1721	G
25	2.500	1721	G
26	2.600	1624	G
27	2.700	2012	G
28	2.800	2303	G
29	2.900	1915	G
30	3.000	1624	G
31	3.100	2012	G
32	3.200	1818	G
33	3.300	1624	G
34	3.400	1818	G
35	3.500	2206	G
36	3.600	2012	G
37	3.700	1818	G
38	3.800	2303	G
39	3.900	2981	G
Average IRI Value		2069.13	

[Signature]
10/1/22
JC

[Signature]
10.01.2022
A-E

[Signature]
21/1/2022
Executive Engineer
R.W.D. (W) Division
Kathihar

Lab Job number :25

Date :09-01-2022

Name of Customer : Ashok Kumar

Name of Work/ Road : Sarsi-Kursela PWD Road to Gobindpur

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
9/1/22	13:59:27	25	0.1	280	0	2800	2787	G	25.60241	87.28320	Normal
9/1/22	13:59:27	25	0.1	220	20.2	2200	2206	G	25.60218	87.28222	Normal
9/1/22	13:59:27	25	0.1	240	30.3	2400	2400	G	25.60198	87.28125	Normal
9/1/22	14:0:2	25	0.1	200	30.3	2000	2012	G	25.60181	87.28027	Normal
9/1/22	14:0:2	25	0.1	210	20.2	2100	2109	G	25.60193	87.27931	Normal
9/1/22	14:0:38	25	0.1	200	30.3	2000	2012	G	25.60214	87.27800	Normal
9/1/22	14:0:38	25	0.1	210	40.4	2100	2109	G	25.60237	87.27736	Normal
9/1/22	14:0:38	25	0.1	180	40.4	1800	1818	G	25.60252	87.27636	Curve
9/1/22	14:1:0	25	0.1	170	40.4	1700	1721	G	25.60222	87.27544	Normal
9/1/22	14:1:13	25	0.1	210	30.3	2100	2109	G	25.60191	87.27444	Normal
9/1/22	14:1:13	25	0.1	210	30.3	2100	2109	G	25.60169	87.27357	Normal
9/1/22	14:1:48	25	0.1	220	20.2	2200	2206	G	25.60147	87.27247	Speed Breaker
9/1/22	14:2:0	25	0.1	380	20.2	3800	3756	G	25.60128	87.27158	Normal
9/1/22	14:2:0	25	0.1	230	30.3	2300	2303	G	25.60090	87.27067	Normal
9/1/22	14:2:0	25	0.1	230	30.3	2300	2303	G	25.60030	87.27007	Normal
9/1/22	14:2:24	25	0.1	230	40.4	2300	2303	G	25.60016	87.26901	Normal
9/1/22	14:2:24	25	0.1	190	30.3	1900	1915	G	25.60028	87.26800	Normal
9/1/22	14:2:24	25	0.1	180	40.4	1800	1818	G	25.60038	87.26704	Normal
9/1/22	14:2:24	25	0.1	190	30.3	1900	1915	G	25.60035	87.26608	Normal
9/1/22	14:2:24	25	0.1	210	40.4	2100	2109	G	25.60023	87.26505	Culvert
9/1/22	14:3:0	25	0.1	190	40.4	1900	1915	G	25.60024	87.26411	Normal
9/1/22	14:3:0	25	0.1	170	40.4	1700	1721	G	25.60028	87.26310	Normal
9/1/22	14:3:0	25	0.1	150	40.4	1500	1528	G	25.60016	87.26205	Normal
9/1/22	14:3:0	25	0.1	170	40.4	1700	1721	G	25.59997	87.26118	Normal
9/1/22	14:3:34	25	0.1	170	40.4	1700	1721	G	25.59980	87.26015	Normal
9/1/22	14:3:34	25	0.1	160	50.5	1600	1624	G	25.59970	87.25911	Normal
9/1/22	14:3:34	25	0.1	200	40.4	2000	2012	G	25.59951	87.25818	Normal
9/1/22	14:4:0	25	0.1	230	30.3	2300	2303	G	25.59921	87.25722	Curve
9/1/22	14:4:9	25	0.1	190	30.3	1900	1915	G	25.59932	87.25623	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 3000$$

$$Y = 2981$$

(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

Signature
 Executive Engineer
 R.W.D. (W) Division
 Kathar

Signature
 10.01.2022
 P.E

Signature
 10/1/22
 P.E

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
9/1/22	14:4:9	25	0.1	160	40.4	1600	1624	G	25.59952	87.25525	Normal
9/1/22	14:4:9	25	0.1	200	40.4	2000	2012	G	25.59964	87.25429	Normal
9/1/22	14:4:9	25	0.1	180	40.4	1800	1818	G	25.59971	87.25327	Normal
9/1/22	14:4:45	25	0.1	160	50.5	1600	1624	G	25.59964	87.25224	Normal
9/1/22	14:4:45	25	0.1	180	40.4	1800	1818	G	25.59958	87.25128	Normal
9/1/22	14:5:0	25	0.1	220	40.4	2200	2206	G	25.59954	87.25032	Normal
9/1/22	14:5:0	25	0.1	200	40.4	2000	2012	G	25.59930	87.24931	Normal
9/1/22	14:5:20	25	0.1	180	40.4	1800	1818	G	25.59877	87.24852	Normal
9/1/22	14:5:20	25	0.1	230	20.2	2300	2303	G	25.59810	87.24776	Normal
9/1/22	14:5:20	25	0.04	120	60.6	3000	2981	G	25.59804	87.24773	Normal


10.01.2022
A.E.

Wdell
10/1/22
pe

Pranav
Executive Engineer
R.W.D. (W) Division
Kathihar

File : C:\RAM KUMAR\MISC Files\Bump integrator\Falka\PWD Road To Govindpur\09011405.X1s. Section No. 25.

Name of Customer : Askok Kumar, Name of Work/ Road : Sarsi-Kursela PWD Road to Gobindpur, Lab Job number

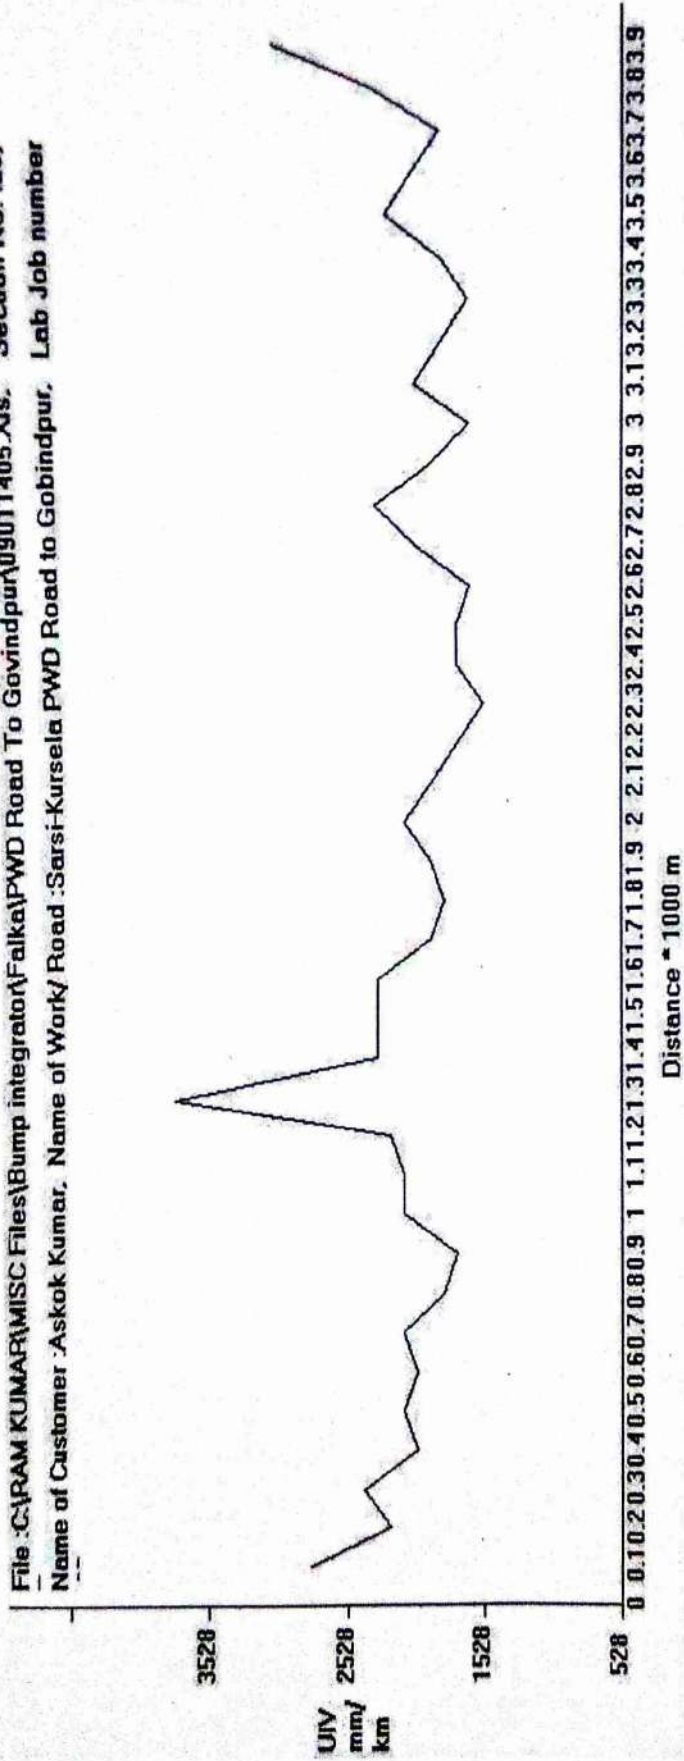

Handwritten signature
10/1/22
A-E

Handwritten signature
10.01.2022
A-E

Handwritten signature
Executive Engineer
R.W.D. (W) Division
Kathihar
