
RURAL WORKS DEPARTMENT



GOVERNMENT OF BIHAR

NAME OF ROAD:-

RESTORATION OF ROAD FROM JAGIR HALHALIYA TO MUSHAHARI TOLA

DIVISION:-

R.W.D, WORKS DIVISION, FORBESGANJ

CIRCLE:-

R.W.D, WORK CIRCLE, KISHANGANJ

BLOCK:-

FORBESGANJ

ESTIMATED COST

1245326.00

Inspection Report for Flood Damage Work

1.Name of PIUs

: EE RWD forbesgaij

2. Name Of Block / Road

Forbesgay

A. For Road

1.Damage Location / Chainage

26.22594, 87.3438

2.Damage Length

: 155 m

3. Nature Of Damage

Flood damage deft ups.om

4. Details Of Restoration

i) Material Being Used In Restoration

Local sand, Brick bat, Bebay, bemons pill.

ii) Equipment / Tools Being Used In Restoration Works

: Practor, Illy rollar

iii) Procedure Taken Up In Restoration Works

: Filly all out Properly in damage are

iv) Restored Length

ISSM

B. For Bridge

1.Damage Location / Chainage

2.Damage Length

3. Nature Of Damage

4. Details Of Restoration

i) Material Being Used In Restoration

ii) Equipment / Tools Being Used in Restoration Works

iii) Procedure Taken Up In Restoration Works

iv) Restored Length

N/A

A Toliver

Signatu

(Name Of Inspector)

Signature of JE / AE / EE

प्रतिवेदन

प्रस्तुत प्राक्कलन ग्रामीण कार्य विभाग, कार्य प्रमंडल, फारबिसगंज अंतर्गत

<u>भाटिक्स ग्रंथ</u>

प्रखंड के पथ हिल्हानीच। जाजी के मुसरी होला

जो विभागीय Online Monitoring System MIS पर अपलोड

है के बाढ़ 2021 से क्षतिग्रस्त हो जाने के कारण यातायात लायक Motorable हेतु बनाया गया है। इस कार्य को कराने का निर्देश ग्रामीण कार्य विभाग, विहार सरकार के पत्रांक—मु030—4(मु0) विविध कार्य—23—60/2020—1937/पटना, दिनांक—07.07.2021 से प्राप्त है। इस पत्र के Real time geo-tagged Photograph को कार्य के दौरान अपलोड करते हुए (Motorable) कार्य कराना सुनिश्चित करने का निर्देश प्राप्त है।

उक्त निर्देश के आलोक में... पूर्मार्ग........ नदी / नदी उपधार एवं अतिवृष्टि से आए बाढ़ के कारण इस पथ के Road Way के क्षतिग्रस्त हो जाने से सुरक्षित आवागमन हेतु Motorable कार्य कराया गया है। नेपाल तराई से निकलने वाली इस नदी के तेज धार एवं अतिवृष्टि से इस पथ में कटाव की स्थिति बनी। Motorable कार्य में आवश्यकता अनुसार Bamboo Pilling/Pitching of E.C Bags filled with local sand/ Local Sand Filling/ Brick bats का इस्तेमाल किया गया है। Motorable कार्य कराकर यातायात बहाल कर दिया गया है। निर्देशानुसार कराये गये Geo-tagged Photograph real time के साथ MIS पर अपलोड है। MIS की छायाप्रति, अपलोडेड फोटोग्राफ की छायाप्रति दर विश्लेषण एवं विभागीय आदेशों की छायाप्रति प्राक्कलन में संलग्न की जा रही है। प्राक्कलन में प्रयुक्त दर अद्धतन है।

प्राक्कलन की यथा शीध्र अनुमोदन अपेक्षित है ताकि अग्रेतर कार्रवाई की जा सके।

den

कनीय अभियंता ग्रामीण कार्य विभाग कार्य प्रशाखा— सहायक अभियंता ग्रामीण कार्य विभाग कार्य अवर प्रमंडल–

कार्यपालक अभियंता ग्रामीण कार्य विभाग कार्य प्रमंडल,फारबिसगंज

Abstract of Cost

Name of Work:- Estimate for Repairing/Restoration/ Making Motorable Roads
Damaged during Flood in JULY 2021 in ARARIA District

Name of Roads: Halhaliya Jagir To Mushahari Tola

BLOCK:- FORBESGANG

DISTRICT:-ARARIA

Divison:- RWD, Works Division, FORBESGANJ

Circle:-RWD, Works Circle, Kishanganj

Cost of RESTORATION

Rs.

1245326,00

TOTAL COST OF RESTORATION Rs.

1245326.00

Say Rs

1245326.00

Ref. E.E. Letter No. 1561 20031

13)9) A58 4 22 EE619

Technically Sanctioned For Rs. 12,45,326 20

(Rupees Twelve Lac Footy five Howard

2011/1/22

AE, circle

perintending Engil.

Jual Works Department

Juan Works Circle, Kis.

Nam	Name of Road:-					
	Restoration of Road From Rai	ilenus T	- 11			
SI.No	o.	iikpur i	o Mushahari To	ola Cutting-1		
	Items of Works	Unit	Quantity (m3	Rate (Rs.)	Amount (Rs.)	
1	2	3	4	5		
1.0	Filling of local sand obtained from river bed, watering & ramming, all complete job as per specification & direction of Engineer in-charge.		873.17	627.77	<u>6</u> 548,147.8	
2.0	Labour for cutting 62mm to 75mm dia bamboo piles to size and making shoes & driving by jet machine etc. all complete job as per specification & direction of Engineer in-Charge.	Mtr	930.00	75.86	70,549.80	
	Labour for fitting & fixing 62mm to 75mm dia bamboo runners in position at every vertical pile with 150 mm long nails or 38 swg G.I wire including cost of G.1 wire or nails etc all complete job as per specification & direction of Engineer-in-Charge.	Mtr	465.00	40.06	18,627.90	
		Sec.				
	Supplying of EC bag, filling of local sand, stitching and placing in position as per the direction of Engineer-in-charge.	Each	11266.96	37.35	420,820.82	
k	Supply and Carriage of brick bats upto 8 cm breach and placing in breaches and ying of bats, all complete job.	Cum	29.03	1851.91	53,751.69	
1.						
0 S	Supply, laying and Carriage of Hume pipe 000 mm dia (HPC), all complete job.	Mtr	0.00	5382.71	-	

Total Amount =

1,111,898.00

Add 12% GST =

133,428.00

SAY TOTAL AMOUNT =

1,245,326.00

13 (9/14 JE

JE RWD WORKS DIV. FORBESGANJ

RWD WORKS DIV FORBESGANJ E.E. RWD WORKS DIV. FORBESGANJ

हप्रहाप्त्रा लागरी खे. विशहरी द्यार



Ahm










Olm 1319171 28

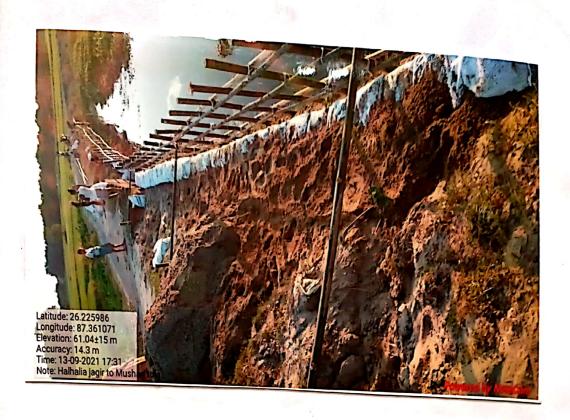



(M8/9/M













