


RURAL WORKS DEPARTMENT

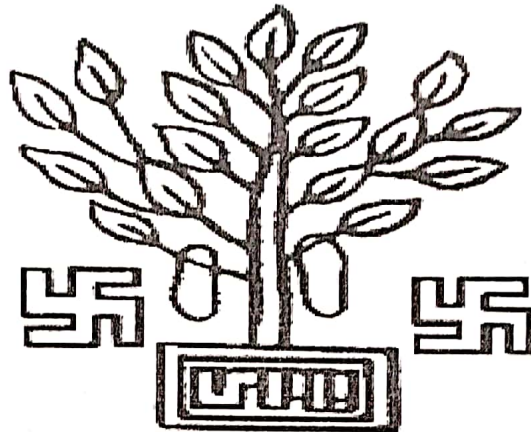

GOVERNMENT OF BIHAR

NAME OF ROAD:- RESTORATION OF ROAD FROM SIMRAHA RAILWAY
STATION TO KURWA LAXMIPUR

DIVISION:- R.W.D, WORKS DIVISION, FORBESGANJ

CIRCLE:- R.W.D, WORK CIRCLE, KISHANGANJ

BLOCK:- FORBESGANJ

ESTIMATED COST

303681.00

Inspection Report for Flood Damage Work

1. Name of PIUs

: E.E. RND, Forbesganj

2. Name Of Block / Road

: Forbesganj

A. For Road

1. Damage Location / Chainage

: 2G-196565887-29177

2. Damage Length

: 42.0 M

3. Nature Of Damage

: Flood Damage.

4. Details Of Restoration

:

i) Material Being Used In Restoration

: Sand, brick-bats, bamboo, E.C bags etc.

ii) Equipment / Tools Being Used In Restoration Works

:

iii) Procedure Taken Up In Restoration Works

: By using bamboo filling filly sand
E.C bags and brick-bats after completion.

iv) Restored Length

: 42.0 M.

B. For Bridge

1. Damage Location / Chainage

:

2. Damage Length

:

3. Nature Of Damage

:

4. Details Of Restoration

:

i) Material Being Used In Restoration

:

ii) Equipment / Tools Being Used in Restoration Works

:

iii) Procedure Taken Up In Restoration Works

:

iv) Restored Length

:

N/A

"S"

Signature of JE / AE / EE
15/8/21 15/8/21 C 26/9

Signature
(Name Of Inspector)

प्रतिवेदन

प्रस्तुत प्राक्कलन ग्रामीण कार्य विभाग, कार्य प्रमंडल, फारबिसगंज अंतर्गत

फारबिसगंज प्रखंड के पथ सिमराहा रेलवे स्टेशन से करवा

अस्सीपुर जो विभागीय Online Monitoring System MIS पर अपलोड है के बाद 2021 से क्षतिग्रस्त हो जाने के कारण यातायात लायक Motorable हेतु बनाया गया है। इस कार्य को कराने का निर्देश ग्रामीण कार्य विभाग, विहार सरकार के पत्रांक-मु0अ0-4(मु0) विविध कार्य-23-60/2020-1937/पटना, दिनांक-07.07.2021 से प्राप्त है। इस पत्र के Real time geo-tagged Photograph को कार्य के दौरान अपलोड करते हुए (Motorable) कार्य कराना सुनिश्चित करने का निर्देश प्राप्त है।

उक्त निर्देश के आलोक में सिमराहा नदी/नदी उपधार एवं अतिवृष्टि से आए बाढ़ के कारण इस पथ के Road Way के क्षतिग्रस्त हो जाने से सुरक्षित आवागमन हेतु Motorable कार्य कराया गया है। नेपाल तराई से निकलने वाली इस नदी के तेज धार एवं अतिवृष्टि से इस पथ में कटाव की स्थिति बनी। Motorable कार्य में आवश्यकता अनुसार Bamboo Pilling/Pitching of E.C Bags filled with local sand/ Local Sand Filling/ Brick bats का इस्तेमाल किया गया है। Motorable कार्य कराकर यातायात बहाल कर दिया गया है। निर्देशानुसार कराये गये Geo-tagged Photograph real time के साथ MIS पर अपलोड है। MIS की छायाप्रति, अपलोडेड फोटोग्राफ की छायाप्रति दर विश्लेषण एवं विभागीय आदेशों की छायाप्रति प्राक्कलन में संलग्न की जा रही है। प्राक्कलन में प्रयुक्त दर अद्धतन है।

प्राक्कलन की यथा शीघ्र अनुमोदन अपेक्षित है ताकि अग्रेतर कार्रवाई की जा सके।

15/8/21
कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा-

15/8/21
सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल-

15/8/21
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, फारबिसगंज

Abstract of Cost

Name of Work:- Estimate for Repairing/Restoration/ Making Motorable Roads
Damaged during Flood In JULY 2021 In ARARIA District

Name of Roads: Restoration of Road From Simraha Railway
Station To Kurwa Laxmipur

BLOCK:- FORBESGANG

DISTRICT:-ARARIA

Division:- RWD, Works Division, FORBESGANJ

Circle:-RWD, Works Circle, Kishanganj

Cost of RESTORATION

Rs.

303681.00

TOTAL COST OF RESTORATION Rs.

303681.00

Say Rs.

303681.00

15/8/21
J.E.

15/8/21
A.E.

26/9
E.E.

Ref. E.E. Letter No...1561 (2030) Dt...28/4/22

Technically Sanctioned For Rs...3,03,681.00

(Rupees) three lac three thousand

Six hundred eighty one only

11/4/22
A.E. circle

28/4/22

Superintending Engineer
Rural Works Department
Works Circle, Kishanganj

Detailed Estimate					
Name of Roads: Restoration of Road From Simraha Railway Station To Kurwa Laxmipur					
Sl.No.	Items of Works	Unit	Quantity (m3)	Rate (Rs.)	Amount (Rs.)
1	2	3	4	5	6
1.0	Filling of local sand obtained from river bed, watering & ramming, all complete job as per specification & direction of Engineer-in-charge.	Cum	221.76	627.77	139,214.28
2.0	Labour for cutting 62mm to 75mm dia bamboo piles to size and making shoes & driving by jet machine etc. all complete job as per specification & direction of Engineer-in-Charge.	Mtr	252.00	75.86	19,116.72
3.0	Labour for fitting & fixing 62mm to 75mm dia bamboo runners in position at every vertical pile with 150 mm long nails or 38 swg G.I wire including cost of G.I wire or nails etc all complete job as per specification & direction of Engineer-in-Charge.	Mtr	126.00	40.06	5,047.56
4.0	Supplying of EC bag, filling of local sand, stitching and placing in position as per the direction of Engineer-in-charge.	Each	2323.02	37.35	86,764.82
5.0	Supply and Carriage of brick bats upto 8 km breach and placing in breaches and lying of bats, all complete job.	Cum	11.34	1851.91	21,000.66
6.0	Supply, laying and Carriage of Hume pipe 1000 mm dia (HPC), all complete job.	Mtr	0.00	5382.71	-

Total Amount = 271,144.00

Add 12% GST = 32,537.00

SAY TOTAL AMOUNT = 303,681.00

Alam
15/8/21
JE
RWD WORKS
DIV.
FORBESGANJ

(15/8/21)
AE
RWD WORKS
DIV.
FORBESGANJ

C
26/9
E.E.
RWD WORKS
DIV.
FORBESGANJ

सीमलखड़ा रेलवे कृमारी से कुरवा लखमपुर



कुरवा लखमपुर
AC

ਸੀਮਰਾਈ ਰੇਲਵੇ ਸਟੇਸ਼ਨ ਦੇ ਕੁਰਵਾ ਲਾਖਮਪੁਰ



15/9/21
 06



15/11/21
PC



Am
18/9/21
A2
