

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, त्रिवेणीगंज।

पत्रांक 381/5150 / त्रिवेणीगंज,
प्रेषक,

दिनांक 2-3-23..... /

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, त्रिवेणीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह- सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- MR-3054 (New Maintenance Policy-2018) योजनान्तर्गत राशि विमुक्ति हेतु
अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maintenance Policy-2018) योजनान्तर्गत अधियाचना इस पत्र के साथ संलग्न विहित प्रपत्र में तैयार कर समर्पित की जा रही है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

विश्वासभाजन

12.3.23

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, त्रिवेणीगंज।

2/3/23

Rural Works Department

Requisition Form for Scheme Head - MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Division :- Triveniganj

S. No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lacs)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done PCC Works (in Lakh)	Remarks
					Length (in Km.)	Amount of (in Lacs)	Initial Rectification and Surface Renewal	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/2022-23-Triveniganj/07	PMGSY Road-Nirmali Goth to Bela Tola via Dhanuk Tola.	21005113005	Letter No- 2011 dated- 02.05.22	2.00	125.000000	100.73794	22.25791	13/MBD/MR-3054/2022-23 DTD-	21.05.2023	Ongoing	3197	25	5.01	0.00000	70.98265	70.98265	Ongoing
Total					2.000	125.000000	100.73794	22.25791							0.00000	70.98265	70.98265	

Executive Engineer
R.W.D. (W.D.) Triveniganj

2.3.2023

2.3.23

FORM GFR - 19 - A
(See Government of India's Decision (i) below Rule - 150)
Form of Utilization Certificate up to 02.03.2023

(Programming Fund)

Sl. N.	Name of Scheme	Sanction No. & Date with Amount (in Lac.)	Total Amount Received (in Lac.)	Particulars
1	2	3	4	5
1.	Construction of Rural Road under MR-3054 (Bihar Rural Road Maintenance Policy)	Total Allotment received vide Secretary-cum-Empowered Officer BRRDA, Additional CEO, Patna. Letter No-53 Dated-12.12.2022 Letter No-54 Dated-14.12.2022 Letter No-04 Dated-10.01.2023 Letter No-12 Dated-03.02.2023 Letter No-26 Dated-25.02.2023 Letter No-29 Dated-01.03.2023	Rs- 5687.44184	Total Allotment Rs.- 5687.44184 Lakh CFMS Expenditure Rs.-5254.11143 Lakh Balance Rs.- 433.33041 Lakh
		Total	5687.44184	
2.	Certified that I have satisfied myself that the condition on which the grants in aid sanctioned have been duly fulfilled / are being fulfilled and that I have Exercised the following Checks to see that the money was actually utilized for the purpose for which it was sanctioned . i) Works have been supervised by Executive Engineer / Superintending Engineer. ii) Periodical inspection has been conducted by A.E. / Executive Engineer / Superintending Engineer. iii) Construction materials have been tested. iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer. v) All other Codal formalities have been observed.			

Sr. D.A.O.

RWD, Works Division, Triveniganj

Executive Engineer

RWD, Works Division, Triveniganj

Test Date :	3 / 1 / 2022	Road Name :	To Bela Tola via Dhanuk Tola
Machine No :	418	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		UV Range :	1704 To 5000 1000 mm/km
Start Location :	Nirmali Goth	Dist Range :	0 To 21 0.1 1000 m
End Location :	Dhanuk Tola	Equation :	$Y = 0.4X^2 + 0.998X + 109.5$

Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\RWD\OneDrive\Desktop\GOTH.Xls. Section No. : 81. Eqn : $Y = 0.4X^2 + 0.998X + 109.5$
 Name of Customer : Sanjay Kumar, Name of Work : Road : PMGSY Road Nirmali Goth To Bela Tola via Dhanuk Tola.



Distance * 1000 m


0.1 0.2 0.3 0.4 0.5 0.6 0.7 0.8 0.9 1 1.1 1.2 1.3 1.4 1.5 1.6 1.7 1.8 1.9 2

Handwritten signature
 28/1/23

Handwritten signature
 12.3.23

Executive Engineer
Rural Works Department
Work Division, Tinsukia

File : C:\Users\PRWD\OneDrive\Desktop\GOTH.xls, Section No. : 81, Eqn : $Y = 0 \cdot X^2 + 0.998 \cdot X + 109.5$
 Name of Customer : Sanjay Kumar, Name of Work/ Road : PMGSY Road Nirmali Goth To Bela Tola via Dhanuk Tola.

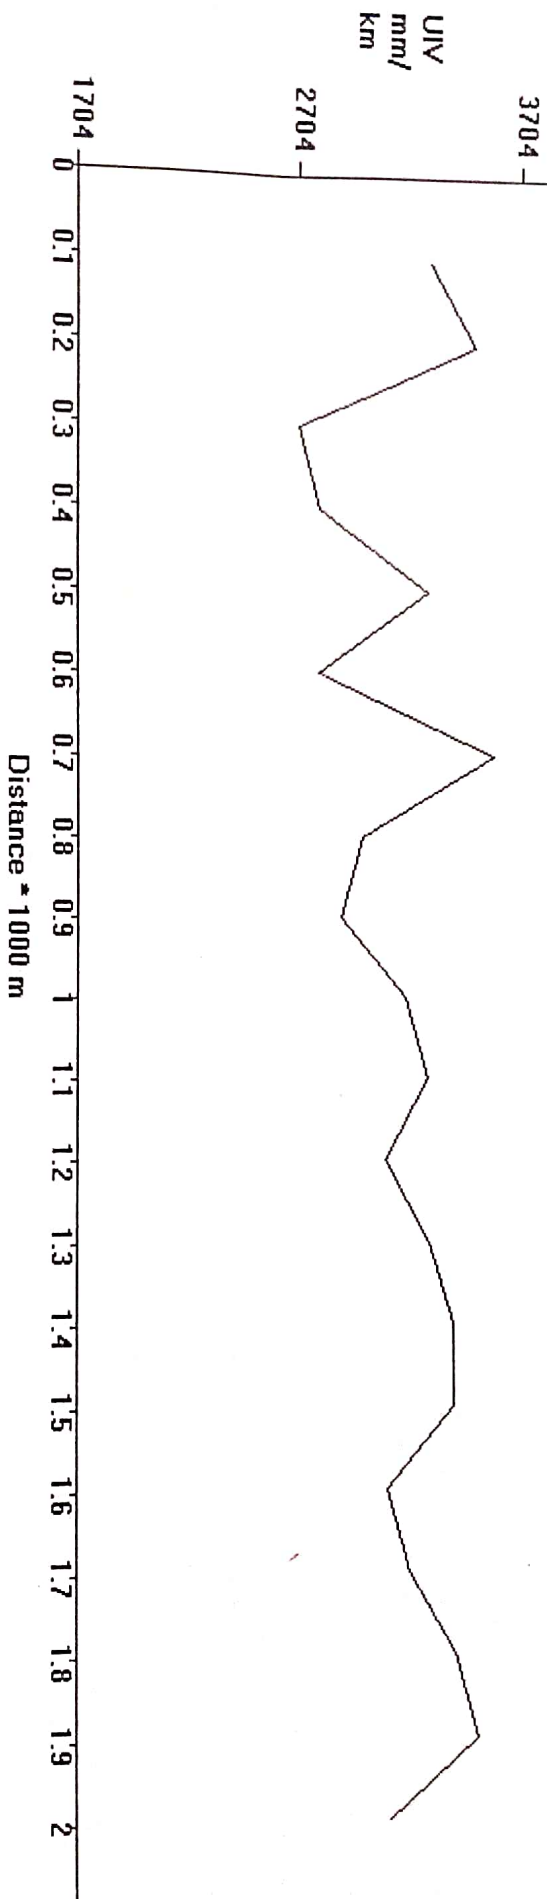

Sanjay Kumar

**Executive Engineer,
 Rural Works Department,
 PWD Station, Tirunelveli.**

Sanjay Kumar

NAME OF ROAD :-PMGSY Road Nirmali Goth To Bela Tola via Dhanuk Tola

LENGTH:-2.00 K.M

NAME OF CONTRACTOR:- Sanjay Kumar

AGREEMENT NO. :-13MBD./MR-3054/22-23

PROJECT ID:-21005113005

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 * X^2 + 0.998 * X + 109.5$		
1/3/2023	2: 27: 49	81	0.1	320	10.1	3200	3303	G	26.13539	86.68204	Normal	X = 3000		
1/3/2023	2: 29: 0	81	0.1	340	20.2	3400	3502	G	26.135662	86.681813	Curve	Y = 3103		
1/3/2023	2: 29: 35	81	0.1	260	20.2	2600	2704	G	26.135311	86.681457	Curve			
1/3/2023	2: 30: 46	81	0.1	270	10.1	2700	2804	G	26.135217	86.680911	Normal			
1/3/2023	2: 31: 17	81	0.1	320	20.2	3200	3303	G	26.13538	86.679941	Normal	RURAL ROAD		
1/3/2023	2: 31: 52	81	0.1	270	10.1	2700	2804	G	26.135698	86.67876	Culvert	Good	Average	Poor
1/3/2023	2: 32: 19	81	0.1	350	10.1	3500	3602	G	26.136317	86.676381	Curve	<4000	4001-5000	>5001
1/3/2023	2: 32: 19	81	0.1	290	10.1	2900	3003	G	26.135762	86.675948	Normal			
1/3/2023	2: 33: 0	81	0.1	280	10.1	2800	2903	G	26.134592	86.675561	Curve			
1/3/2023	2: 33: 32	81	0.1	310	10.1	3100	3203	G	26.13429	86.676034	Curve			
1/3/2023	2: 34: 7	81	0.1	320	10.1	3200	3303	G	26.133792	86.675909	Culvert			
1/3/2023	2: 34: 43	81	0.1	300	10.1	3000	3103	G	26.133124	86.675662	Normal			
1/3/2023	2: 34: 43	81	0.1	320	20.2	3200	3303	G	26.132395	86.675306	Normal			
1/3/2023	2: 35: 18	81	0.1	330	10.1	3300	3402	G	26.132253	86.674817	Normal			
1/3/2023	2: 37: 47	81	0.1	330	20.2	3300	3402	G	26.132433	86.67347	bridge			
1/3/2023	2: 38: 25	81	0.1	300	10.1	3000	3103	G	26.132962	86.671446	Normal			
1/3/2023	2: 39: 1	81	0.1	310	10.1	3100	3203	G	26.133156	86.670483	Curve			
1/3/2023	2: 39: 36	81	0.1	330	10.1	3300	3402	G	26.132981	86.670185	Curve			
1/3/2023	2: 39: 36	81	0.1	340	10.1	3400	3502	G	26.133122	86.669405	Normal			
1/3/2023	2: 40: 11	81	0.1	300	20.2	3000	3103	G	26.133223	86.668764	Normal			
							63957							

Sanjay Kumar
24/3/23

12.3.23
Executive Engineer
Road Works Department
Vidya Sadan, Thiruvananthapuram

Lab Job number :81

Date :3/1/2023

Name of Customer :Sanjay Kumar

Name of Work/ Road :PMGSY Road Nirmali Goth To Bela Tola via Dhanuk Tola

Sr.no Location o Corrected U.I Road catagory
test(in km) value(mm/km)

2	0.1	3303 G
3	0.2	3502 G
4	0.3	2704 G
5	0.4	2804 G
6	0.5	3303 G
7	0.6	2804 G
8	0.7	3602 G
9	0.8	3003 G
10	0.9	2903 G
11	1	3203 G
12	1.1	3303 G
13	1.2	3103 G
14	1.3	3303 G
15	1.4	3402 G
16	1.5	3402 G
17	1.6	3103 G
18	1.7	3203 G
19	1.8	3402 G
20	1.9	3502 G
21	2	3103 G

Puc
2/3/23
re

2.3.23
Executive Engineer
Rural Works Department
Work Station, Trivandrum

pedras
cristal

Recd
1/13/13
N



Executive Engineer
Barrage Works Department
Vijay Nagar, Tirunelveli

12.3.27
