

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक1394..... /

बारसोई, दिनांक.....15-07-2024..... /

प्रेषक:-

ई० विश्वबंधु राजीव रंजन
कार्यपालक अभियंता

सेवा में,

अपर मुख्य कार्यपालक पदाधिकार-सह-सचिव,
ग्रामीण कार्य विभाग, ब्राडा बिहार, पटना।

विषय : शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:- भवदीय का पत्रांक 4843 दिनांक 06.12.2021

महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त।

विश्वास भाजन



कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमंडल, बारसोई, कटिहार

15.7.24

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक /

बारसोई, दिनांक..... /

प्रेषक:-

ई० विश्वबंधु राजीव रंजन
कार्यपालक अभियंता

सेवा में,

अपर मुख्य कार्यपालक पदाधिकार-सह-सचिव,
ग्रामीण कार्य विभाग, ब्राडा बिहार, पटना।

विषय : शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:- भवदीय का पत्रांक 4843 दिनांक 06.12.2021

महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त।

विश्वास भाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार

ज्ञापांक 1394 दिनांक 15-07-2024

प्रतिलिपि - नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार
15.7.24

Rural Works Department, Works Division, Barsoi, Katihar.
MIR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)

Name of Division :- Barsoi (Katihar)

Sl. No.	Package No.	Name Of Road	Project ID as per MIS	Administrative Approval (AA) Letter No / Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No	Date	Date of Completion as per Agreement	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allocated Amount (In Lkh)	up-to-date expenditure as per MIS (In Lakh)	Total Value of Measurement (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length of (in Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
1	MR-N/22-23 BARSOI /5	Abadpur Halka Kachari Se Kubei Para Jarmuniya Sohar Tak	21105612001	992 / 10.08.2022	4.000	286.64500	195.19135	47.21689	06/MBD/2023-24		Completed	2666.20	25mm	5.1%	0.000	0.000	186.40685	186.40685	
		L022-Karanpur to Chechors (VR22)	NEA22000890		2.952	206.83200	135.43222	38.40028				2651.17	25mm	5.1%	0.000	0.000	131.49138	131.49138	
				Total :-	6.952	493.47700	330.62357	85.61717							0.000	0.000	317.89823	317.89823	

(Signature)
Executive Engineer
R.W.D. Works Division
Barsoi, Katihar
15-8

FROM GFR 19 - A

(See Government of India's Decision (I) Below Rule - 150)

Form of Utilisation Certificate

Sl. No.	Name of Scheme	Sanctioned No Date with Amount (in Lakh Rs.)	Amount Received (in Lakh Rs.)	Particulars
1	2	4	5	6
1	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year-2021-22, 2022-23 & 2023-24)	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year- 2021-22, 2022-23 & 2023-24) Lt. No. 32 Dt- 28.05.2021 Lt. No. 40 Dt- 14.06.2021 Lt. No. 05 Dt- 25.01.2022 Lt. No. 10 Dt- 21.02.2022 Lt. No. 49 Dt- 27.04.2022 Lt. No. 22 Dt- 08.08.2022 Lt. No. 12 Dt- 03.02.2023 Lt. No. 35 Dt- 14.03.2023 Lt. No. 42 Dt- 20.03.2023 Lt. No. 72 Dt- 10.05.2023 Lt. No. 78 Dt- 24.05.2023 Lt. No. 84 Dt- 08.06.2023 Lt. No. 96 Dt- 07.07.2023 Lt. No. 106 Dt- 02.08.2023 Lt. No. 113 Dt- 14.08.2023 Lt. No. 136 Dt- 10.10.2023 Lt. No. 140 Dt- 16.10.2023 Lt. No. 144 Dt- 20.10.2023 Lt. No. 152 Dt- 16.11.2023 Lt. No. 14 Dt- 06.02.2024 Lt. No. 31 Dt- 09.03.2024 Lt. No. 37 Dt- 15.03.2024 Lt. No. 40 Dt- 18.03.2024 Lt. No. 47 Dt- 25.03.2024 Lt. No. 72 Dt- 29.05.2024 Lt. No. 74 Dt- 03.06.2024	4344.31204	Certified that out of Rs.- 4344.31204 Lakh of grants in aid sanctioned during the Years 2021-22, 2022-23 & 2023-24 In Favour of Executive Engineer, Rural Works Department, Works Division, Barsoi sum of Rs.- 4190.06724 Lakh has been utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.- 154.24480 Lakh remaining unutilized at the end of the period under report.purpose.
	Total -		4344.31204	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose fo


Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test checks conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD. Works.

[Signature]
15/07/24
Executive Engineer
Rural Works Department
Works Division, Barsoi, Katihar

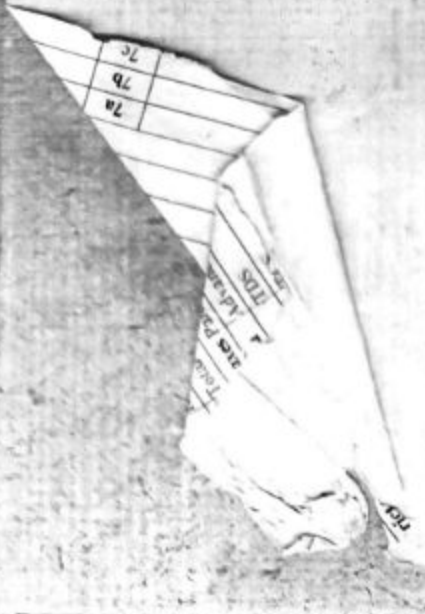

Handwritten text: *Handwritten signature/initials*
Handwritten text: *Handwritten signature/initials*

(Abadpur Halka Kachari Se Kybey Para
Jamunaya sohar Tak.
Schedule XLV-Form No. 134

Executive Engineer

Rural Works Department
Morang District, Bhaupur

MR-3054(N.M.P.)

DIVISION

Barsoi

SUB-DIVISION

Agg. → 06 MBN/2023-24

MEASUREMENT BOOK

No. - 2051

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement			Contents of area
	No.	B.	D.	
1st and final bill				
Name of work:	Abaalpara Taluka			
Kachari Se Kuber Para Jammija				
Sohar Tak				
Name of Agency:-	Pankaj Kumar Singh			
Const. Company Pvt Ltd				
Agreement No.:-	06 MBB/2023-24			
Date of start:-	10-5-2023			
Date of completion:-	09-2-24			

Date of measurement:- 06.06.2023

1. P/v & Firing logo of
20 Project - - - etc -
03 Nos

2. clearing & grubbing of
I Road land.

$$2 \times 133 \times 30.0M \times 1.0M = 7980M^2$$

$$2 \times 10.0M \times 1.0M = 20M^2$$

$$8000M^2$$

$$= .80 Hae$$

3. Ripmantling of Cement concrete

2. Pavement Continuation

$$20 \times 30.0M \times 3.050M \text{ or } 100m \times 183.00M^2$$

1st bill
06.06.23
JE

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
35. P/V MSS type-B mattr					
2934.13 m ³ vide TMB P-28					
@ 275.14/m ²					R. 807297.00
					R. 18596752.00
Add. S.F. vide TMB P-38					R. 210091.00
Add. GST. - 18%					R. 3347415.00
Add. L.C. - 1%					R. 185968.00
					R. 2,23,40,226.00
Less 16.56% below					R. 3639541.00
					R. 1,86,40,685.00
<i>[Signature]</i> 30.05.2024 JE					
<i>[Signature]</i> 30/5/24 JE					

The work has been completed
as per specification and
Measurement.

[Signature]
30.05.24
JE

[Signature]
30/5/24
JE

Attested
[Signature]
Executive Engineer
Rural Works Department
P Works Division, Barsol
15.2.24

Lab Job number :71

Date :15-05-2024

Name of Customer :Pankaj Kumar Singh Const. Co. Pvt. Ltd.

Name of Work/ Road :Abadpur Halka Kachari Se Kubey Para Jamuniya Sohar Tak

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2981	G
2	0.200	3175	G
3	0.300	3078	G
4	0.400	2981	G
5	0.500	3175	G
6	0.600	3078	G
7	0.700	2109	G
8	0.800	2303	G
9	0.900	3078	G
10	1.000	2981	G
11	1.100	3175	G
12	1.200	3078	G
13	1.300	3369	G
14	1.400	2884	G
15	1.500	2981	G
16	1.600	2981	G
17	1.700	2884	G
18	1.800	3078	G
19	1.900	2206	G
20	2.000	2109	G
21	2.100	2206	G
22	2.200	2012	G
23	2.300	2206	G
24	2.400	2497	G
25	2.500	2981	G
26	2.600	2593	G
27	2.700	2400	G
28	2.800	2012	G
29	2.900	2303	G
30	3.000	-2593	G
31	3.100	2497	G
32	3.200	2109	G
33	3.300	3175	G
34	3.400	2981	G
35	3.500	2884	G
36	3.600	2109	G
37	3.700	2497	G
38	3.800	2303	G
39	3.900	2400	G
40	4.000	2206	G
Average IRI Value		2666.20	

Sp. lit.
30.05.2024
202

20/05/24
20

75107129
Executive Engineer
Rural Works Department
Works Division, Barsoi

Lab Job number :71

Date :15-05-2024

Name of Customer :Pankaj Kumar Singh Const. Co. Pvt. Ltd.
Name of Work/ Road :Abadpur Halka Kachari Se Kubey Para Jamunliya Sohar Tak

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
15/5/24	9:8:9	71	0.1	300	0	3000	2981	ROAD	25.53121	87.99218	Normal
15/5/24	9:8:45	71	0.1	320	10.1	3200	3175	G	25.53073	87.99309	Normal
15/5/24	9:9:14	71	0.1	310	20.2	3100	3078	G	25.53031	87.99391	Normal
15/5/24	9:9:32	71	0.1	300	20.2	3000	2981	G	25.53003	87.99453	Normal
15/5/24	9:9:55	71	0.1	320	30.3	3200	3175	G	25.52943	87.99544	Curve
15/5/24	9:10:19	71	0.1	310	30.3	3100	3078	G	25.52867	87.99572	Normal
15/5/24	9:10:49	71	0.1	210	30.3	2100	2109	G	25.52776	87.99613	Normal
15/5/24	9:11:22	71	0.1	230	20.2	2300	2303	G	25.52735	87.99690	Curve
15/5/24	9:11:56	71	0.1	310	10.1	3100	3078	G	25.52738	87.99783	Normal
15/5/24	9:12:17	71	0.1	300	10.1	3000	2981	G	25.52729	87.99856	Normal
15/5/24	9:12:46	71	0.1	320	10.1	3200	3175	G	25.52749	87.99956	Normal
15/5/24	9:13:15	71	0.1	310	20.2	3100	3078	G	25.52773	88.00051	Curve
15/5/24	9:13:40	71	0.1	340	10.1	3400	3369	G	25.52835	88.00096	Normal
15/5/24	9:13:59	71	0.1	290	20.2	2900	2884	G	25.52829	88.00195	Normal
15/5/24	9:14:31	71	0.1	300	20.2	3000	2981	G	25.52829	88.00292	Normal
15/5/24	9:14:54	71	0.1	300	10.1	3000	2981	G	25.52832	88.00396	Normal
15/5/24	9:15:26	71	0.1	290	10.1	2900	2884	G	25.52838	88.00494	Normal
15/5/24	9:15:57	71	0.1	310	10.1	3100	3078	G	25.52823	88.00590	Normal
15/5/24	9:16:24	71	0.1	220	30.3	2200	2206	G	25.52818	88.00668	Curve
15/5/24	9:16:55	71	0.1	210	30.3	2100	2109	G	25.52894	88.00699	Normal
15/5/24	9:17:19	71	0.1	220	30.3	2200	2206	G	25.52897	88.00799	Normal
15/5/24	9:17:46	71	0.1	200	40.4	2000	2012	G	25.52872	88.00900	Normal
15/5/24	9:18:14	71	0.1	220	40.4	2200	2206	G	25.52839	88.00992	Culvert
15/5/24	9:18:53	71	0.1	250	10.1	2500	2497	G	25.52801	88.01086	Normal
15/5/24	9:19:16	71	0.1	300	10.1	3000	2981	G	25.52762	88.01173	Normal
15/5/24	9:19:48	71	0.1	260	10.1	2600	2593	G	25.52733	88.01259	Normal
15/5/24	9:20:18	71	0.1	240	10.1	2400	2400	G	25.52662	88.01265	Curve
15/5/24	9:20:50	71	0.1	200	20.2	2000	2012	G	25.52584	88.01353	Normal
15/5/24	9:21:19	71	0.1	230	20.2	2300	2303	G	25.52543	88.01440	Normal
15/5/24	9:21:52	71	0.1	260	10.1	2600	2593	G	25.52545	88.01541	Normal
15/5/24	9:22:21	71	0.1	250	20.2	2500	2497	G	25.52558	88.01636	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2200$$

$$Y = 2206$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

30.05.2024
02

30/05/24

30/05/24
Executive Engineer
Rural Works Department
Works Division, Barsn

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
15/5/24	9:22:56	71	0.1	210	30.3	2100	2109	ROAD	25.52592	88.01718	Normal
15/5/24	9:23:26	71	0.1	320	10.1	3200	3175	G	25.52632	88.01819	Normal
15/5/24	9:23:59	71	0.1	300	20.2	3000	2981	G	25.52653	88.01913	Normal
15/5/24	9:24:23	71	0.1	290	20.2	2900	2884	G	25.52673	88.01986	Normal
15/5/24	9:24:53	71	0.1	210	30.3	2100	2109	G	25.52657	88.02082	Normal
15/5/24	9:25:27	71	0.1	250	20.2	2500	2497	G	25.52636	88.02156	Culvert
15/5/24	9:25:58	71	0.1	230	10.1	2300	2303	G	25.52595	88.02228	Normal
15/5/24	9:26:30	71	0.1	240	20.2	2400	2400	G	25.52561	88.02295	Normal
15/5/24	9:26:57	71	0.1	220	10.1	2200	2206	G	25.52514	88.02330	Normal

8.612
30.05.2024
202

20.05.2024
202

Dr. J. P. K. K. K.

Executive Engineer
Rural Works Department
Works Division, Barsoi

File : E:\Bump Integrator\Barsoi\Abadpur Halka Kachari Se Kubey Para Jamuniya Sohar Tak\15050930.Xls. Section

Name of Customer : Pankaj Kumar Singh Const. Co. Pvt. Ltd., Name of Work/ Road : Abadpur Halka Kachari Se



0 0.10.20.30.40.50.60.70.80.9 1 1.11.21.31.41.51.61.71.81.9 2 2.12.22.32.42.52.62.72.82.9 3 3.13.23.33.43.53.63.73.83.9 4

Distance * 1000 m

Handwritten signature and date: 20/08/2012

Handwritten signature and date: 23.05.2012

Handwritten signature and date: 20/08/2012
Executive Engineer
Rural Works Department
Works Division, Barsoi
