

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सोनपुर

Mob No :- 8986915436

E.Mail :- eerwdsonpur@gmail.com

पत्रांक 791/अ/सु
प्रेषक,

सोनपुर, दिनांक 17/4/23

ई0 प्रियंका कुमारी
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर।

सेवा में,

नोडल पदाधिकारी (3054),
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना में
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक ग्रामीण कार्य विभाग कार्य प्रमंडल सोनपुर के अंतर्गत बिहार
ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना के क्रियान्वयन हेतु आवंटन की
मांग विहित प्रपत्र में तैयार कर भेजी जा रही है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की
जाये।

अनु0:-उपयोगिता प्रमाण-पत्र।

विश्वासभाजन

Prigaula
17/4/23

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर
17/4/23

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **April-2025**

PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18		10548.81267	Certified that out of Rs 10548.81267 lakh received during the years 2020-21 to 2024-25 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 10548.81267 Lakh has been utilized for the purpose of New Maintenance Policy-18 Scheme as given in the margin for which it was sanctioned and that the balance of Rs NIL Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

P. S. K. K. K.
17/4/25
EXECUTIVE ENGINEER
R.W.D. Works Division Sonapur.
mm
17/4/25

Requisition Formate for Scheme Head - MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and surface Renewal)

Division Name:- Rural Works Department, Works Division- Sonpur

Sl.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lac)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content In %	Previous Total Allocated Amount (In Lac)	Upto date expenditure as per MIS (In Lac)	Requisition against Work Done (In Lac)	Remarks
					Length (In Km.)	Amount (In Lac)	Initial Rectification on Surface Renewal (In Lac)	5 Years Routine Maintenance (In Lac)										
1		Kaparfara darihara R.E.O. road to mathchilawe	31306201008	6153 03.12.23	2.600	126.660	68.56636	17.39474	15/MBD/2024-25 05.11.2024	29.05.2025	-	2874	25	5.02	21.90297	21.90297	16.17384	
2		L043-T03 Road To Magar Pal (VR21)	31306402124	6115 04.12.23	0.740	34.633	17.62470	6.15379	15/MBD/2024-25 05.11.2024	29.05.2025	25.02.25	3036	25	5.02	10.12504	10.12504	7.39645	
3		Sonepur Rewaghat road - Kusiyalpur	NEA220001801	6115 04.12.23	0.700	28.430	14.98218	4.32206	15/MBD/2024-25 05.11.2024	29.05.2025	19.02.25	2665	25	5.03	8.64048	8.64048	6.31196	
Total																	29.88225	

April
D.A. 20-1
R.W.D. Works Division Sonpur

Rajendra Kumar
12/4/23
Executive Engineer
R.W.D Works Div- Sonpur

... darihara R.E.O. road to mathchilawe

Contractor- Lalan Kumar

$$Y = 0 * X^2 + 1.000 * X + 415.2$$

$$X = 3150$$

$$Y = 3020$$

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5000

Contractor- Lalan Kumar											
Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
		No.						ROAD			
18/2/25	16:11:0	24	0.1	260	0	2600	2704	G	25.804725	85.084944	Normal
18/2/25	16:11:23	24	0.1	280	10.1	2800	2920	G	25.804497	85.084955	Normal
18/2/25	16:11:41	24	0.1	310	10.1	3100	3150	G	25.802736	85.084157	Normal
18/2/25	16:12:0	24	0.1	290	20.2	2900	2970	G	25.801994	85.083791	Curve
18/2/25	16:12:32	24	0.1	290	10.1	2900	2970	G	25.801502	85.084084	Normal
18/2/25	16:13:8	24	0.1	280	10.1	2800	2920	G	25.800718	85.084886	Normal
18/2/25	16:13:18	24	0.1	310	20.2	3100	3150	G	25.800177	85.085248	Curve
18/2/25	16:13:39	24	0.1	300	10.1	3000	3120	G	25.799479	85.085917	Normal
18/2/25	16:14:8	24	0.1	250	10.1	2500	2580	G	25.798509	85.086519	Curve
18/2/25	16:14:23	24	0.1	310	20.2	3100	3150	G	25.798139	85.08662	Normal
18/2/25	16:14:41	24	0.1	260	20.2	2600	2704	G	25.796923	85.086864	Normal
18/2/25	16:15:4	24	0.1	270	10.1	2700	2760	G	25.79613	85.086968	Normal
18/2/25	16:15:21	24	0.1	290	20.2	2900	2970	G	25.795791	85.087146	Curve
18/2/25	16:15:37	24	0.1	260	10.1	2600	2704	G	25.795263	85.087432	Normal
18/2/25	16:16:3	24	0.1	270	20.2	2700	2760	G	25.794699	85.087594	Normal
18/2/25	16:16:21	24	0.1	250	20.2	2500	2580	G	25.793359	85.088435	Speed Breaker
18/2/25	16:16:46	24	0.1	260	10.1	2600	2704	G	25.793407	85.088538	Normal
18/2/25	16:17:4	24	0.1	280	10.1	2800	2920	G	25.79197	85.089856	Normal

2874

 $\|R\| =$

19/03/15
with info
aff

8/2/04
EJ
C. J. [Signature]

19.3.21


Pigou's Law
19/3/25

Executive Engineer

W.D. Works Div. Sonapur

File : C:\Users\DELL\Desktop\18021560.Xls, Section No. : 24, Eqn : $Y = 0 * X^2 + 1.000 * X + 415.2$

Name of Customer : Lalan Kumar, Name of Work/ Road : Kapafora darihara R.E.O. road to mathchilawe, Lab Job

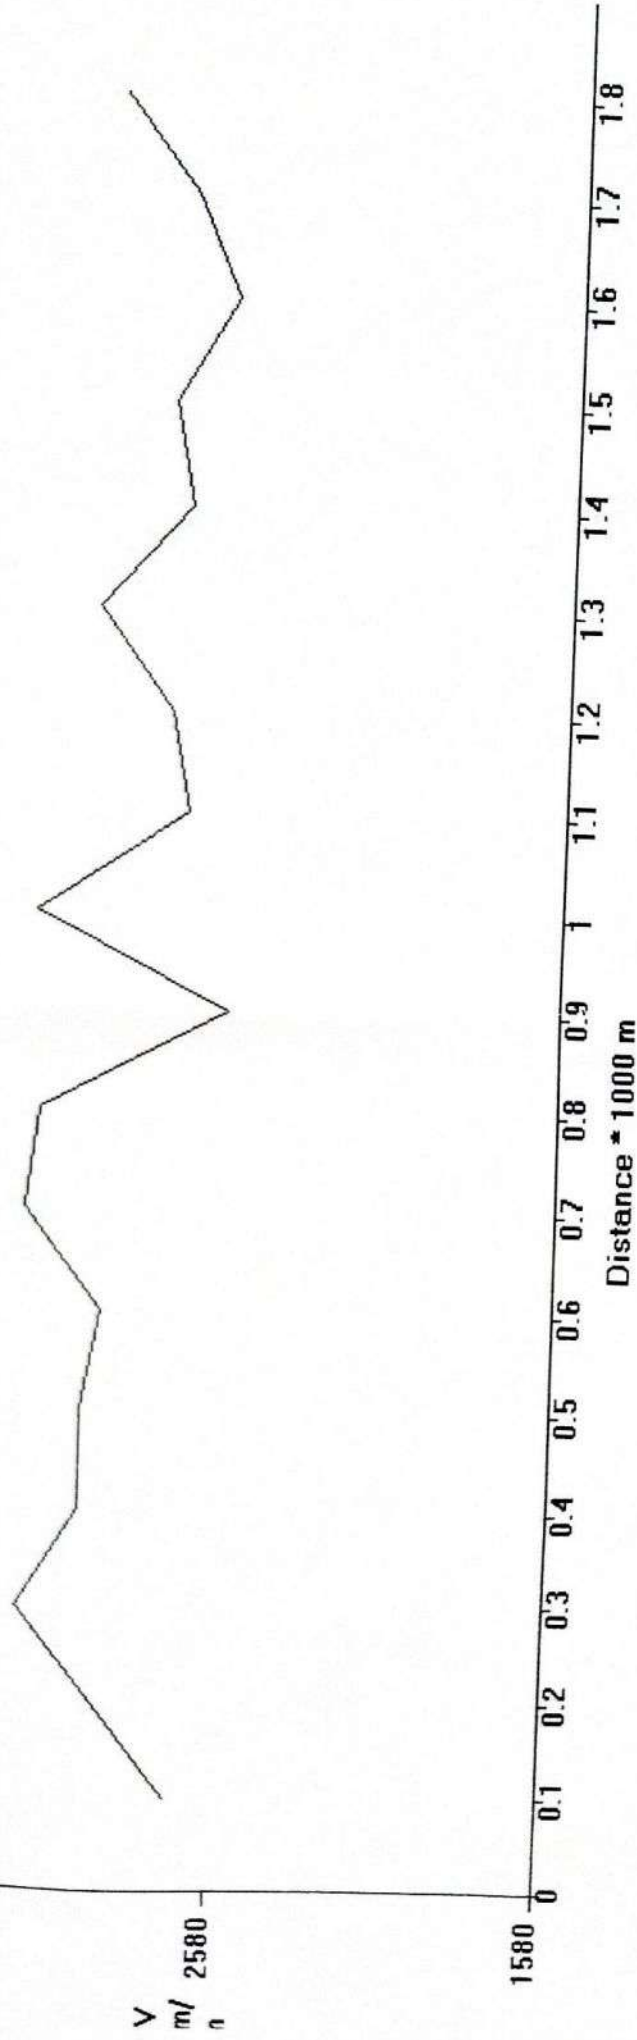

Sund
29/03/18

Shyam
09/03/18
AK

Riyendra Kumar
29/03/18

Executive Engineer
R.W.D. Works Div. Sonapur

2nd & final Bill

20

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
Name of work:- 2nd Met road from Kappadanga to road to math chilawa.					
Agreement NO:- 151 MND, 2024-2025					
Name of Cont:- Sri Lakshmi Kumar					
Date of Start:- 30.08.2024					
Date of Comp:- 29.05.2025					
Measurement - nil					

31/5/2025 1E					
(1) Clearing and grubbing of road level on right side of road (T.M.S.D. 1)					
0.366 Ha					
@ 76926.00/Ha - Rs 28155.00					
(2) Construction of sub-grade and earthen shoulder					
Right side - T.M.S.D. 1					
828.6 m³					
@ 284.57/m³ - Rs 219123.00					

Continuation

247328 = Rs

Continuation
