

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल पकड़ीदयाल।**

पत्रांक.....1400 अलग

पकड़ीदयाल

दिनांक.....05.07.25

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी—सह—सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय :-

(New Maintenance Policy 2018) अन्तर्गत चयनित पथों के लिए
प्राप्त राशि का उपयोगिता प्रमाण-पत्र एवं अधियाचना के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि (New Maintenance Policy 2018)
अन्तर्गत चयनित पथों के लिए उपयोगिता प्रमाण-पत्र एवं अधियाचना विहित प्रपत्र में तैयार
कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

- अनु०—
1. उपयोगिता प्रमाण-पत्र Form GFR 19A
 2. अधियाचना पत्र।
 3. प्रतिवेदन की छायाप्रति।

विश्वासभाजन

Handwritten signature
5/7/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,

कार्य प्रमंडल, पकड़ीदयाल।

Handwritten signature
4/7/2025

Handwritten signature
05/07/25

Form.GFR 19-A Form.

(See Government of India's Decision (1) below Rule .150)
Form Of Utilisation Certificate up to the Month Of July 2025
(New Maintenance Policy 2018)

वर्ष 2018-19, 2019-20 एवं 2020-21 में चयनित पथों के लिए उपयोगिता प्रमाण पत्र

PIU -

SL. No.	Name Of Scheme	Sanction No. & Date With Amount	Amount Received (InRs.)	Particulars
1	Construction Of Rural roads Under (New Maintenance Policy 2018)	Lt. 37 (We) Dt. 27.05.2020 Rs. 75,00,000.00 Lt. 45 (We) Dt. 18.06.2020 Rs. 01,04,50,000.00 Lt. 47 (We) Dt. 24.06.2020 Rs. 96,00,000.00 Lt. 72 (We) Dt. 07.10.2020 Rs. 01,03,00,000.00 Lt. 77 (We) Dt. 14.10.2020 Rs. 01,45,00,000.00 Lt. 80 (We) Dt. 05.11.2020 Amount. Rs. 01,36,50,000.00 Lt. 82 (We) Dt. 13.11.2020 Amount. Rs. 01,35,50,000.00 Lt. 84 (We) Dt. 26.11.2020 Amount. Rs. 01,16,00,000.00 Lt. 86 (We) Dt. 11.12.2020 Amount. Rs. 04,71,14,000.00 Lt. 05 (We) Dt. 12.01.2021 Amount. Rs. 04,88,72,500.00 Lt. 17 (We) Dt. 26.02.2021 Amount. Rs. 04,47,26,500.00 Lt. 20 (We) Dt. 19.03.2021 Amount. Rs. 06,09,42,938.00 Lt. 20 (We) Dt. 19.03.2021 Amount. Rs. 06,09,42,938.00 Lt. 35 (We) Dt. 14.03.2023 Amount. Rs. 06,09,42,938.00 Lt. 60 (We) Dt. 07.04.2023 Amount. Rs. 01,49,00,000.00 Lt. 67 (We) Dt. 27.04.2023 Amount. Rs. 01,77,87,000.00 Lt. 72 (We) Dt. 10.05.2023 Amount. Rs. 11,18,55,000.00 Lt. 81 (We) Dt. 31.05.2023 Amount. Rs. 07,06,59,000.00 Lt. 84 (We) Dt. 08.06.2023 Amount. Rs. 03,02,73,000.00 Lt. 92 (We) Dt. 28.06.2023 Amount. Rs. 05,25,84,000.00 Lt. 100 (We) Dt. 14.07.2023 Amount. Rs. 01,25,59,000.00 Lt. 120 (We) Dt. 04.09.2023 Amount. Rs. 08,09,48,998.00	149,75,61,956.00	Certified that out of Rs. 149,75,61,956.00 received during the year 2017-18 in favour of EX. Engineer, R.W.D W.D Pakridayal sum of Rs. 149,40,24,289.00 has been utilized for the purpose of New Maintenance Policy 2018) schemes as given in the margin for which it was sanctioned and that the balance of Rs 35,37,667.00 remaining Unutilized at the end of the period under.
		149,75,61,956.00	149,75,61,956.00	

2. Certified that I have satisfied myself that the conditions on which the grant in aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was Sanctioned.

Kind Of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MB'S and test check conducted by the Assistant.
- All other codal Formalities have been Observed.

3. Physical Progress Achieved:

- Construction Of Road Works.
- Construction Of CD works.

[Signature]
D.A.O, Grade - 1,
Rural Works Department,
Works Division Pakridayal.

[Signature]
Executive Engineer,
Rural Works Department,
Works Division Pakridayal
[Signature]

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Pakridayal.**

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Works Division : Pakridayal

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval ((AA) Latter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In lakh)	up-to- date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/24-25 Pakridayal/01	Kodariya Petrol Pump To Mirzapur Via Ratanwa.	517871916156	Latter No. 1086 Date- 01.03.2024	0.900	97.33000	49.25009	4.77395	20-MBD/2024-25 Date- 01.10.2024	09.12.2025	In Progress	3301	25	5.00	0.00000	0.00000	20.00000	
2	MR-N/23-24 Pakridayal/09	Parsauni R.E.O Road To Harnatha Mani Bhusan ke Ghar Tak.	517871916154	Latter No. 1086 Date- 01.03.2024	1.000	98.97100	77.29986	3.93418	15-MBD/2024-25 Date- 02.11.2024	01.08.2025	In Progress	3211	25	5.00	0.00000	0.00000	75.00000	
																	95.00000	

- 1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.

J.E. 04/07/25
TS

Pakridayal
A.E. 04/07/25

Pakridayal
4/7/25
D.A.O, Grade-I,
R.W.D, Pakridayal

Executive Engineer,
Rural Works Department,
Works Division, Pakridayal
04/07/25

Kodaria Petrol Pump to Mirzapur via Ratnawa

Contractor Name.- M/S Star Construction

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY		Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD				
04/ 07/ 25	12: 30: 11	60	0.1	320	10.1	3000	3577	G		26.564801	85.185592	Normal
04/ 07/ 25	12: 31: 38	60	0.1	260	10.1	2600	3028	G		26.565015	85.18606	Normal
04/ 07/ 25	12: 32: 07	60	0.1	310	10.1	2900	3442	G		26.564844	85.186096	Normal
04/ 07/ 25	12: 33: 27	60	0.085	270	10.1	3100	3155	G		26.564746	85.185788	Normal

Average 3300.50

$$Y = 0 * X^2 + 0.984 * X + 510.$$

$$X = 3100$$

$$Y = 3155$$

Abhi
07/07/25
TS

Nikash K.R.
04.07.25
AITM

Pavani
07/07/25
AE

Shraddha
5/7/25
SE

Analyzer

Name of Customer : M/S Star Construction

Name of Work/ Road : Kodana Petrol Pump to Mirzapur

Lab Job number : 60

Date : 04-07-2025

Section No. : 60

Test Date : 04-07-2025

Machine No : 437

Start S No :

Start E No :

Weather :

Start Location :

End Location :

Road Name : Kodaria Petrol Pump to Mirzapur

Road Type : (A) ASPHALTIC

Side :

Interval :

UIV Range : 2028 To 5000 1000 mm/km

Dist Range : 0 To 0.5 0.1 * 1000 m


Equation : 1st

Print

Generate Report and Graph

Redraw Graph

Map View

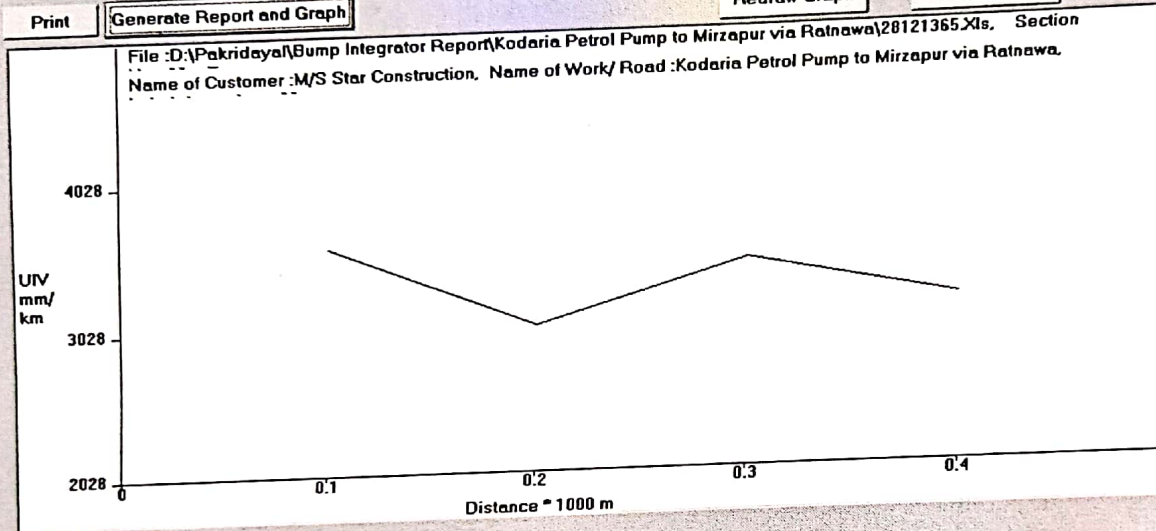

Atti
04/07/25
TS

Vikash K2.
04.07.25
AETM

Palem
04/07/25
AE

Almeed
5/7/25
