

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण)।

पत्रांक: ५३० अनु० / चकिया, दिनांक: १२ / ०३ / २०२५

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, चकिया।

सेवामे,

अपर मुख्य कार्यपालक पदाधिकारी—सह—सचिव,
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय— विभाग के नई निति रख—रखाव २०१८ M.R (३०५४) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख—रखाव २०१८ M.R (३०५४) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:— १. आवंटन की सूची।

२. Bump Test Integrator Machine

विश्वासभाजन,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल—चकिया।

ज्ञापांक— ५३० अनु० दिनांक— १२-०३-२०२५

प्रतिलिपि—नोडल पदाधिकारी (३०५४), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु०:— १. आवंटन की सूची।

२. Bump Test Integrator Machine

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल—चकिया।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Administrative Approval (AA)			Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (in Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	RM/EA/CHA/24/0006	PMGSY Road Balochak Bazar To Konhya Via Palthanla	31708413006	Latter No.1086 Date- 01.03.2024	3.500	218.32000	175.20968	22.85688	10 MBD/2024-25 Date- 29.10.2024	28.07.2025	Work in Progress	2972.00	25	5.00	0.00000	0.00000	97.51000	Work in Progress	
					3.500	218.320	175.20968	22.85688							0.000	0.000	97.51000		

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.

2 Up-to-date Physical Progress has been uploaded in MIS.

[Signature]
Executive Engineer,
Rural Works Department,
Works Division, Chakia.

Form GER 19-A
(See Government of India's decision (1) below Rule - 150)
Form of utilization certificate up to the month up to 03/2025
M.R. (3054) New maintenance Policy-2018.

PIU - RWD , W.D- CHAKIA

SL. NO	Name of Scheme	Sanction No. / Date with Amount (in RS. Lacks)	Amount Received (in RS. Lacks)	particulars
1	M.R. (3054) New maintenance Policy-2018	12164.03492	12164.03492	Certified that out of Rs 12164.03492 Lakh Receive upto the year.2024-25 executive engineer RWD, (W) DIV, chakia a sum of RS.12160.28492 Lakh has been utilized for the perpose of M.R. (3054) New maintenance Policy-2018 'CFMS' Schemes given in the margin for which it was sanctioned and that the balance of Rs.3.75000 lacks remaining unutilized at this end of the (up to 03/2025)

2. Certificate that I have satisfied myself that the conditions on which the grand's-in-aid was sanctioned have been duly fulfilled/ate being fulfilled and that have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned kinds of cheks exercised:-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.

3. Physical Progress achieved :-

- Construction of M.R. (3054) New maintenance Policy-2018 (Details in Progress report)
- Construction of Road Works. (.....Do.....)

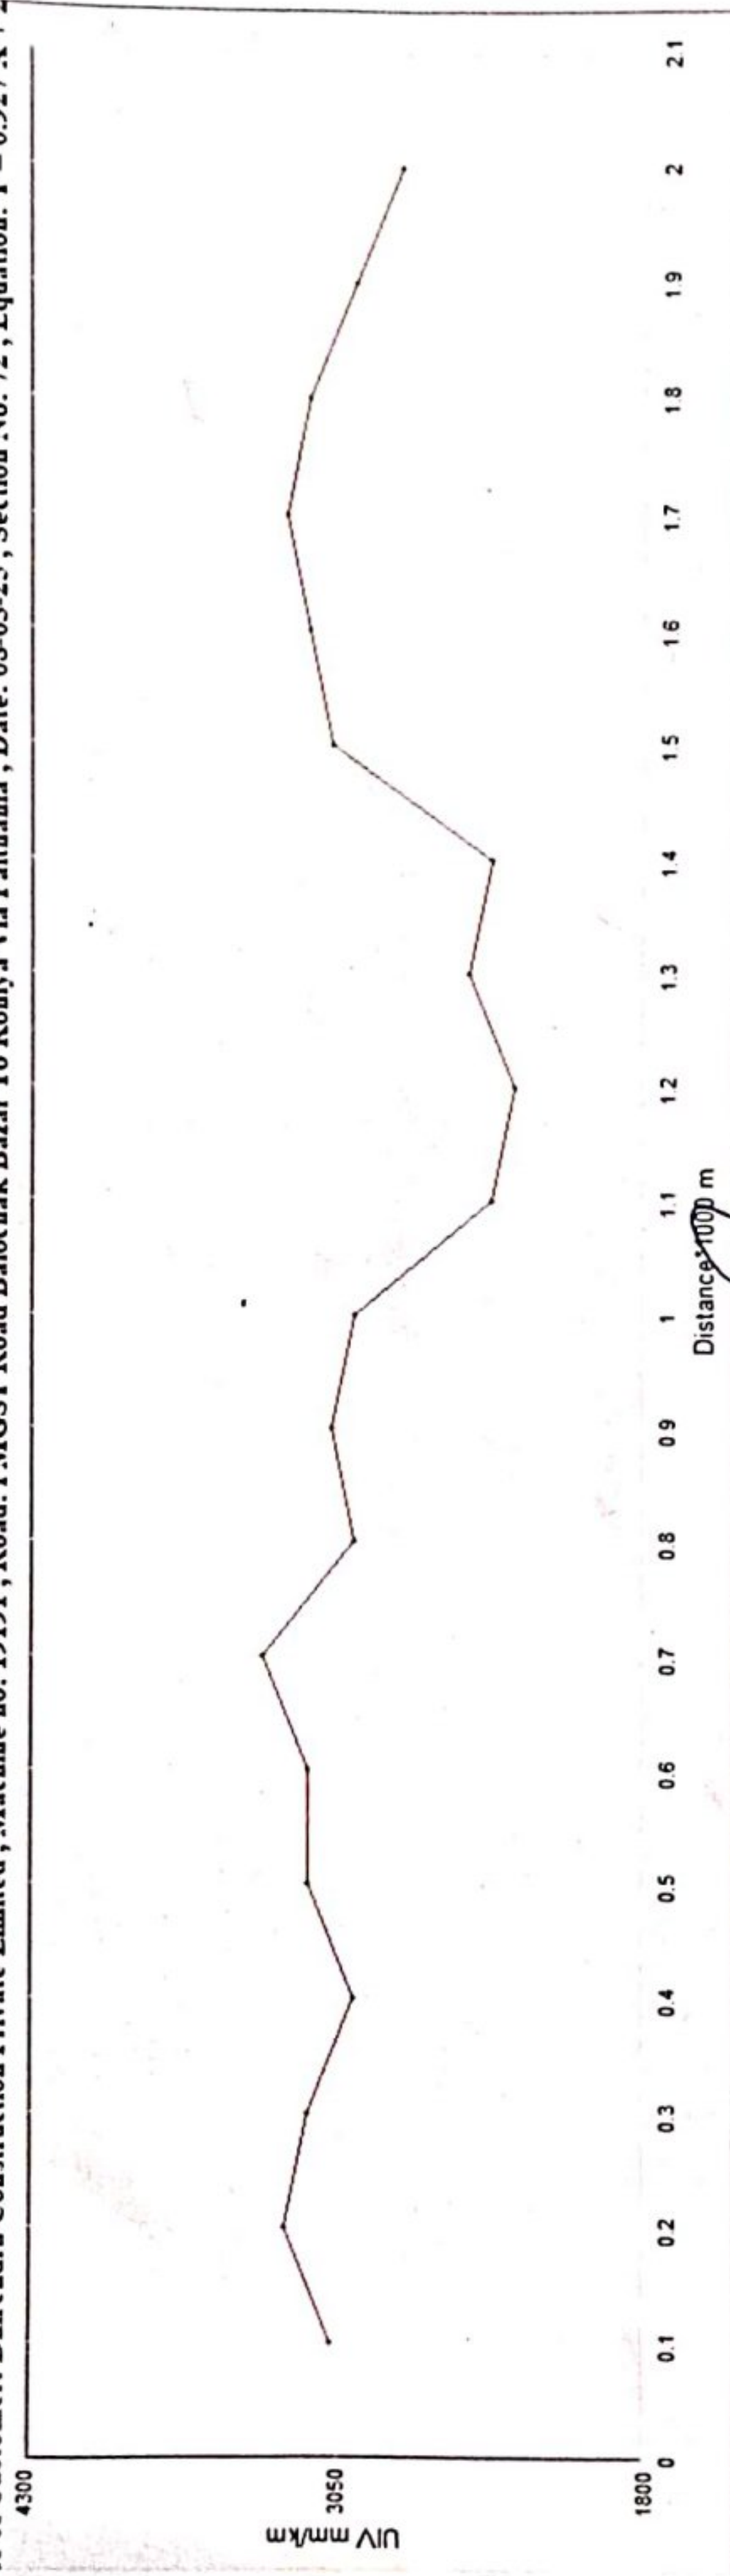

EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT
WORKS DIVISION, CHAKIA.

Name of work		: PMGSY Road Balochak Bazar To Koniya Via Paithania													
Name of customer		: Dhirendra Construction Private Limited													
(R)Rural Road															
Good		Average										Poor			
< 4000		4001 - 5000										> 5000			
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
08/03/25	17:07:46	72	100	100	31.0 cm	25.6 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.4436956	N	85.0487232	E	Normal
08/03/25	17:08:01	72	100	200	33.0 cm	23.4 Km/Hr	3300.0 mm/Km	3264	4.34	Good	26.4436882	N	85.0487071	E	Normal
08/03/25	17:08:14	72	100	300	32.0 cm	27.0 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.4437392	N	85.0494691	E	Normal
08/03/25	17:08:26	72	100	400	30.0 cm	31.5 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.4435254	N	85.0507035	E	Normal
08/03/25	17:08:36	72	100	500	32.0 cm	33.4 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.4435287	N	85.0507059	E	Normal
08/03/25	17:08:47	72	100	600	32.0 cm	33.4 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.4435315	N	85.0507187	E	Normal
08/03/25	17:08:57	72	100	700	34.0 cm	36.0 Km/Hr	3400.0 mm/Km	3357	4.45	Good	26.4426253	N	85.0539024	E	Normal
08/03/25	17:09:11	72	100	800	30.0 cm	26.7 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.4419083	N	85.0556252	E	Normal
08/03/25	17:09:24	72	100	900	31.0 cm	27.7 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.4418016	N	85.0574213	E	Normal
08/03/25	17:09:37	72	100	1000	30.0 cm	27.3 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.4418042	N	85.0574231	E	Normal
08/03/25	17:09:49	72	100	1100	24.0 cm	29.7 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4420366	N	85.0590063	E	Normal
08/03/25	17:10:04	72	100	1200	23.0 cm	25.2 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.4420341	N	85.0590071	E	Normal
08/03/25	17:10:18	72	100	1300	25.0 cm	24.6 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.4420311	N	85.0590113	E	Normal
08/03/25	17:10:24	72	100	1400	24.0 cm	23.4 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.4420301	N	85.0590092	E	Normal
08/03/25	17:10:34	72	100	1500	31.0 cm	27.0 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.4419597	N	85.0612641	E	Normal
08/03/25	17:10:46	72	100	1600	32.0 cm	31.5 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.4420154	N	85.0623095	E	Normal
08/03/25	17:10:56	72	100	1700	33.0 cm	33.4 Km/Hr	3300.0 mm/Km	3264	4.34	Good	26.4422945	N	85.0642291	E	Normal
08/03/25	17:11:07	72	100	1800	32.0 cm	33.4 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.4418823	N	85.0662217	E	Normal
08/03/25	17:11:18	72	100	1900	30.0 cm	36.0 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.4419553	N	85.0673724	E	Normal
08/03/25	17:11:27	72	100	2000	28.0 cm	24.6 Km/Hr	2800.0 mm/Km	2800	3.79	Good	26.4412001	N	85.0695303	E	Normal
AVG IRI-2972															


 11-3-25
 J.E


 11/03/25

Client of Customer: Dhirendra Construction Private Limited, Machine no: 19191, Road: PMGSY Road Balochak Bazar To Koniya Via Paithania, Date: 08-03-25, Section No: 72, Equation: $Y = 0.927X + 2$



[Signature]
11/03/25
J.E

[Signature]
11/03/25
J.E

[Signature]
11-3-25
J.E
