

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।**

पत्रांक 1963 (अकू)

रक्सौल, / दिनांक 21/12/20

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेन्सी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 के तहत आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषयक गैर योजना शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 संलग्न सूची के अनुसार आवंटन अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।

विश्वासभाजन,


21/12/20
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Division :- Raxaul

Requisition of Allotment under Head MR HEAD-3054 Under Bihar Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)


Sl. No.	Package No.	Name of Road	Contractor Name	Project ID as Per MIS	Administrative Approval (AA) Letter No. & Date	A.A.		Agreement Value			Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of BIL (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Added Amount	up-to-date Expenditure as per MIS (in Lakh)	Requestion against work done. (in Lakh)	Remarks
						Length (in Km)	Total (Amount) (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Yrs Routine Maintenance (in Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	
MIR-N/19-20/Raxaul/09	NH 28A to Bishambarpur	Paramba Construction Private Limited	31708202154	3054-04-117-2019, 5973/पदपि, दिनांक-30.10.2019	2.520	95.77200	68.06300	26.6183	172MBD/20-21 Date-06-08-2020	05-08-2021	-	2567.9	25mm	5	0	0	0	68.000000	Work Completed	
																		68.000000		

Engineer,
Rural Works Department,
Works Division, Raxaul

Name of Customer : PRAMBHA CONSTRUCTION F
 Name of Work/ Road : NH28A TO BISHAMBHARPUR
 Lab Job number :
 Date : 20-12-2020
 Section No. : 23

Test Date :	20-12-2020	Road Name :	NH28A TO BISHAMBHARPUR	
Machine No :	378	Road Type :	(R) RURAL ROAD	
Start S No :	0.00 KM	Side :		
Start E No :	2.520 KM	Interval		
Weather :		UIV Range :	905 To 5000	mm/km
Start Location :		Dist Range :	0 To 2.7	0.1 * 1000 m
End Location :		Equation :	$Y = 0 * X^2 + 0.998 * X + 109.5$	

File : D:\BuMP Indicator\Roxaul\Prambha Construction\19121759.Xls. Section No. : 23, Eqn : $Y = 0 * X^2 + 0.998 * X + 109.5$
 Name of Customer : PRAMBHA CONSTRUCTION PVT. LTD., Name of Work/ Road : NH28A TO BISHAMBHARPUR,

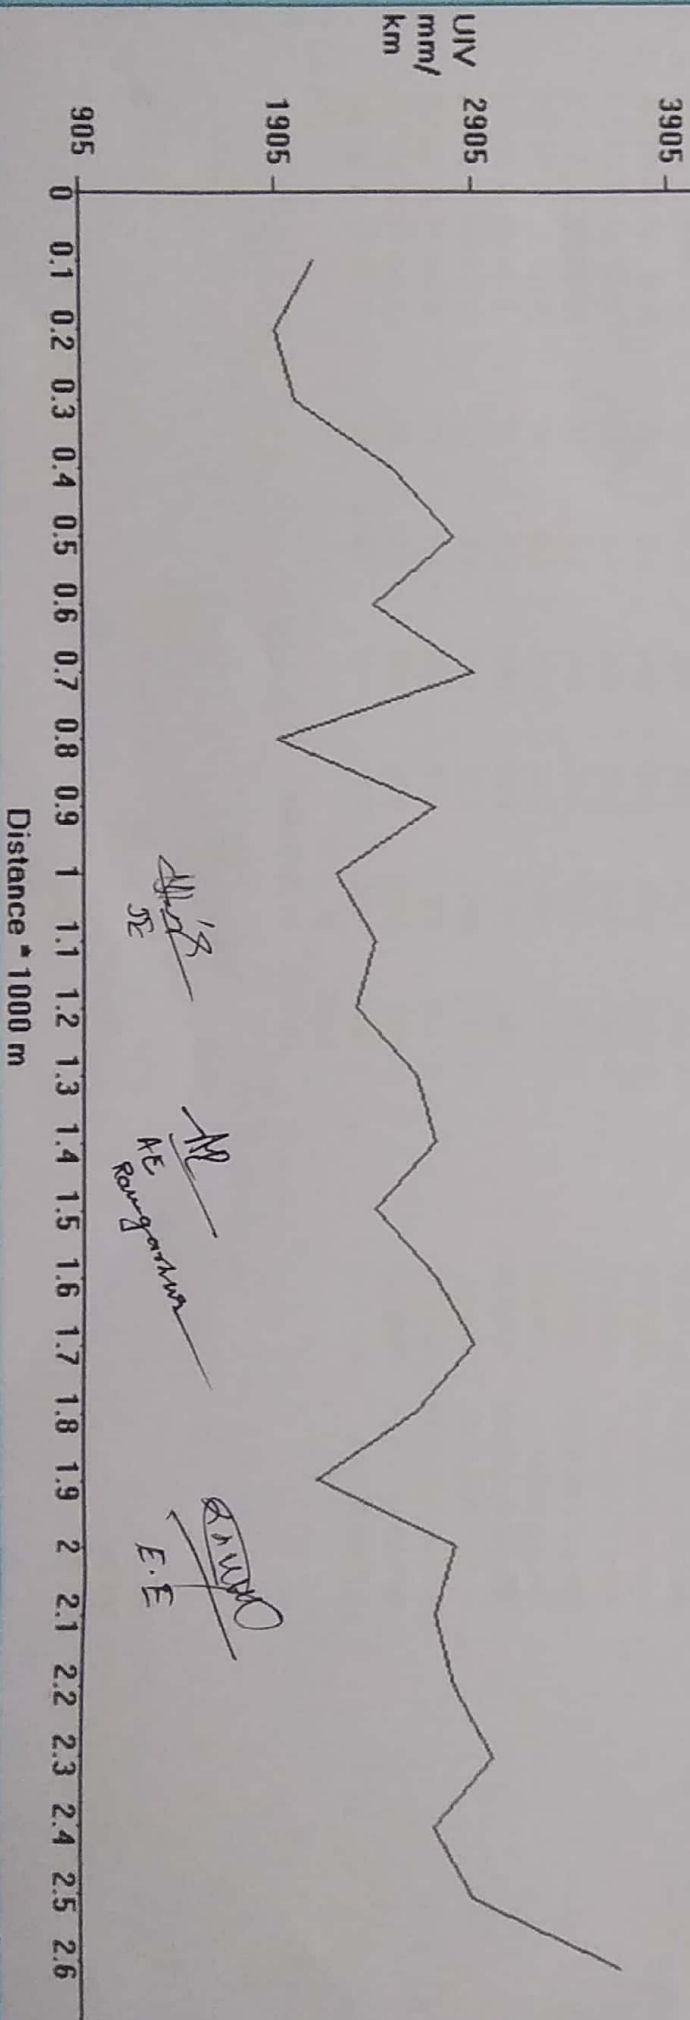

ROAD NAME-NH28A TO BISHAMBHARPUR, CONTRACTOR-PRAMBHA CONSTRUCTION PVT. LTD

Date	Time	Section	Length	Bumps	Speed	OR	IRI in	CATEGORY	Latitude	Longitude	Event	
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD				
20/12/20	15:50:29	23	0.1	200	0	2000	2105 G		26.90275	84.81843	Normal	$Y = 0 * X^2 + 0.998 * X + 109.5$
20/12/20	15:51:5	23	0.1	180	30.3	1800	1905 G		26.90263	84.819343	Normal	$X = 3559$
20/12/20	15:52:0	23	0.1	190	30.3	1900	2005 G		26.90225	84.820185	Normal	$Y = 3661$
20/12/20	15:52:15	23	0.1	240	30.3	2400	2504 G		26.90203	84.821093	Normal	
20/12/20	15:52:15	23	0.1	270	30.3	2700	2804 G		26.90188	84.822053	Normal	(R) RURAL ROAD
20/12/20	15:52:15	23	0.1	230	30.3	2300	2404 G		26.90187	84.823047	Normal	Good
20/12/20	15:53:0	23	0.1	280	20.2	2800	2903 G		26.90256	84.823652	Normal	Average
20/12/20	15:53:0	23	0.1	180	20.2	1800	1905 G		26.90243	84.824578	Normal	4001-5000
20/12/20	15:53:26	23	0.1	260	30.3	2600	2704 G		26.90229	84.825555	Normal	>5001
20/12/20	15:53:26	23	0.1	210	30.3	2100	2205 G		26.90223	84.826582	Normal	
20/12/20	15:54:0	23	0.1	230	30.3	2300	2404 G		26.90242	84.827542	Normal	
20/12/20	15:54:0	23	0.1	220	30.3	2200	2305 G		26.9027	84.82847	Normal	
20/12/20	15:54:0	23	0.1	250	20.2	2500	2604 G		26.90299	84.829393	Normal	
20/12/20	15:54:35	23	0.1	260	30.3	2600	2704 G		26.90336	84.830285	Normal	
20/12/20	15:55:0	23	0.1	230	20.2	2300	2404 G		26.90405	84.830958	Normal	
20/12/20	15:55:11	23	0.1	260	30.3	2600	2704 G		26.90469	84.831632	Normal	
20/12/20	15:55:11	23	0.1	280	30.3	2800	2903 G		26.90536	84.832103	Normal	
20/12/20	15:55:46	23	0.1	250	30.3	2500	2604 G		26.90622	84.832525	Normal	
20/12/20	15:56:0	23	0.1	200	20.2	2000	2105 G		26.90654	84.8334	Normal	
20/12/20	15:56:21	23	0.1	270	20.2	2700	2804 G		26.90693	84.834242	Normal	
20/12/20	15:57:0	23	0.1	260	30.3	2600	2704 G		26.90652	84.835	Normal	
20/12/20	15:57:0	23	0.1	270	30.3	2700	2804 G		26.90579	84.835505	Normal	
20/12/20	15:58:0	23	0.1	290	30.3	2900	3003 G		26.9051	84.83606	Normal	
20/12/20	15:58:7	23	0.1	260	30.3	2600	2704 G		26.90541	84.836902	Normal	
20/12/20	15:59:0	23	0.1	280	20.2	2800	2903 G		26.90529	84.837743	Normal	
20/12/20	15:59:0	23	0.059	210	10.1	3559	3661 G		26.90513	84.838	Normal	
		TOTAL IRI		66764								
		AVERAGE IRI		2567.85								

JE

[Signature]
21/12/20
JE

[Signature]
21/12/20
AE
Rambhadracharya

[Signature]
21/12/20
AE
Rambhadracharya

EXECUTIVE ENGINEER
RURAL WORK DEPARTMENT
WORKS DIVISION, RAXAUL
