

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा ।

पत्रांक:.....2.0.05 (3177)

/ हिलसा, दिनांक:.....22/12/2020

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा ।

सेवा में,

नोडल पदाधिकारी,
नई अनुरक्षण निति-2018 (3054),
ग्रामीण कार्य विभाग, बिहार, पटना ।

विषय- नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन की मांग ।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु संलग्न विवरणी के अनुसार रु० 95.33019 (रु० पंचान्नावे लाख तैतीस हजार उन्नीस रुपया मात्र) रुपये का आवंटन उपलब्ध कराने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके ।
अनुलग्नक :- विहित प्रपत्र में अधियाचना ।



विश्वास भाजन

22/12/2020

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा ।

22/12/20

22/12

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Hilsa

Name of Works Division :-Hilsa																		
SI No.	Package No.	Name of Road	Project ID as per MIS	Administ rative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to- date expendit re as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (In km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	RM/NA/HIL/19 /0006	Bisurwa to dharanapur	1281033305	5275/ 04.10.19	0.505	20.678	18.38732	4.63907	01/MBD/20 20-21	02.12.2020	15.11.2020	2167	25.03	5.09	18.38732	0.00	0.000000	
1	RM/NA/HIL/19 /0006	Hilsa-Noorsarai main lahradak to kachhiyawan	1281033288	5275/ 04.10.19	3.500	161.658	149.33713	32.46151	01/MBD/20 20-21	02.12.2020	12.11.2020	2503	25.02	5.13	104.53599	0.00	44.80114	
2	RM/NA/HIL/19 /0006	Hilsa-Noorsarai Rd - Mominpur	10200802047	5275/ 04.10.19	1.440	56.565	49.48510	13.31634	01/MBD/20 20-21	02.12.2020	16.11.2020	2325	25.04	5.08	49.48510	0.00	0.000000	
3	RM/NA/HIL/19 /0006	Hilsa-Noorsarai Rd - Mominpur	10200802047	5275/ 04.10.19	1.440	56.565	49.48510	13.31634	01/MBD/20 20-21	02.12.2020	16.11.2020	2325	25.04	5.08	49.48510	0.00	0.000000	
4	RM/NA/HIL/19 /0006	Hilsa-Noorsarai Rd - Bhabhanbarui	10200802048	5275/ 04.10.19	1.152	32.277	24.14317	10.59988	01/MBD/20 20-21	02.12.2020	13.11.2020	2655	25.05	5.09	24.14000	0.00	0.000317	
5	RM/NA/HIL/19 /0006	Hilsa-Reri Bansigha Rd. - Alipur	10200802049	5275/ 04.10.19	1.950	93.09	85.37092	18.06239	01/MBD/20 20-21	02.12.2020	14.11.2020	1720	25.04	5.11	68.29674	0.00	17.07418	
6	RM/NA/HIL/19 /0006	Kawa Villae to Jatipur Bansi Bigha	10200901005	5275/ 04.10.19	1.700	68.056	59.96201	15.58088	01/MBD/20 20-21	02.12.2020	26.11.2020	2583	25.01	5.16	47.96961	0.00	11.99240	
7	RM/NA/HIL/19 /0006	Milki Narayanpur RWD Path to Prathmik vidyala kesopur	1281033301	5275/ 04.10.19	0.350	14.724	13.16037	3.24535	01/MBD/20 20-21	02.12.2020	11.11.2020	2394	25.05	5.18	13.16000	0.00	0.000000	
8	RM/NA/HIL/19 /0006	Reri Majidpur Road to Supra (TRACK36)	10200802084	5275/ 04.10.19	1.310	56.06	52.38452	12.21356	01/MBD/20 20-21	02.12.2020	27.11.2020	3461	25.05	5.11	41.90762	0.00	10.47690	
9	RM/NA/HIL/19 /0006	Sultanpur arpa road to nagma	1281033300	5275/ 04.10.19	1.510	61.87	54.91202	16.26875	01/MBD/20 20-21	02.12.2020	28.11.2020	1594	25.04	5.13	43.92962	0.00	10.98240	
10	RM/NA/HIL/19 /0006	Yogipur- Harbanpur Rd. - Fujiwariya	10200802075	5275/ 04.10.19	0.700	20.094	15.24695	6.43171	01/MBD/20 20-21	02.12.2020	29.11.2020	3610	25.01	5.05	15.24695	0.00	0.000000	
TOTAL													95.33019					

1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.

2 Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer
RWD, Works Division,
Hilsa

25/11/2020

NAME OF THE ROAD : SULTANPUR ARPA PATH TO NAGMA

LENGTH OF THE ROAD : 1.510 KM

PACKAGE NO. : IMR-N/19-20/HILSA/04

DIVISION : HILSA

BLOCK : HILSA

Date	Time	Section	Length in km	Bumps in m/m	Speed Rate	OR mm/km	UIV mm/km	CATEGORY ROAD	IRI	Latitude	Longitude	Event			
24/11/20	14:17:4	12	0.1	130	0	1300	1495	G	2.16	25.25055	85.31512	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
24/11/20	14:17:24	12	0.1	210	20.2	2100	2244	G	3.11	25.25062	85.314175	Normal	$X = 900$		
24/11/20	14:17:39	12	0.1	150	30.3	1500	1682	G	2.4	25.25079	85.31313	Normal	$Y = 1120$		
24/11/20	14:17:54	12	0.1	150	30.3	1500	1682	G	2.4	25.25084	85.312205	Normal			
24/11/20	14:18:0	12	0.1	220	20.2	2200	2337	G	3.22	25.25054	85.311278	Normal	(R) RURAL ROAD		
24/11/20	14:18:34	12	0.1	220	20.2	2200	2337	G	3.22	25.24968	85.31116	Speed Breaker	Good	Average	Poor
24/11/20	14:19:0	12	0.1	160	10.1	1600	1776	G	2.52	25.24936	85.310522	Normal	<4000	4001-5000	>5001
24/11/20	14:19:18	12	0.1	170	30.3	1700	1869	G	2.63	25.24939	85.309562	Normal			
24/11/20	14:19:34	12	0.1	190	30.3	1900	2056	G	2.87	25.24942	85.308585	Normal			
24/11/20	14:19:48	12	0.1	130	30.3	1300	1495	G	2.16	25.24941	85.307608	Normal			
24/11/20	14:19:59	12	0.1	170	30.3	1700	1869	G	2.63	25.24939	85.306582	Normal			
24/11/20	14:20:15	12	0.1	100	20.2	1000	1214	G	1.79	25.24939	85.305555	Normal			
24/11/20	14:20:32	12	0.1	130	20.2	1300	1495	G	2.16	25.25011	85.305453	Normal			
24/11/20	14:20:49	12	0.1	100	30.3	1000	1214	G	1.79	25.25103	85.305487	Normal			
24/11/20	14:21:9	12	0.1	100	30.3	1000	1214	G	1.79	25.25185	85.305318	Normal			
24/11/20	14:21:29	12	0.1	90	30.3	900	1120	G	1.66	25.25284	85.305268	Normal			
TOTAL			1.51	2420	383.8	24200	27099		38.51	404.0053	1364.947008				

Ramp
11:20
14:15Carp
11:20
14:15

Name of Customer : SUNNY CONTR. AND ENGG.
 Name of Work : SULTANPUR ARPA RD TO N
 Road :
 Lab Job number :
 Date : 24/11/2020
 Section No. : 12

Test Date :	24/11/2020	Road Name :	NUPUR ARPA RD. TO NAQMA		
Machine No :		Road Type :	(R) RURAL ROAD		
Start S No :		Side :			
Start E No :		U/V Range :	0	To	4000
Weather :				Interval	1000
Start Location :		Dist Range :	0	To	1000
End Location :		Equation :	$Y = 0.0 \cdot X^2 + 0.936 \cdot X + 278.4$		


Print

Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\SHAZID\Desktop\1112.Xls. Section No. : 12. Eqn : $Y = 0.0 \cdot X^2 + 0.936 \cdot X + 278.4$
 Name of Customer : SUNNY CONTR. AND ENGG. PVT LTD. Name of Work/ Road : SULTANPUR ARPA RD. TO

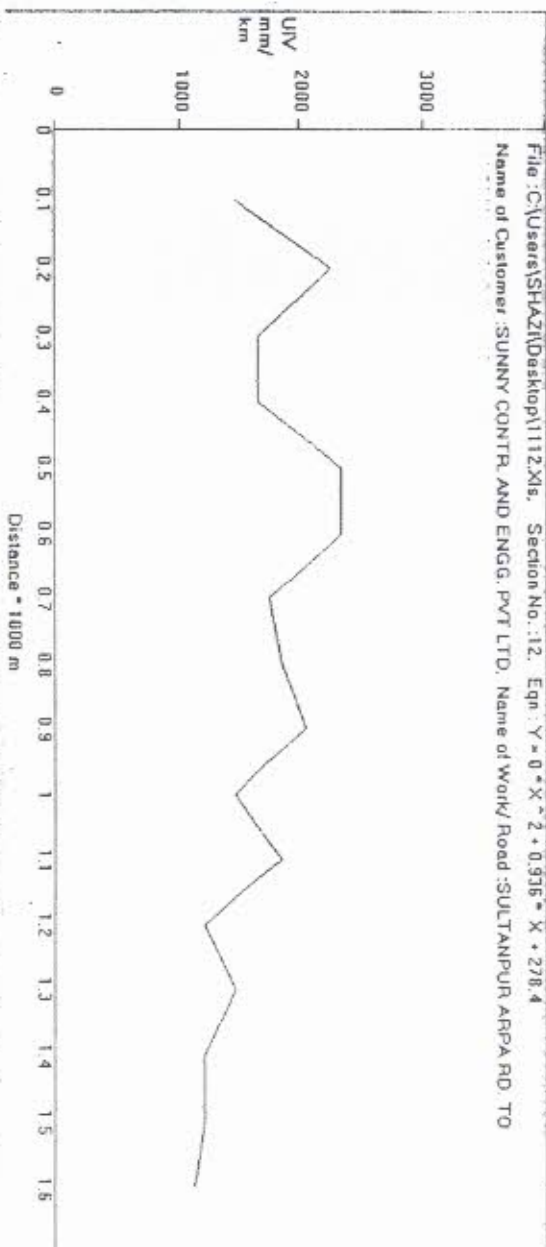

Page 2
24/11/2020
5.13

Calculated
24/11/2020
ATE

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D. GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Sultanpur Arba Road to Nagma

Name of Scheme :- 3054-MR

Name of Agency :- Sunny Contractors and Engineers Pvt Ltd

Nature of sample :- Bitumens Content for source

Location :- Gorum

Date of Collection/Received :- 01/12/2020

Date of Test :- 02/12/2020

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Hilga vide letter No. 331 Dt. 28.11.2020Agreement No / Package No. : 01MRD/2020-21

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	508.30	510.40	506.86	
2	Wt. of Dry chips after extraction (b)	482.29	484.29	480.81	
3	Percentage of bitumen (in the mix) [(a-b)*100]/a (%)	5.12	5.12	5.14	
4	Average % bitumen	5.13			

Handwritten: 17/12/20
02.12.20
L.A.

A.D.

A.E.

E.E.

Regional Laboratory

Regional Laboratory

Regional Laboratory

Regional Laboratory

R.W.D. Guljarbagh patna - 7

R.W.D. Guljarbagh patna - 7

R.W.D. Guljarbagh patna - 7

R.W.D. Guljarbagh patna - 7

Handwritten: 17/12/20
02.12.20
L.A.

Handwritten: 17/12/20
02.12.20
L.A.

Handwritten: 17/12/20
02.12.20
L.A.
