

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, पीरो।

पत्रांक :- 1047

पीरो, दिनांक :- 23/12/2020

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, पीरो।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय :- योजना शीर्ष Bihar Maintenance Policy (2018) के अंतर्गत किये गये कार्य का
आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि योजना शीर्ष Bihar Maintenance Policy (2018) के अंतर्गत कार्य किया गया है किये गये कार्य के भुगतान हेतु संलग्न विवरणी के अनुसार 250.82297 दो करोड़ पचास लाख बयासी हजार दो सौ सत्तानबे रू० की आवश्यकता है।

अतः अनुरोध है कि उक्त राशि का आवंटन उपलब्ध कराया जाय, ताकि किये गये विभागीय कार्य का भुगतान हो सके।

अनु०-यथोक्त।

विश्वासभाजन

(R. B. Singh)
23/12/2020

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, पीरो।

23.12.2020

Requisition Format for Scheme Head - MR (045) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Work Division:- Piro

Sl. No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) letter No. & Date	Administrative		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of R/I (in m/cum)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount (in Lakh)	Up-to-date expenditure against work done (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-207Pro02	Improvement of Itan Bazar Teraich Katana Road	10401604122	402 / 02-07-2019	1.750	571.6000	36.128	12.99601	08NAEB/D/M/ R-2019-20/ 31-01-2020	30-10-2020	12/10/2020	2964	25mm	5%	0.00	0.00	36	Completed
2	MR-N/19-207Pro02	Amhara Pad to Binger Shwari Via Dangar Tola Sahabudin, Sanyapur Tola Bhatman Tola	14181031840	400 / 02-07-2019	7.600	206.51000	124.607	53.96596	08NAEB/D/M/ R-2019-20/ 31-01-2020	30-10-2021	14-10-2020	3042	25mm	5%	0.00	0.00	124.5	Completed
3	MR-N/19-207Pro02	Construction of Road from Sahajan at Aya Sasaram main Road to Baraach	10401801008	400 / 02-07-2019	2.900	81.48000	48.484	21.48596	08NAEB/D/M/ R-2019-20/ 31-01-2020	30-10-2022	16-10-2020	3088	25mm	5%	0.00	0.00	48.38	Completed
4	MR-N/19-207Pro12	Kuna Bazar - Milky Samra	NEA220001713	402 / 02-07-2019	1.830	66.19000	42.542	14.41489	08NAEB/D/M/ R-2019-20/ 31-01-2020	30-10-2023	26-10-2020	3203	25mm	5%	0.00	0.00	41.94297	Completed
Total					14.080	411.34000	251.761	102.46232							0.00	0.00	230.82297	

1. Signed Hard Copy and Soft Copy (in excel) of recorded R/I is enclosed.

2. Up-to date Physical Progress has been uploaded in MIS.

23/12
D.A.O

Executive Engineer
Rural Works Department
Works Division, Piro
23/12/2020


Name of Customer: VISHNU SHANKAR OJHA
 Name of Work/Road: AHMEHTA PUL TO VIRPUR SHWAT
 Lab Job number:
 Date: 11-11-2020
 Section No. 35

Test Date: 11-11-2020 Road Name: ITA PUL TO VIRPUR SHWAT
 Machine No: 308 Road Type: (R) RURAL ROAD
 Start S No: Side:
 Start E No: Interval
 Weather: UV Range: 1577 To 5000 1000 mm/km
 Start Location: MEHTA PUL Dist Range: 0 To 7.7 0.1 * 1000 m
 End Location: PUR SHWAT Equation: $Y = 0 \cdot X^2 + 0.984 \cdot X + 510.70$

Print Generate Report and Graph

Redraw Graph

Map View

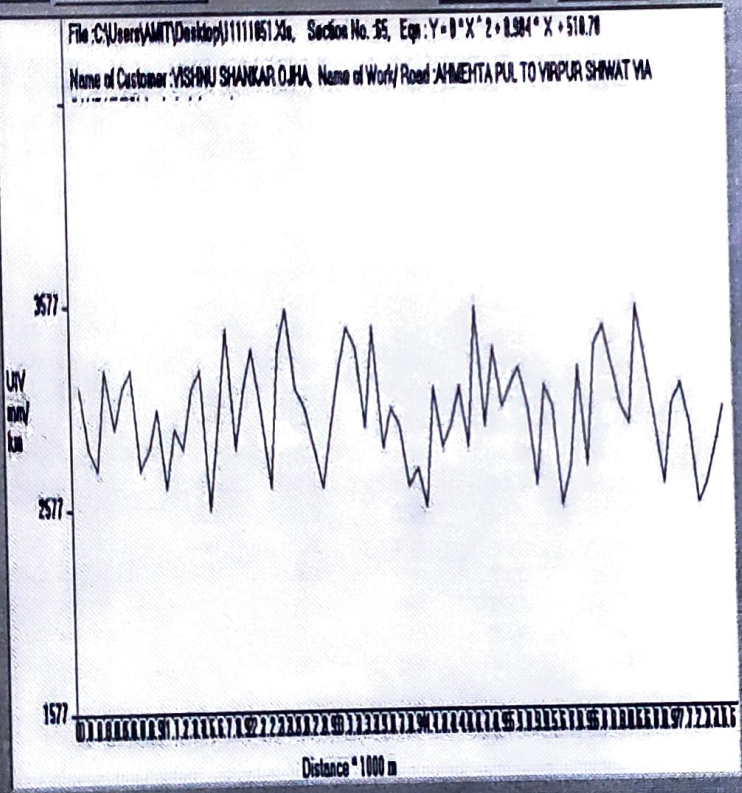

Spice
 25/11/2020
 BR

(BPKSH)
 25/11/2020

CONTRACTOR NAME - VISHNU SHANKAR OJHA ROAD NAME - AMHATA PUL TO BIRPUR SIWAT VIA GANPAT TOLA SALAKHINA, SURYAPURA TOLA BUDHRAMTOLA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR	IRI	TEGORY	Latitude	ongitude	Event
11/11/20	15:45:11	65	0.1	270	0	2700	3167	G	25.35097	84.38724	Normal
11/11/20	15:46:0	65	0.1	240	31.2	2400	2872	G	25.3518	84.38689	Normal
11/11/20	15:46:0	65	0.1	230	30.3	2300	2773	G	25.35264	84.38652	Normal
11/11/20	15:46:21	65	0.1	280	30.3	2800	3265	G	25.3535	84.38614	Normal
11/11/20	15:46:21	65	0.1	250	32.5	2500	2970	G	25.35434	84.38577	Normal
11/11/20	15:46:21	65	0.1	270	31.2	2700	3167	G	25.35461	84.38505	Normal
11/11/20	15:47:0	65	0.1	280	30.3	2800	3265	G	25.35462	84.38406	Normal
11/11/20	15:47:0	65	0.1	230	30.3	2300	2773	G	25.35522	84.38332	Normal
11/11/20	15:47:32	65	0.1	240	30.3	2400	2872	G	25.35581	84.38263	Normal
11/11/20	15:47:32	65	0.1	260	31.2	2600	3069	G	25.35644	84.3819	Normal
11/11/20	15:48:7	65	0.1	220	31.2	2200	2675	G	25.35707	84.38118	Normal
11/11/20	15:48:7	65	0.1	250	31.5	2500	2970	G	25.35766	84.38047	Normal
11/11/20	15:48:7	65	0.1	240	30.3	2400	2872	G	25.35827	84.37978	Normal
11/11/20	15:48:42	65	0.1	270	31.2	2700	3167	G	25.35885	84.37911	Normal
11/11/20	15:49:0	65	0.1	280	32.5	2800	3265	G	25.35948	84.37838	Normal
11/11/20	15:49:18	65	0.1	210	31.2	2100	2577	G	25.36007	84.37769	Normal
11/11/20	15:49:18	65	0.1	250	30.3	2500	2970	G	25.36068	84.37697	Normal
11/11/20	15:50:0	65	0.1	240	31.2	2400	2872	G	25.3613	84.37625	Normal
11/11/20	15:50:0	65	0.1	270	31.2	2700	3167	G	25.36191	84.37552	Normal
11/11/20	15:50:0	65	0.1	290	32.5	2900	3364	G	25.36248	84.37487	Normal
11/11/20	15:50:28	65	0.1	260	30.3	2600	3069	G	25.36314	84.37412	Normal
11/11/20	15:50:28	65	0.1	220	31.2	2200	2675	G	25.36371	84.37345	Normal
11/11/20	15:51:4	65	0.1	290	30.3	2900	3364	G	25.36432	84.37273	Normal
11/11/20	15:51:4	65	0.1	310	30.3	3100	3561	G	25.36491	84.37204	Normal
11/11/20	15:51:4	65	0.1	270	32.5	2700	3167	G	25.36554	84.37128	Normal
11/11/20	15:51:39	65	0.1	260	30.3	2600	3069	G	25.36614	84.37057	Normal
11/11/20	15:51:39	65	0.1	240	30.3	2400	2872	G	25.36677	84.36985	Normal
11/11/20	15:52:0	65	0.1	220	30.3	2200	2675	G	25.36737	84.36914	Normal
11/11/20	15:52:14	65	0.1	250	30.3	2500	2970	G	25.36798	84.36843	Normal
11/11/20	15:52:14	65	0.1	280	30.3	2800	3265	G	25.36858	84.36773	Normal
11/11/20	15:52:14	65	0.1	300	31.2	3000	3462	G	25.36919	84.36702	Normal
11/11/20	15:52:49	65	0.1	290	30.3	2900	3364	G	25.36979	84.36633	Normal
11/11/20	15:53:0	65	0.1	250	30.3	2500	2970	G	25.37041	84.36559	Normal
11/11/20	15:53:0	65	0.1	300	30.3	3000	3462	G	25.37102	84.3649	Normal
11/11/20	15:53:25	65	0.1	240	32.5	2400	2872	G	25.3716	84.36421	Normal
11/11/20	15:53:25	65	0.1	260	30.3	2600	3069	G	25.37222	84.36348	Normal
11/11/20	15:53:25	65	0.1	250	31.2	2500	2970	G	25.37283	84.36278	Normal
11/11/20	15:54:0	65	0.1	220	32.5	2200	2675	G	25.3734	84.3621	Normal
11/11/20	15:54:0	65	0.1	220	32.5	2200	2675	G	25.37403	84.3614	Normal

$$Y = 0^\circ X^2 + 0.984^\circ X + 510.70$$

$$X = 7368$$

$$Y = 7760$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

11/11/20	15:54:0	65	0.1	230	30.3	2300	2773 G	25.37463	84.36069	Normal
11/11/20	15:54:0	65	0.1	210	30.3	2100	2577 G	25.37527	84.35995	Normal
11/11/20	15:54:35	65	0.1	270	30.3	2700	3167 G	25.37592	84.35938	Curve
11/11/20	15:55:0	65	0.1	240	31.2	2400	2872 G	25.37652	84.35865	Normal
11/11/20	15:55:11	65	0.1	250	30.3	2500	2970 G	25.37709	84.35801	Normal
11/11/20	15:55:11	65	0.1	270	30.3	2700	3167 G	25.37772	84.35727	Normal
11/11/20	15:55:11	65	0.1	240	30.3	2400	2872 G	25.37828	84.35662	Normal
11/11/20	15:55:11	65	0.1	310	30.3	3100	3561 G	25.37889	84.35591	Normal
11/11/20	15:55:46	65	0.1	310	30.3	3100	3561 G	25.37954	84.35515	Normal
11/11/20	15:56:0	65	0.1	250	30.3	2500	2970 G	25.38013	84.35448	Normal
11/11/20	15:56:0	65	0.1	290	30.3	2900	3364 G	25.38074	84.35375	Normal
11/11/20	15:56:0	65	0.1	260	30.3	2600	3069 G	25.38074	84.35375	Normal
11/11/20	15:56:21	65	0.1	270	30.3	2700	3167 G	25.38196	84.35234	Normal
11/11/20	15:56:21	65	0.1	280	30.3	2800	3265 G	25.38196	84.35234	Normal
11/11/20	15:56:21	65	0.1	260	30.3	2600	3069 G	25.3826	84.35162	Normal
11/11/20	15:56:21	65	0.1	270	30.3	2700	3167 G	25.38307	84.35081	Normal
11/11/20	15:57:0	65	0.1	220	31.2	2200	2675 G	25.38317	84.34988	Normal
11/11/20	15:57:32	65	0.1	270	32.5	2700	3167 G	25.38329	84.34889	Normal
11/11/20	15:57:32	65	0.1	260	30.3	2600	3069 G	25.38341	84.3479	Normal
11/11/20	15:57:32	65	0.1	210	30.3	2100	2577 G	25.38353	84.34694	Normal
11/11/20	15:58:0	65	0.1	230	30.3	2300	2773 G	25.38364	84.34594	Normal
11/11/20	15:58:7	65	0.1	280	30.3	2800	3265 G	25.38376	84.34497	Normal
11/11/20	15:58:7	65	0.1	230	30.3	2300	2773 G	25.38387	84.34407	Normal
11/11/20	15:58:7	65	0.1	290	30.3	2900	3364 G	25.38395	84.34342	Normal
11/11/20	16:1:39	65	0.1	300	31.2	3000	3462 G	25.38383	84.34456	Normal
11/11/20	16:9:4	65	0.1	280	32.5	2800	3265 G	25.38372	84.34545	Normal
11/11/20	16:9:4	65	0.1	260	30.3	2600	3069 G	25.38352	84.34712	Normal
11/11/20	16:9:39	65	0.1	250	31.2	2500	2970 G	25.3834	84.34811	Normal
11/11/20	16:10:0	65	0.1	310	32.5	3100	3561 G	25.38328	84.34912	Normal
11/11/20	16:10:15	65	0.1	280	30.3	2800	3265 G	25.38316	84.35	Normal
11/11/20	16:10:15	65	0.1	250	30.3	2500	2970 G	25.38303	84.35104	Curve
11/11/20	16:10:15	65	0.1	220	30.3	2200	2675 G	25.38245	84.35175	Normal
11/11/20	16:10:15	65	0.1	260	30.3	2600	3069 G	25.38184	84.35246	Normal
11/11/20	16:10:51	65	0.1	270	31.2	2700	3167 G	25.3812	84.35322	Normal
11/11/20	16:11:0	65	0.1	250	32.5	2500	2970 G	25.38062	84.35389	Normal
11/11/20	16:11:0	65	0.1	210	30.3	2100	2577 G	25.38003	84.3546	Normal
11/11/20	16:11:26	65	0.1	220	30.3	2200	2675 G	25.37937	84.35535	Normal
11/11/20	16:11:26	65	0.1	240	30.3	2400	2872 G	25.37915	84.35561	Normal
11/11/20	16:12:0	65	0.1	260	32.5	2600	3069 G			

Signature of Junior Engineer

Signature of Assistant Engineer

Signature of Executive Engineer
