

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद

Email ID:- eerwdaurangabad1@gmail.com

Mob:- 8986915333

पत्रांक... 49.12.3130

औरंगाबाद/दिनांक... 24/12/20

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुस्क्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुस्क्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन

24/12/20
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद
(H.M.)
24/12/20

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/AU/AUR/19/0024	Amba nabinagar Road - Chakua	10602802022	3140/22.07.2019	6.5	203.08	122.37	12.05	74MBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3401	25MM	5.041%	0.00000	0.00000	122.37	Comp.
2	RM/AU/AUR/19/0030	Deo - Bahlola	10602802105	3140/22.07.2019	6.52	261.88	130.92	59.68	58MBD-2019-20 04.02.2020	03.11.2020	21.12.2020	3210	25MM	5.012%	0.00000	0.00000	130.92	Comp.
3	RM/AU/AUR/19/0030	GT Rd Deo More - Rasalpur	10602802115	3140/22.07.2019	2.62	92.14	57.95	24.22	58MBD-2019-20 04.02.2020	03.11.2020	17.12.2020	2875	25MM	5.063%	0.00000	0.00000	57.95	Comp.
4	RM/AU/AUR/19/0031	Khairiawan - Bariawan	10602802121	3140/22.07.2019	2.07	76.02	48.85	18.91	61MBD-2019-20 05.02.2020	04.11.2020	17.12.2020	3335	25MM	5.010%	0.00000	0.00000	48.85	Comp.
5	RM/AU/AUR/19/0015	Deo Narayanpur Rd. - Erki	10602802112	3140/22.07.2019	0.82	34.18	23.26	7.33	78MBD-2019-20 20-02-2020	19.11.2020	17.12.2020	2971	25MM	5.010%	0.00000	0.00000	23.26	Comp.
6	RM/AU/AUR/19/0015	Deo Jeevabigha - Eroura	10602902011	3140/22.07.2019	1.56	59.49	39.87	13.60	78MBD-2019-20 20-02-2020	19.11.2020	17.12.2020	3199	25MM	5.014%	0.00000	0.00000	39.87	Comp.
7	RM/AU/AUR/19/0033	AURANGABAD NABINAGAR ROAD - SORI	NEA22000214	3140/22.07.2019	2.2	71.85	44.54	20.04	80MBD-2019-20 20.02.2020	19.11.2020	18.12.2020	2961	25MM	5.080%	0.00000	0.00000	44.54	Comp.
8	RM/AU/AUR/19/0033	Aurangabad Navinagar - Sonbarsa Khaira	10602802096	3140/22.07.2019	1.49	53.57	37.61	15.96	80MBD-2019-20 20.02.2020	19.11.2020	28.11.2020	2988	25MM	5.005%	0.00000	0.00000	37.61	Comp.
9	RM/AU/AUR/19/0034	Aurangabad Navinagar Rd. Charan Vaijaipur Rajpur	10602802097	3140/22.07.2019	4.84	157.38	95.33	9.23	64MBD-2019-20 05.02.2020	04.11.2020	18.12.2020	2404	25MM	5.000%	0.00000	0.00000	95.33	Comp.
10	RM/AU/AUR/19/0034	Charan Mali Road - Sanoura Khamba	10602802103	3140/22.07.2019	2.57	89.38	55.76	24.65	64MBD-2019-20 05.02.2020	04.11.2020	18.12.2020	3012	25MM	5.000%	0.00000	0.00000	55.76	Comp.
11	RM/AU/AUR/19/0010	Khaira to Gram Sonahi Road	10602901035	3140/22.07.2019	2.05	78.8	50.88	19.97	84MBD-2019-20 25.02.2020	24.11.2020	13.11.2020	3549	25MM	5.011%	0.00000	0.00000	50.88	Comp.
12	RM/AU/AUR/19/0018	Khetpura Neura Road - Matihar	10602802063	3140/22.07.2019	0.8	29.96	19.75	7.09	83MBD-2019-20 24.02.2020	23.11.2020	24.12.2020	3230	25MM	5.031%	0.00000	0.00000	19.75	Comp.
13	RM/AU/AUR/19/0027	Basudev Kenal to Tamshi village	10602901031	3140/22.07.2019	2.3	76.08	47.32	20.92	62MBD-2019-20 05.02.2020	04.11.2020	18.12.2020	2934	25MM	5.017%	0.00000	0.00000	47.32	Comp.
14	RM/AU/AUR/19/0027	Amba Jiwa Bigha Road to Choraha	10602901012	3140/22.07.2019	5.5	175.66	109.15	48.86	62MBD-2019-20 05.02.2020	04.11.2020	24.12.2020	3012	25MM	5.093%	0.00000	0.00000	109.15	Comp.

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad

Regisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurangabad

Sl no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative		Agreement Amount		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
15	RM/AU/AUR/19/0036	AURANGABAD NABINAGAR ROAD - SATTAR	NEA22000221	3140/22.07.2019	1.6	56.81	35.7	15.35	68MBD-2019-20 08.02.2020	07.02.2020	28.11.2020	2655	25MM	5.195%	0.00000	0.00000	35.7	Comp.
16	RM/AU/AUR/19/0032	Modernnition & Const of NH-2 Dadpi to deojara Rd via Mahuwan art Rd	10602803009	3140/22.07.2019	6.8	258.417	153.52	63.19	69MBD-2019-20 10.02.2020	09.11.2020	08.12.2020	2770	25MM	5.000%	0.00000	0.00000	153.52	Comp.
17	RM/AU/AUR/19/0028	G.T. Road to Narkappi	10602802400	3140/22.07.2019	4.1	165.66	110.98	37.89	80MBD-2019-20 20.02.2020	19.11.2020	17.12.2020	3016	25MM	5.000%	0.00000	0.00000	110.98	Comp.
18	RM/AU/AUR/19/0009	Nabinagar Road - Kunrwa	10602902029	3140/22.07.2019	3.32	118.96	76.06	30.93	82MBD-2019-20 20.02.2020	19.11.2020	18.12.2020	2986	25MM	5.042%	0.00000	0.00000	76.06	Comp.
19	RM/AU/AUR/19/0028	Const of Rd from Madanpur NH-2 Ghorghat more to Ghorghat thawai Rd	10602801016	3140/22.07.2019	5	246.1	174.29	47.12	65MBD-2019-20 05.02.2020	04.11.2020	17.12.2020	2276	25MM	5.000%	0.00000	0.00000	174.29	Comp.
20	RM/AU/AUR/19/0034	AURANGABAD NABINAGAR ROAD - GHAMHARIA	NEA22000211	3140/22.07.2019	1.6	50.44	31.92	13.36	64MBD-2019-20 05.02.2020	04.11.2020	18.12.20	3103	25MM	5.000%	0.00000	0.00000	31.92	Comp.
21	RM/AU/AUR/19/0024	Const of Rd from Amba Nabinagar to persawan	10602801003	3140/22.07.2019	2.5	88.42	55.36	24.09	74MBD-2019-20 20.02.2020	19.11.2020	24.12.2020	2425	25MM	5.012%	0.00000	0.00000	55.36	Comp.
TOTAL																	1526.47	

Divisional Accounts Officer
Rural Works Department, works Division,
Aurangabad

Executive Engineer
Rural Works Department
Works Division, Aurangabad

Const of Rd from Madanpur NH-2 Ghorghat more to Ghorghat thawai Rd

Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
17/12/20	17:51:0	57	0.1	100	40.4	1000	1268	G	1.87	24.658848	84.579208	Normal
17/12/20	17:51:17	57	0.1	310	20.2	3100	3654	G	4.8	24.659742	84.579377	Normal
17/12/20	17:51:17	57	0.1	270	20.2	2700	3199	G	4.26	24.660675	84.57941	Normal
17/12/20	17:51:52	57	0.1	310	20.2	3100	3654	G	4.8	24.661563	84.579443	Normal
17/12/20	17:52:0	57	0.1	190	10.1	1900	2290	G	3.16	24.662503	84.579325	Normal
17/12/20	17:52:28	57	0.1	310	20.2	3100	3654	G	4.8	24.663342	84.579628	Normal
17/12/20	17:52:28	57	0.1	270	10.1	2700	3199	G	4.26	24.663637	84.58037	Speed Breaker
17/12/20	17:53:3	57	0.1	130	30.3	1300	1609	G	2.31	24.664512	84.580487	Normal
17/12/20	17:53:3	57	0.1	120	40.4	1200	1495	G	2.16	24.665415	84.580538	Normal
17/12/20	17:53:3	57	0.1	110	40.4	1100	1382	G	2.02	24.66638	84.580588	Normal
17/12/20	17:53:3	57	0.1	180	30.3	1800	2177	G	3.02	24.667312	84.58042	Normal
17/12/20	17:53:38	57	0.1	130	30.3	1300	1609	G	2.31	24.668162	84.580268	Normal
17/12/20	17:53:38	57	0.1	190	20.2	1900	2290	G	3.16	24.669062	84.5801	Normal
17/12/20	17:54:0	57	0.1	150	30.3	1500	1836	G	2.6	24.669187	84.57914	Normal
17/12/20	17:54:14	57	0.1	130	40.4	1300	1609	G	2.31	24.669348	84.578113	Normal
17/12/20	17:54:14	57	0.1	100	40.4	1000	1268	G	1.87	24.66961	84.57712	Normal
17/12/20	17:54:14	57	0.1	100	40.4	1000	1268	G	1.87	24.670012	84.576245	Normal
17/12/20	17:54:14	57	0.1	110	40.4	1100	1382	G	2.02	24.670698	84.575605	Normal
17/12/20	17:54:49	57	0.1	140	40.4	1400	1722	G	2.45	24.671537	84.575168	Normal
17/12/20	17:55:0	57	0.1	250	30.3	2500	2972	G	3.99	24.672412	84.574865	Normal
17/12/20	17:55:24	57	0.1	200	20.1	2000	2404	G	3.3	24.673303	84.574393	Normal
17/12/20	17:56:0	57	0.1	180	10.1	1800	2177	G	3.02	24.674162	84.574662	Normal
17/12/20	17:56:0	57	0.1	230	20.2	2300	2745	G	3.72	24.67506	84.575	Normal
17/12/20	17:56:35	57	0.1	190	10.1	1900	2290	G	3.16	24.6759	84.575337	Speed Breaker
17/12/20	17:57:10	57	0.1	250	10.1	2500	2972	G	3.99	24.676787	84.575622	Normal
17/12/20	17:57:10	57	0.1	170	30.3	1700	2063	G	2.88	24.677698	84.575875	Normal
17/12/20	17:57:45	57	0.1	220	10.1	2200	2631	G	3.58	24.678592	84.576027	Normal
17/12/20	17:58:0	57	0.1	220	10.1	2200	2631	G	3.58	24.67955	84.576245	Normal
17/12/20	17:58:21	57	0.1	270	10.1	2700	3199	G	3.26	24.680457	84.576363	Normal
17/12/20	17:58:56	57	0.1	310	10.1	3100	3654	G	3.8	24.681353	84.576463	Normal
17/12/20	17:59:0	57	0.1	140	20.2	1400	1722	G	2.45	24.682225	84.576515	Normal
17/12/20	17:59:0	57	0.1	140	40.4	1400	1722	G	2.45	24.68316	84.57672	Normal
17/12/20	17:59:0	57	0.1	210	30.3	2100	2518	G	3.44	24.683968	84.57638	Normal
17/12/20	17:59:31	57	0.1	120	30.3	1200	1495	G	2.16	24.684737	84.575858	Normal
17/12/20	17:59:31	57	0.1	200	40.4	2000	2404	G	3.3	24.68552	84.575235	Normal
17/12/20	18:0:0	57	0.1	160	30.3	1600	1950	G	2.74	24.686432	84.575185	Normal
17/12/20	18:0:6	57	0.1	120	40.4	1200	1495	G	2.16	24.687253	84.574848	Normal
17/12/20	18:0:6	57	0.1	150	30.3	1500	1836	G	2.6	24.688222	84.574697	Normal

$$Y = 0 * X^2 + 1.136 * X + 132.5$$

$$X = 1888$$

$$Y = 2276$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Ym
29/12/20

17/12/20	18:0:6	57	0.1	160	30.3	1600	1950	G	2.74	24.689128	84.574662	Normal
17/12/20	18:2:28	57	0.1	220	10.1	2200	2631	G	3.58	24.689905	84.574948	Speed Breaker
17/12/20	18:4:0	57	0.1	160	30.3	1600	1950	G	2.74	24.690648	84.57547	Normal
17/12/20	18:4:13	57	0.1	210	10.1	2100	2518	G	3.44	24.691392	84.575842	Normal
17/12/20	18:4:13	57	0.1	110	30.3	1100	1382	G	2.02	24.692277	84.576043	Normal
17/12/20	18:4:13	57	0.1	160	30.3	1600	1950	G	2.74	24.6932	84.576328	Normal
17/12/20	18:4:13	57	0.1	200	10.1	2000	2404	G	3.3	24.694098	84.576615	Normal
17/12/20	18:5:0	57	0.1	200	20.2	2000	2404	G	3.3	24.694893	84.577087	Normal
17/12/20	18:5:0	57	0.1	180	10.1	1800	2177	G	3.02	24.695732	84.577542	Normal
17/12/20	18:5:24	57	0.1	220	20.2	2200	2631	G	3.58	24.696448	84.57808	Normal
17/12/20	18:5:24	57	0.1	230	20.2	2300	2745	G	3.72	24.697375	84.57848	Normal
17/12/20	18:6:0	57	0.1	310	10.1	3100	3654	G	3.8	24.698245	84.578687	Normal
17/12/20	18:7:0	57	0.1									
Total Length			5									

J.E
17/12/2020

A.E
17/12/20

E'E
21/12/2020

Name of Customer : Ram Nandan Singh
 Name of Work/ Road : 1st more to Ghorghat tharwal Rd
 Lab Job number : 57
 Date : 17-12-2020
 Section No. : 57


Test Date : 17-12-2020 Road Name : 1st more to Ghorghat tharwal Rd
 Machine No : 377 Road Type : (R) RURAL ROAD
 Start S No : 447 Side : Madanpur
 Start E No : 496 Interval
 Weather : Normal UIV Range : 268 To 5000 1000 mm/km
 Start Location : 24658848 84' Dist Range : 0 To 51 01 * 1000 m
 End Location : 24698245 84' Equation : $Y = 0 * X^2 + 1.136 * X + 132.5$

Print

Generate Report and Graph

Redraw Graph

Map View

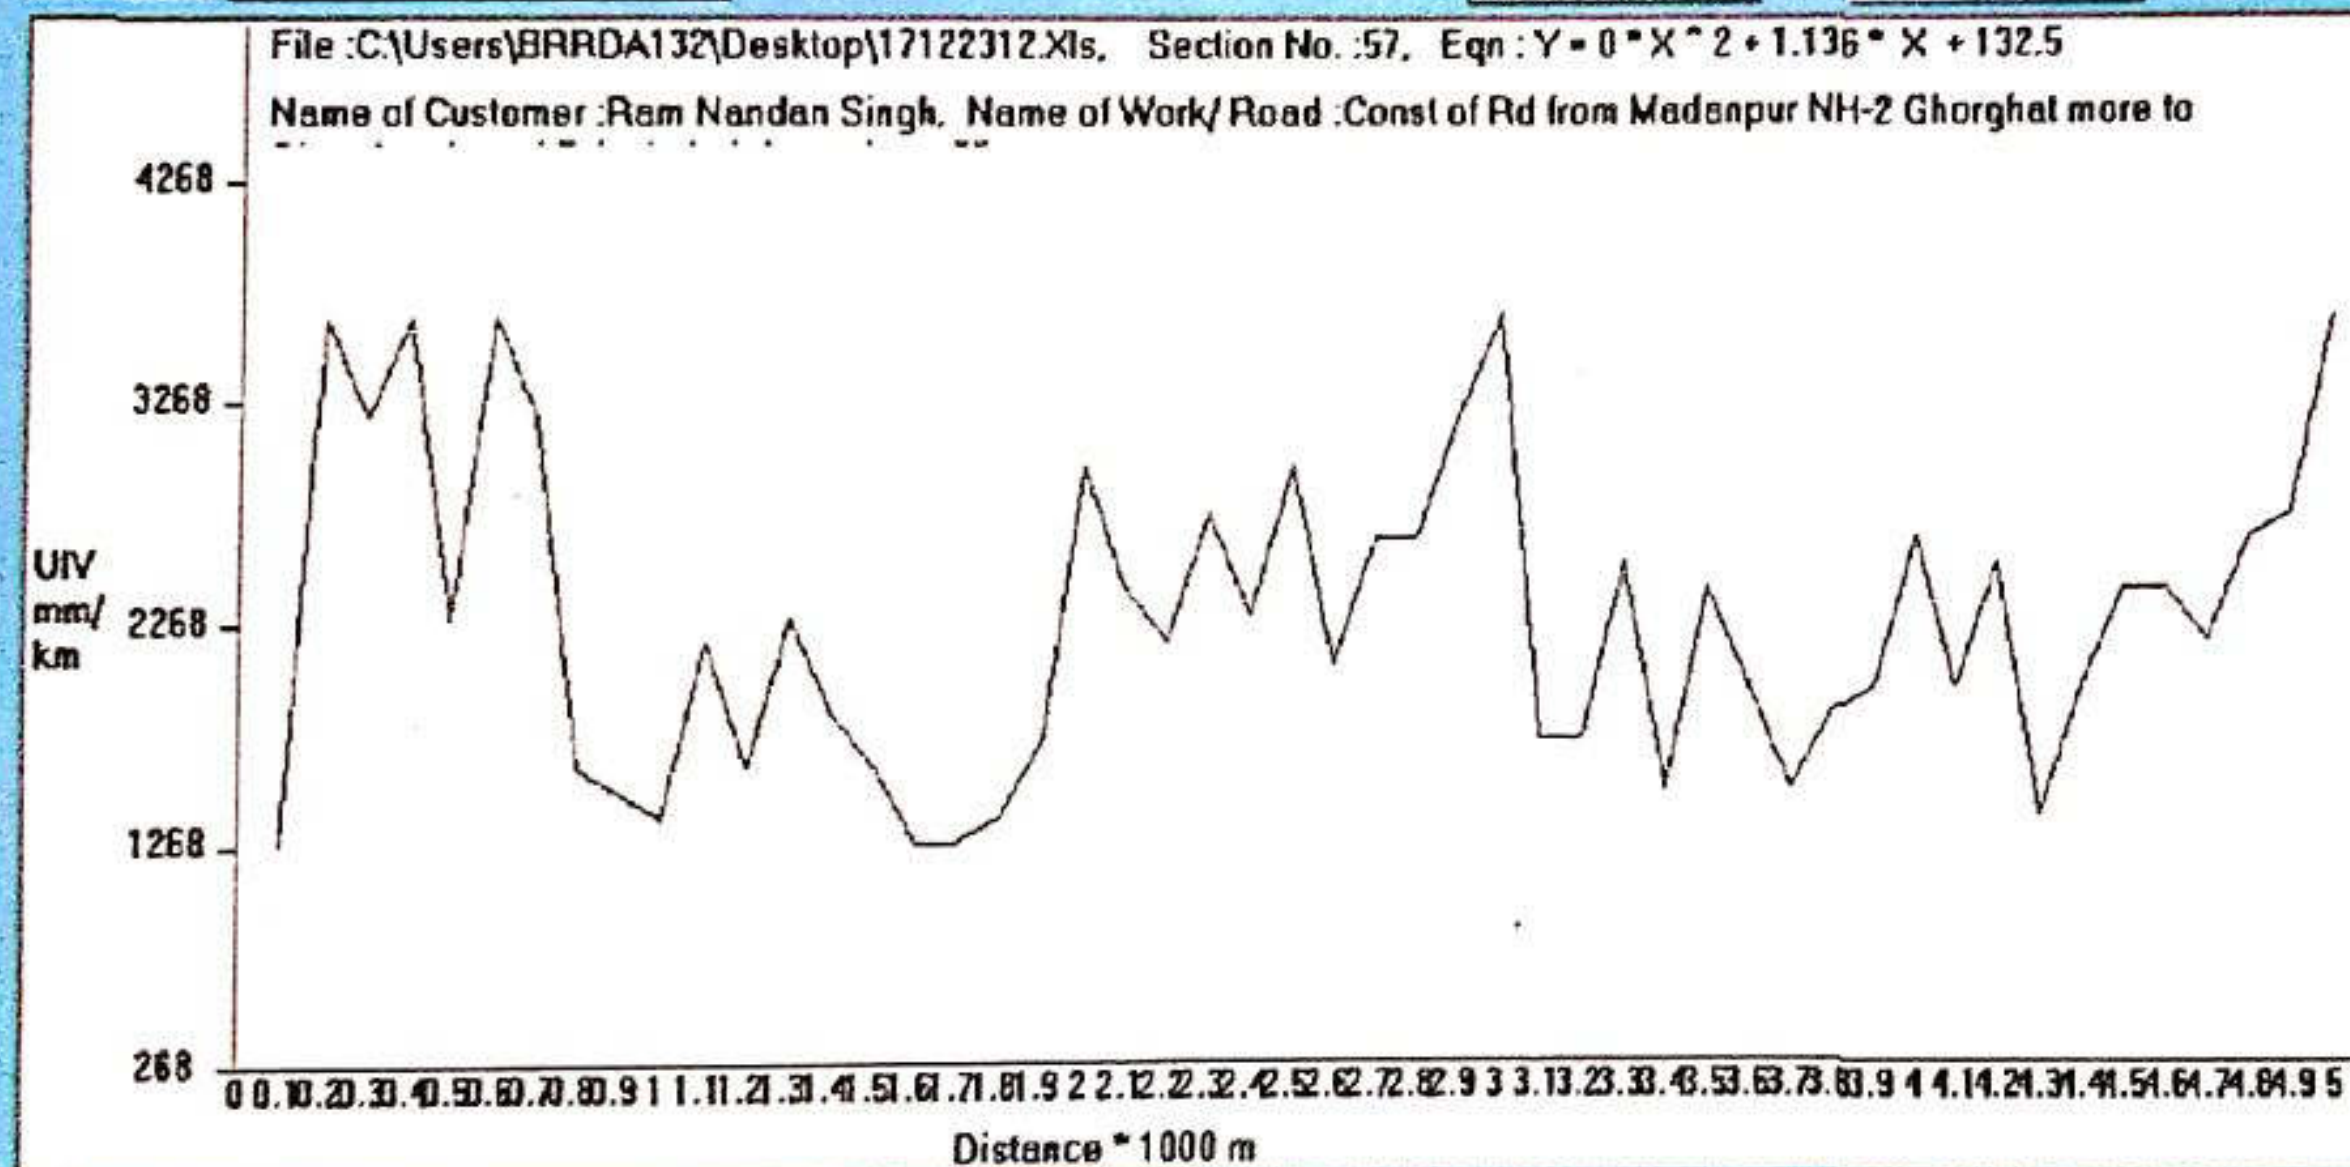

17/12/2020
 JE

17/12/20
 A.E

21/12/20



OM SAI CONSULTANTS

(AN ISO 9001:2015 & ISO/IEC 17025:2017 CERTIFIED NABL ACCREDITED LAB)
Address: - Bank of India Colony, Near 1st Street Gas Godown, South IVSS,
P.O. B.V. College Raja Baroar, Pains-800014, Contact No. 9919472909287
Email- omsaiconsultantspetna@gmail.com

Det. No: OSC/11/2020

TEST REPORT

Issue To:
EXECUTIVE ENGINEER
R.W.D., Works Division,
Aurangabad

Report No: OSC/BR/160620/52

Date of Receiving: 28/11/2020

Testing Period: 28/11/2020 TO 30/11/2020

Date of Reporting: 30/11/2020

Project Name: CONSTRUCTION OF ROAD FROM MADANPUR NH2 TO GORHAT MORE THAWI ROAD

Sample Description Semi Dense Bituminous Concrete (S.D.B.C.)

Sample Condition: Good (Packed in Bag).

BITUMEN CONTENT TEST

S. No.	Test Parameter	Test Method	Result	Requirements MORTH Specification Table- 500-7	Conformity
1.	Binder Content (%)	IRC SP-11	5.08	5.0 Min.	Yes

-----End of Report-----

Checked By

Authorized Signatory

The result listed refers only to the tested samples and applicable parameters endorsement of product is neither inferred nor implied.
Total Liability of our Lab. is limited to the invoiced amount.
Samples will be destroyed after 90 days from the date of issue of test report.
This report is not to be reproduced wholly or in part and cannot be used as an evidence in the court of law and should not be used in any advertising media without our special permission in writing.

NABL ACCREDITED
LABORATORY



OM SAI CONSULTANTS

(AN ISO 9001:2015 & ISO/IEC 17025:2017 CERTIFIED NABL ACCREDITED LAB)
Address: - Bank of India Colony, Near Jai Shree Gas Godown, South D/SS,
P.O.-B.V. College Raju Bazar, Patna-800014, Contact No. +919472909287
Email- omaiconsultantspatna@gmail.com
Det. No. OSC/7.3/7-21

TEST REPORT

Issue To:

EXECUTIVE ENGINEER
R.W.D., Works Division,
Aurangabad

Report No.: OSC/BR/160620/51

Date of Receiving: 28/11/2020

Testing Period: 28/11/2020 TO 28/11/2020

Date of Reporting: 28/11/2020

Project Name: CONSTRUCTION OF ROAD FROM MADANPUR NH2 TO GORHAT MORE THAWI ROAD

Sample Description: Bituminous Macadam (B.M.)

Sample Condition: Good (Packed in Bag).

BITUMEN CONTENT TEST

S. No.	Test Parameter	Test Method	Result	Requirements MORTH Specification Table- 500-7	Conformity
1.	Binder Content (%)	IRC SP-11	3.34	3.3 Min.	Yes

.....End of Report.....

Checked By

Authorized Signatory

The result listed refers only to the tested samples and applicable parameters endorsement of product is neither inferred nor implied.
Total liability of our Lab. is limited to the invoiced amount.
Samples will be destroyed after 90 days from the date of issue of test report.
This report is not to be reproduced wholly or in part and cannot be used as an evidence in the court of law and should not be used in any advertising media without our special permission in writing.

NABL ACCREDITED
LABORATORY
