

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण),

पत्रांक: 2136.अनु0 / चकिया, दिनांक: 28/12/2020

प्रेषक

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, चकिया।

सेवा मे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन पथ के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन पथ का पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0:- 1. आवंटन की सूची
बम्प मशीन रिपोर्ट।

वश्वासभाजन,



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

ज्ञापांक- 2136

दिनांक- 28-12-2020

प्रतिलिपि-नोडल पदाधिकारी (3054), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु0:- 1. आवंटन की सूची


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल-चकिया।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Latter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (in Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20Chakia/04 (RM/EA/CHA/19/0004)	Rampur Korar to Baria Dhekha	31708202043	Latter No.1883 Date- 24.06.2019	10.000	468.38650	296.55269	140.00384	97MBD/2019-20 Date- 23.03.2020	22.12.2020	In Progress	2592.06	25	05.00	0.00000	0.00000	291.25500	Work in Progress
					10.000	468.38650	296.55269	140.00384									291.25500	

- 1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.

(Signature)
DAO

Rural Works Department,
Works Division, Chakia

(Signature)
Executive Engineer,
Rural Works Department,
Works Division, Chakia.

Name of Customer : M/S RUDRA ENTERPRISES
 Name of Work/ Road : RAMPUR KORAR TO BAIRIA DHEKHA
 Lab Job number :
 Date : 23-12-2020
 Section No. : 15

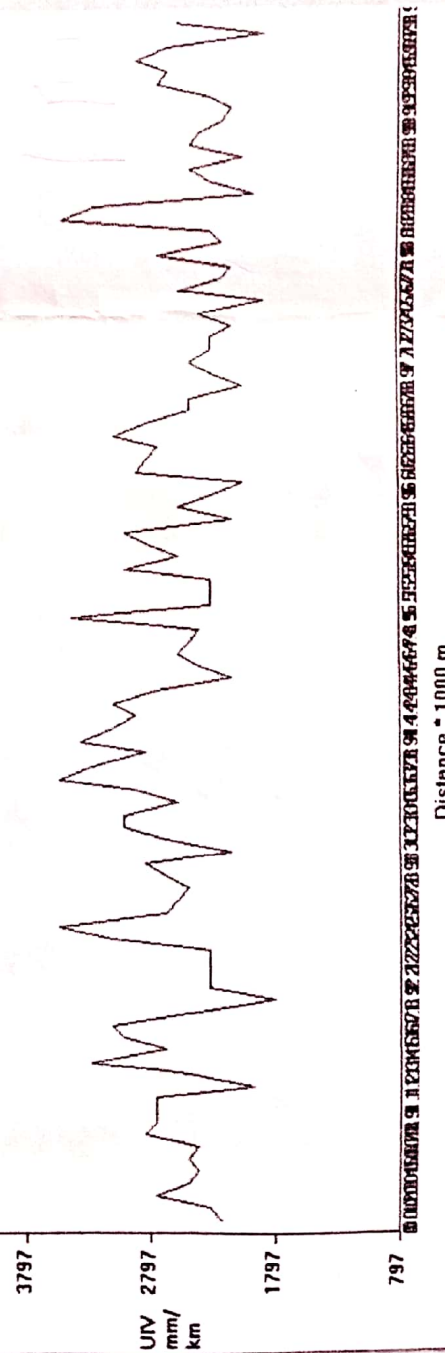
Test Date : 23-12-2020
 Machine No :
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : KORAR TO BAIRIA DHEKHA
 Road Type : (A) ASPHALTIC
 Side :
 UV Range : 797 To 5000
 Dist Range : 0 To 10
 Equation : test
 Interval : 1000 mm/km

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\BRRDA103\Desktop\BUMP INTREGRETOR REPORT\satam singh\23121529 Xls, Section No. : 15,
 Name of Customer : M/S RUDRA ENTERPRISES, Name of Work/ Road : RAMPUR KORAR TO BAIRIA DHEKHA,



Distance * 1000 m

25.12.2020
 0202
 0202

कायपालक अभियंता
 ग्रामीण कार्य विभाग
 कार्य प्रमण्डल,
 02/12/20

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY
ROAD NAME -RAMPUR KORAR TO BAIRIA DHEKHA							
23/12/20	15:1:17	15	0.1	230	0	2300	2231 G
23/12/20	15:2:0	15	0.1	240	10.1	2400	2318 G
23/12/20	15:2:28	15	0.1	290	10.1	2900	2752 G
23/12/20	15:2:28	15	0.1	260	20.2	2600	2492 G
23/12/20	15:3:3	15	0.1	250	20.2	2500	2405 G
23/12/20	15:3:3	15	0.1	260	20.2	2600	2492 G
23/12/20	15:3:38	15	0.1	250	20.2	2500	2405 G
23/12/20	15:4:0	15	0.1	300	20.2	3000	2839 G
23/12/20	15:4:14	15	0.1	290	20.2	2900	2752 G
23/12/20	15:4:14	15	0.1	290	20.2	2900	2752 G
23/12/20	15:4:49	15	0.1	290	10.1	2900	2752 G
23/12/20	15:5:0	15	0.1	200	30.3	2000	1970 G
23/12/20	15:5:0	15	0.1	260	20.2	2600	2492 G
23/12/20	15:5:24	15	0.1	350	20.2	3500	3274 G
23/12/20	15:5:24	15	0.1	280	20.2	2800	2666 G
23/12/20	15:6:0	15	0.1	320	20.2	3200	3013 G
23/12/20	15:6:0	15	0.1	330	10.1	3300	3100 G
23/12/20	15:6:35	15	0.1	250	20.2	2500	2405 G
23/12/20	15:6:35	15	0.1	180	30.3	1800	1797 G
23/12/20	15:7:0	15	0.1	240	20.2	2400	2318 G
23/12/20	15:7:9	15	0.1	240	20.2	2400	2318 G
23/12/20	15:7:9	15	0.1	240	20.2	2400	2318 G
23/12/20	15:7:44	15	0.1	240	20.2	2400	2318 G
23/12/20	15:8:20	15	0.1	430	10.1	3300	3100 G
23/12/20	15:9:0	15	0.1	380	10.1	3800	3535 G
23/12/20	15:9:0	15	0.1	280	20.2	2800	2666 G
23/12/20	15:9:30	15	0.1	270	20.2	2700	2579 G
23/12/20	15:9:30	15	0.1	260	10.1	2600	2492 G
23/12/20	15:10:5	15	0.1	280	10.1	2800	2666 G
23/12/20	15:10:5	15	0.1	300	20.2	3000	2839 G
23/12/20	15:10:41	15	0.1	220	30.3	2200	2144 G
23/12/20	15:11:0	15	0.1	280	10.1	2800	2666 G
23/12/20	15:11:16	15	0.1	320	10.1	3200	3013 G
23/12/20	15:11:16	15	0.1	320	10.1	3200	3013 G
23/12/20	15:12:0	15	0.1	270	20.2	2700	2579 G
23/12/20	15:12:0	15	0.1	310	20.2	3100	2926 G
23/12/20	15:12:27	15	0.1	380	20.2	3800	3535 G

$$Y = 0 * X^2 + 0.869 * X + 232.9$$

$$X = 2111$$

$$Y = 2067$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Green 25.12.20

23/12/20

Handwritten notes at the top of the page, including "2020" and "2021" written diagonally, and "2020" written horizontally.

23/12/20 15:12:27	15	0.1	450	20.2	3500	3274 A	26.34363	84.8132	Normal
23/12/20 15:13:2	15	0.1	300	20.2	3000	2839 G	26.34335	84.81409	Normal
23/12/20 15:13:2	15	0.1	360	10.1	3600	3361 G	26.34334	84.81513	Normal
23/12/20 15:13:37	15	0.1	330	20.2	3300	3100 G	26.34342	84.81613	Normal
23/12/20 15:14:0	15	0.1	310	20.2	3100	2926 G	26.34344	84.8171	Normal
23/12/20 15:14:12	15	0.1	330	30.3	3300	3100 G	26.34355	84.81811	Normal
23/12/20 15:14:12	15	0.1	290	20.2	2900	2752 G	26.34359	84.81909	Normal
23/12/20 15:14:12	15	0.1	220	20.2	2200	2144 G	26.34385	84.82008	Normal
23/12/20 15:14:48	15	0.1	250	30.3	2500	2405 G	26.34402	84.82109	Normal
23/12/20 15:15:0	15	0.1	270	30.3	2700	2579 G	26.34416	84.82209	Normal
23/12/20 15:15:0	15	0.1	260	20.2	2600	2492 G	26.34434	84.82308	Normal
23/12/20 15:15:23	15	0.1	250	20.2	2500	2405 G	26.3443	84.82412	Normal
23/12/20 15:15:23	15	0.1	370	10.1	3700	3448 G	26.34428	84.82502	Normal
23/12/20 15:16:0	15	0.1	240	30.3	2400	2318 G	26.34375	84.82588	Normal
23/12/20 15:16:0	15	0.1	240	20.2	2400	2318 G	26.34346	84.82682	Normal
23/12/20 15:16:34	15	0.1	240	20.2	2400	2318 G	26.34315	84.82779	Normal
23/12/20 15:16:34	15	0.1	320	20.2	3200	3013 G	26.34285	84.82874	Normal
23/12/20 15:17:0	15	0.1	270	20.2	2700	2579 G	26.34257	84.82971	Normal
23/12/20 15:17:9	15	0.1	300	20.2	3000	2839 G	26.34222	84.83062	Normal
23/12/20 15:17:9	15	0.1	320	10.1	3200	3013 G	26.34177	84.83145	Normal
23/12/20 15:17:44	15	0.1	220	20.2	2200	2144 G	26.34119	84.83229	Normal
23/12/20 15:18:0	15	0.1	270	10.1	2700	2579 G	26.34067	84.83204	Normal
23/12/20 15:18:19	15	0.1	240	20.2	2400	2318 G	26.34012	84.83118	Normal
23/12/20 15:18:19	15	0.1	210	20.2	2100	2057 G	26.33962	84.83035	Normal
23/12/20 15:19:0	15	0.1	310	10.1	3100	2926 G	26.33888	84.82981	Normal
23/12/20 15:19:30	15	0.1	300	10.1	3000	2839 G	26.33836	84.83052	Normal
23/12/20 15:19:30	15	0.1	290	20.2	2900	2752 G	26.33748	84.83076	Normal
23/12/20 15:20:5	15	0.1	330	10.1	3300	3100 G	26.33664	84.83039	Normal
23/12/20 15:20:5	15	0.1	300	20.2	3000	2839 G	26.33594	84.82988	Normal
23/12/20 15:20:40	15	0.1	260	10.1	2600	2492 G	26.33506	84.82978	Normal
23/12/20 15:21:0	15	0.1	260	20.2	2600	2492 G	26.33425	84.83015	Normal
23/12/20 15:21:16	15	0.1	210	20.2	2100	2057 G	26.33371	84.83093	Normal
23/12/20 15:21:16	15	0.1	240	20.2	2400	2318 G	26.33302	84.83145	Normal
23/12/20 15:21:51	15	0.1	260	20.2	2600	2492 G	26.33227	84.83082	Normal
23/12/20 15:22:0	15	0.1	240	20.2	2400	2318 G	26.33148	84.83037	Normal
23/12/20 15:22:0	15	0.1	240	20.2	2400	2318 G	26.33067	84.82988	Normal
23/12/20 15:22:26	15	0.1	220	30.3	2200	2144 G	26.32997	84.82923	Normal
23/12/20 15:22:26	15	0.1	250	10.1	2500	2405 G	26.32923	84.8286	Normal
23/12/20 15:23:2	15	0.1	190	10.1	1900	1883 G	26.32844	84.82825	Normal
23/12/20 15:23:37	15	0.1	270	20.2	2700	2579 G	26.32759	84.82793	Normal

23/12/20 15:23:37	15	0.1	230	20.2	2300	2231 G	26.32673	84.82766	Normal
23/12/20 15:24:0	15	0.1	220	20.2	2200	2144 G	26.32585	84.82734	Normal
23/12/20 15:24:12	15	0.1	290	20.2	2900	2752 G	26.32496	84.8271	Normal
23/12/20 15:24:12	15	0.1	230	20.2	2300	2231 G	26.32418	84.82749	Normal
23/12/20 15:24:47	15	0.1	240	30.3	2400	2318 G	26.32324	84.82751	Normal
23/12/20 15:25:0	15	0.1	410	10.1	3800	3535 G	26.3224	84.82714	Normal
23/12/20 15:25:23	15	0.1	420	20.2	3500	3274 G	26.32153	84.82684	Normal
23/12/20 15:25:23	15	0.1	200	20.2	2000	1970 G	26.32064	84.82685	Normal
23/12/20 15:25:23	15	0.1	240	20.2	2400	2318 G	26.31976	84.82702	Normal
23/12/20 15:26:0	15	0.1	260	10.1	2600	2492 G	26.31883	84.82717	Normal
23/12/20 15:26:0	15	0.1	210	20.2	2100	2057 G	26.31799	84.82732	Normal
23/12/20 15:26:33	15	0.1	260	20.2	2600	2492 G	26.31708	84.82746	Normal
23/12/20 15:26:33	15	0.1	250	20.2	2500	2405 G	26.31614	84.82763	Normal
23/12/20 15:27:0	15	0.1	230	30.3	2300	2231 G	26.31526	84.82783	Normal
23/12/20 15:27:9	15	0.1	220	30.3	2200	2144 G	26.31439	84.82801	Normal
23/12/20 15:27:9	15	0.1	240	20.2	2400	2318 G	26.31362	84.82848	Normal
23/12/20 15:27:44	15	0.1	290	20.2	2900	2752 G	26.31306	84.82933	Normal
23/12/20 15:28:0	15	0.1	280	20.2	2800	2666 G	26.31255	84.8301	Normal
23/12/20 15:28:19	15	0.1	310	20.2	3100	2926 G	26.31189	84.83051	Normal
23/12/20 15:28:19	15	0.1	280	20.2	2800	2666 G	26.31171	84.83152	Normal
23/12/20 15:28:19	15	0.1	190	20.2	1900	1883 G	26.31143	84.83251	Normal
23/12/20 15:29:0	15	0.055	150	30.3	2727	2602 G	26.31129	84.83308	Normal
					TOTAL	256614			
					AVERAGE	2592.06			

25.12.2020
FIF

25/12/20
