

12

Inspection Report for Flood Damage Work

Date:

1. Name of PIUs RWD, works Division, Gopalganj - 2
2. Name of Block/Road - Sihwalia / Jhajhwa Brauli PMHSY Sadak to Dhekahi Lohijara Bazar

A. For Road


1. Damage Location/Chainage : 100M | 140M | 170M
2. Damage Length : 8.0M | 50.0M | 30.0M
3. Nature of Damage : Road wash out
4. Details of Restoration Works :
 - i. Material being used in Restoration works : Brick bats
 - ii. Equipments/Tools being used in Restoration works : JCB Tractor with Trolley
 - iii. Procedure taken up in Restoration works :
 - iv. Restored Length : 88.0M

B. For Bridge

1. Damage Location/Chainage : | NA
2. Damage Length : | NA
3. Nature of Damage : | NA
4. Details of Restoration Works :
 - i. Material being used in Restoration works : | NA
 - ii. Equipments/Tools being used in Restoration works : | NA
 - iii. Procedure taken up in Restoration works : | NA
 - iv. Restored Length : | NA


JE


AE


EE


Signature
Executive Engineer
(Name of Inspector)
Hathua

Report.

Name of work :- Jhajhawa Barauli PMGSY Sadak to
Dhekahi Lohijara Bazar


Estimated Cost :- 1001360.00


Total length of road :- 2.805 KM


Description :- The present estimate has been framed under the supervision of Assistant engineer in accordance with the order of Executive Engineer , RWD , WD Gopalganj-2 , letter no – 1574 dated 18-08-2020. The part of above mentioned road has been damaged due to heavy rain/flood. And due to this damage the transportation has been obstructed . The immediate motorable work is necessary in public interest . Villagers will be benefitted by the completion of this motorable work.

In the estimate there has been a provision of repairing the damaged part of the road & making it motorable by filling brickbats . In the context of post flood scenario there is still the flow of water which prevails through the damaged part of road . This provision has a purpose to put a check on the erosion of embankment of road .

In this estimate the rate of raw materials and labour wages has been prepared after the analysis of new rate. This estimate is as per the specifications. The estimate is devoted to technical and administrative acceptance.


18-09-20
J.E.


18/09/20
A.E.


18/9/20
E.E.

Sr.	Items	no.	L (M.)	W M.)	D (M.)	Qty.	unit	rate	Amount
1	Providing brick bats billed in ditches including all cost of Labour & Material with all complete job .								
	CH- 100 M	1	8.00	3.50	0.60	16.80	M ³		
	CH-1400 M								
	Ditch	1	18.00	4.50	1.00	81.00	M ³		
	Embankment	1	18.00	4.50+3.50/2	1.00	93.60	M ³		
		2	16.00	3.50	1.00	112.00	M ³		
	CH-1700 M	1	30.00	3.50	1.00	105.00	M ³	2412.11	985106.20
						408.40		2427.65	991452.26
	Add 1% contingency								9914.52 98512
									7949.57
							Total		1001366.78
							Say		1001360.00

~~18-09-20~~
JE

AE

18/9/20
EE

Technically Approved for Rs 9.95 Lacs (Rupees Nine Lacs Ninety Five Thousand) only

अधीक्षण अभियंता
प्रमोद कुमार शिवाजी कर्म अंतर्गत मिशन

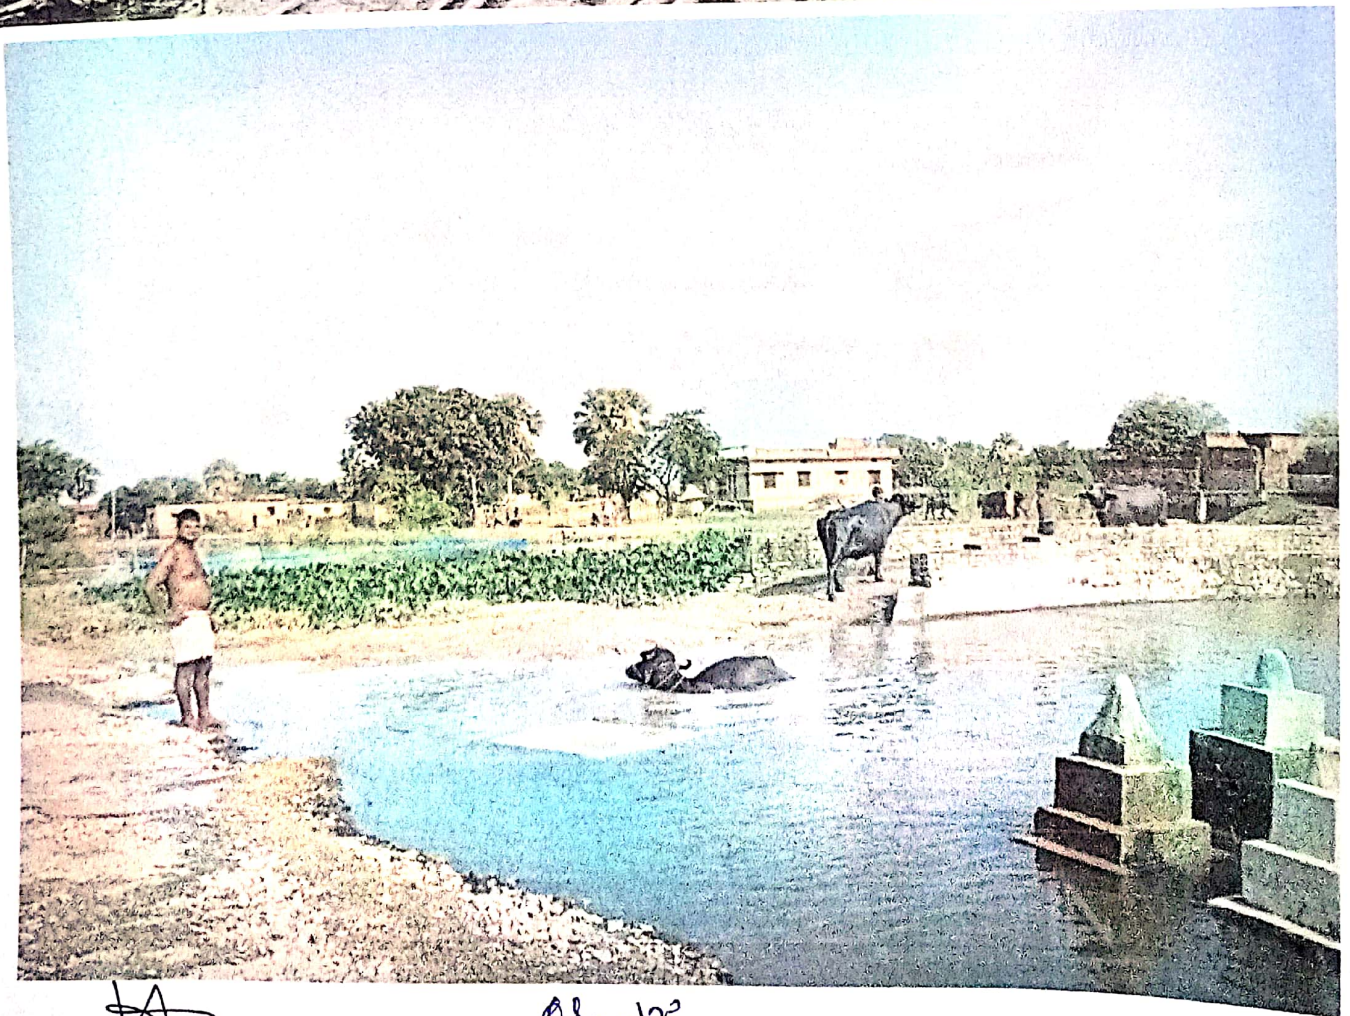
Jhajhawa Barauli PMGSY Sadak to Dhekahi Lohijara Bazar



~~18-09-20~~
18

18/09/20
AE

Shajhawa Barauli PMGSY Sadak to Dhekahi Lohijara Bazar



~~18-09-20~~
18-09-20
or

~~18/09/20~~
18/09/20
AC
