


Name of Customer : M/S Saraswati Construction
 Name of Work/ Road : Aare Sasaram Road Sanjhauli
 Lab Job number : 53
 Date : 07-11-2020
 Section No. : 53

Test Date : 07-11-2020
 Road Name : Aare Sasaram Road Sanjhauli
 Machine No : 405
 Road Type : (R) RURAL ROAD
 Start S No : 1535
 Side : Sanjhauli
 Start E No : 1569
 Interval :
 Weather : Normal
 UV Range : 584 To 4000 mm/km
 Start Location : 25.18147, 84.1
 Dist Range : 0 To 1.008 0.028 * 1000 m
 End Location : 25.21155, 84.1
 Equation : $Y = 0 * X^2 + 0.877 * X + 181.3$

Print Generate Report and Graph

Redraw Graph

Map View

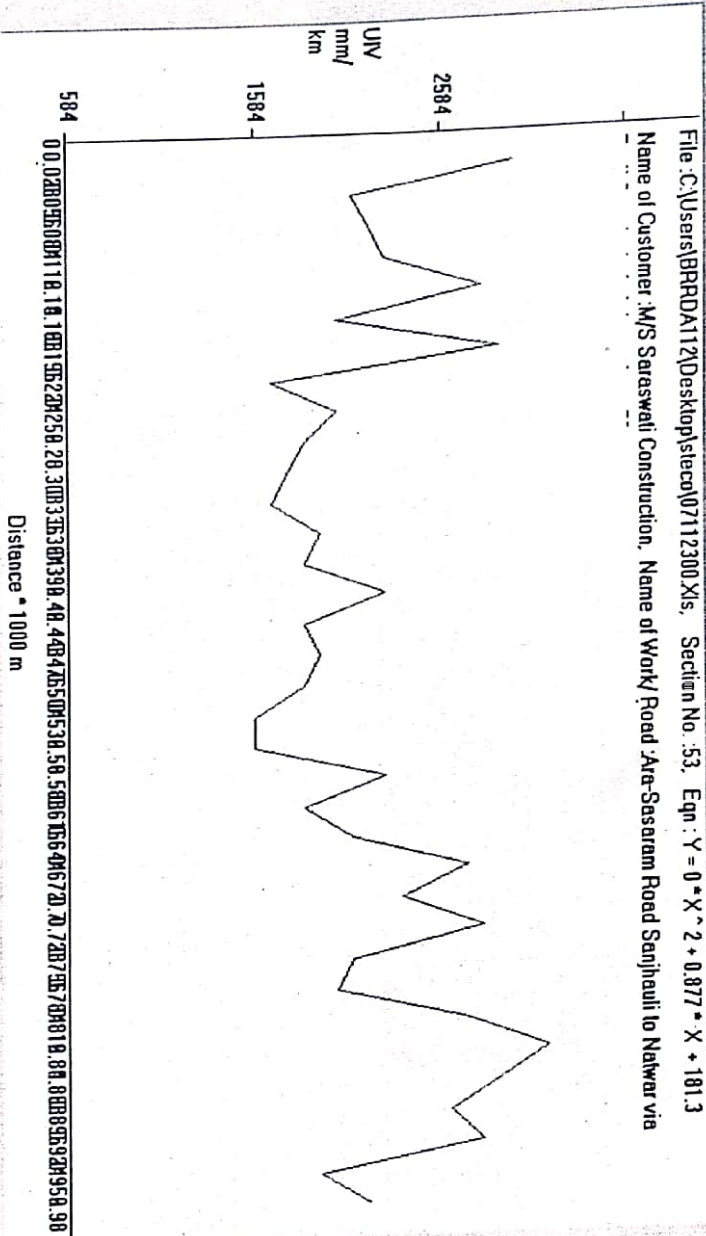

24/5
 22/11/20

Name of Road - Ara-Sasaram Road Sanjhauti to Natwar via Badli Canal

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEG ORY	Latitude	Longitude	Event
		No.									
7/11/20	17:35:25	53	0.1	320	30.3	3200	2987	G	25.18147	84.189057	Normal
7/11/20	17:35:25	53	0.1	220	40.4	2200	2110	G	25.182282	84.188872	Normal
7/11/20	17:35:25	53	0.1	230	50.5	2300	2198	G	25.183168	84.188635	Normal
7/11/20	17:35:25	53	0.1	240	40.4	2400	2286	G	25.184085	84.18842	Normal
7/11/20	17:36:1	53	0.1	300	20.2	3000	2812	G	25.185053	84.188182	Normal
7/11/20	17:36:1	53	0.1	210	30.3	2100	2023	G	25.185963	84.187978	Normal
7/11/20	17:36:1	53	0.1	310	50.5	3100	2900	G	25.186772	84.187777	Normal
7/11/20	17:36:1	53	0.1	170	50.5	1700	1672	G	25.18772	84.187558	Normal
7/11/20	17:36:1	53	0.1	210	60.6	2100	2023	G	25.188597	84.18734	Normal
7/11/20	17:36:36	53	0.1	190	60.6	1900	1847	G	25.18948	84.187137	Normal
7/11/20	17:36:36	53	0.1	180	60.6	1800	1759	G	25.1903	84.186918	Normal
7/11/20	17:36:36	53	0.1	170	60.6	1700	1672	G	25.191328	84.18668	Normal
7/11/20	17:37:0	53	0.1	200	60.6	2000	1935	G	25.192203	84.18648	Normal
7/11/20	17:37:0	53	0.1	190	40.4	1900	1847	G	25.193168	84.186245	Normal
7/11/20	17:37:10	53	0.1	240	50.5	2400	2286	G	25.194012	84.186043	Normal
7/11/20	17:37:10	53	0.1	190	50.5	1900	1847	G	25.194842	84.185842	Normal
7/11/20	17:37:10	53	0.1	200	60.6	2000	1935	G	25.195852	84.185605	Normal
7/11/20	17:37:10	53	0.1	190	60.6	1900	1847	G	25.196727	84.185403	Normal
7/11/20	17:37:10	53	0.1	160	60.6	1600	1584	G	25.19748	84.185218	Normal
7/11/20	17:37:10	53	0.1	160	70.7	1600	1584	G	25.198403	84.184998	Normal
7/11/20	17:37:45	53	0.1	240	60.6	2400	2286	G	25.199305	84.18478	Normal
7/11/20	17:37:45	53	0.1	190	60.6	1900	1847	G	25.200238	84.184562	Normal
7/11/20	17:38:0	53	0.1	220	60.6	2200	2110	G	25.201185	84.184325	Normal
7/11/20	17:38:0	53	0.1	290	50.5	2900	2724	G	25.202118	84.184123	Normal
7/11/20	17:38:21	53	0.1	250	10.1	2500	2373	G	25.203047	84.183872	Normal
7/11/20	17:38:21	53	0.1	300	30.3	3000	2812	G	25.203843	84.183687	Normal
7/11/20	17:38:21	53	0.1	220	40.4	2200	2110	G	25.20473	84.18347	Normal
7/11/20	17:39:0	53	0.1	210	50.5	2100	2023	G	25.20571	84.183248	Normal
7/11/20	17:39:0	53	0.1	290	20.2	2900	2724	G	25.206135	84.182508	Normal
7/11/20	17:39:0	53	0.1	340	30.3	3400	3163	G	25.206358	84.181447	Curve
7/11/20	17:39:31	53	0.1	310	10.1	3100	2900	G	25.206152	84.180588	Normal
7/11/20	17:39:31	53	0.1	280	20.2	2800	2636	G	25.206157	84.180555	Normal
7/11/20	17:39:31	53	0.1	300	20.2	3000	2812	G	25.207842	84.182407	Normal
7/11/20	17:40:31	53	0.1	200	30.3	2000	1935	G	25.209693	84.167592	Normal
7/11/20	17:40:31	53	0.1	230	30.3	2300	2198	G	25.211545	84.169443	Normal
Total Length			3.50								

$$Y = 0 * X^2 + 0.877 * X + 181.3$$

$$X = 2157$$

$$Y = 2072$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

CP5
Rethillan

कार्यालय
कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बिक्रमगंज (रोहतास)।

पत्रांक.....1445-3137 बिक्रमगंज / दिनांक.....19.11.20

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।

सेवा में,

नोडल पदाधिकारी, (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:— नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनुलग्नक:—यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।

Requisition Format for Scheme Head- MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Bikramganj

Sl. No.	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter no. & DT.	Administrative Approval		Agreement Amount (in Lakhs)			Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakhs)	Up-to - Date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (In Lakhs)	Amount of (In Lakhs)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	MR-N/19-20 Bikramgani/1 1	Satempur Chiksil Pwd Road - Turti (L030)	10301002142	3054-04- 139/2019- 6282 DT- 02.12.2019	2.37	106.446	87.89790	24.32348	16MBD/202 0-21 Dt.- 30.06.2020	23.03.2021	-	2547.166	25	5%	0.00	0.00	87.89700		Work in progress
	MR-N/19-20 Bikramgani/1 1	Ghusia Kala Station to Kajhrain (Phase-I)	10301002347	3054-04- 139/2019- 6282 DT- 02.12.2019	1.25	56.641	39.54079	13.91657	16MBD/202 0-21 Dt.- 30.06.2020	23.03.2021	-	2760.75	25	5%	0.00	0.00	39.54000		Work in progress
3	MR-N/19-20 Bikramgani/1 1	Badi Canal to Bageya Path	10301002061	3054-04- 139/2019- 2065 DT- 04.07.2019	1.40	53.609	27.46091	12.80695	66/MBD/ 2019-20 20.03.2020	29.10.2020	-	2642.71	25	5%	0.00	0.00	27.46000		Work in progress
4	MR-N/19-20 Bikramgani/1 1	Ara Sasaram Path (Sanjhauli) to Natwar Via Baci Canal	10301002054	3054-04- 139/2019- 2065 DT- 04.07.2019	3.50	184.498	119.64381	33.54614	66/MBD/ 2019-20 20.03.2020	29.10.2020	-	2223.05	25	5%	0.00	0.00	119.64000		Work in progress
Total:-					8.52	401.194	274.54941	84.59324				10173.676			0.00	0.00	274.53700		

1 Signed Hard Copy and Soft Copy (in excel) of Recorded IRI is enclosed.

2 UP- to date Physical Progress has been Uploaded in MIS.


Executive Engineer
RWD, Works Div. Bikramganj
