

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सासाराम-2

पत्रांक...३२२(३५५)...

सासाराम 2/दिनांक...२७/११/२०...

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सासाराम-2

सेवामें,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु० :- यथोक्त।

विष्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सासाराम-2


Name of Customer :
 Name of Work/ Road :
 Lab Job number :
 Date :
 Section No. :

Test Date :
 Machine No :
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name :
 Road Type :
 Side :
 UIV Range : To
 Dist Range : To
 Equation :
 Interval : mm/km

Print Generate Report and Graph

Redraw Graph

Map View

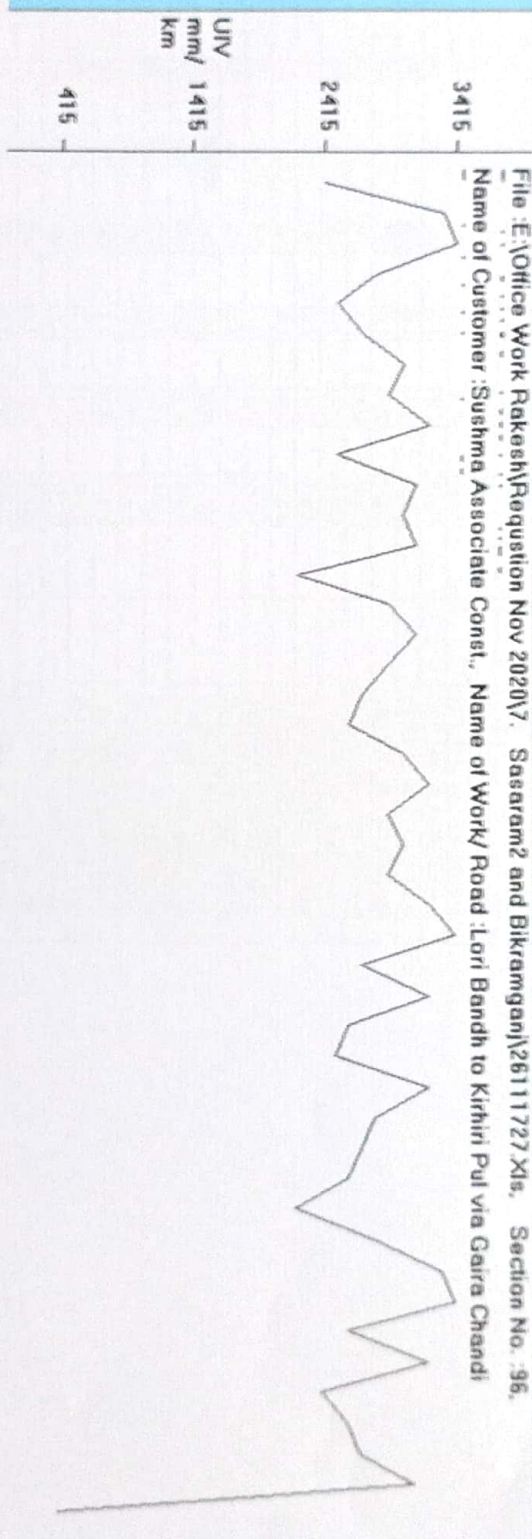

26/11/20
 27/11/20

Name of Road : Karup - Lori Bandh to Kirhri pul via Gaira Chandl Toia

Date	Time	No.	Section	Length in km	Bumps in mm	Speed Rate	OR	IRI	TEGORY		Latitude	ongitude	Event
26/11/20	14:26:0	96	0.1	200	0	2000	2415 G				25.1426	84.30576	Normal
26/11/20	14:26:33	96	0.1	290	20.2	2900	3315 G				25.14291	84.30675	Normal
26/11/20	14:27:8	96	0.1	300	10.1	3000	3415 G				25.14334	84.30759	Normal
26/11/20	14:27:43	96	0.1	240	10.1	2400	2815 G				25.14399	84.30833	Normal
26/11/20	14:28:0	96	0.1	210	10.1	2100	2515 G				25.1446	84.30906	Normal
26/11/20	14:28:19	96	0.1	260	10.1	2600	3015 G				25.14462	84.31082	Normal
26/11/20	14:29:0	96	0.1	250	10.1	2500	2915 G				25.1448	84.31178	Normal
26/11/20	14:29:0	96	0.1	280	10.1	2800	3215 G				25.14536	84.31258	Normal
26/11/20	14:30:0	96	0.1	210	10.1	2100	2515 G				25.1459	84.31338	Normal
26/11/20	14:30:40	96	0.1	270	0	2700	3115 G				25.14664	84.31384	Normal
26/11/20	14:31:0	96	0.1	260	10.1	2600	3015 G				25.14747	84.31428	Normal
26/11/20	14:31:15	96	0.1	270	10.1	2700	3115 G				25.14823	84.3148	Normal
26/11/20	14:31:15	96	0.1	180	10.1	1800	2215 G				25.14902	84.31527	Normal
26/11/20	14:32:0	96	0.1	250	10.1	2500	2915 G				25.14989	84.31562	Normal
26/11/20	14:32:26	96	0.1	270	10.1	2700	3115 G				25.15062	84.31621	Normal
26/11/20	14:33:1	96	0.1	250	10.1	2500	2915 G				25.15134	84.31684	Normal
26/11/20	14:33:1	96	0.1	230	10.1	2300	2715 G				25.15218	84.31722	Normal
26/11/20	14:33:36	96	0.1	220	10.1	2200	2615 G				25.153	84.31705	Normal
26/11/20	14:34:11	96	0.1	260	10.1	2600	3015 G				25.15375	84.31652	Normal
26/11/20	14:34:11	96	0.1	280	10.1	2800	3215 G				25.15461	84.31687	Normal
26/11/20	14:34:47	96	0.1	250	10.1	2500	2915 G				25.15544	84.31702	Normal
26/11/20	14:35:0	96	0.1	260	10.1	2600	3015 G				25.15639	84.31724	Normal
26/11/20	14:35:22	96	0.1	250	10.1	2500	2915 G				25.1563	84.31793	Normal
26/11/20	14:36:0	96	0.1	280	10.1	2800	3215 G				25.15563	84.31862	Normal
26/11/20	14:36:0	96	0.1	300	10.1	3000	3415 G				25.15539	84.31955	Normal
26/11/20	14:36:33	96	0.1	230	10.1	2300	2715 G				25.15522	84.32052	Normal
26/11/20	14:37:8	96	0.1	280	10.1	2800	3215 G				25.15508	84.32153	Normal
26/11/20	14:37:8	96	0.1	220	10.1	2200	2615 G				25.15523	84.32242	Normal
26/11/20	14:37:43	96	0.1	210	20.2	2100	2515 G				25.15512	84.32343	Normal
26/11/20	14:38:0	96	0.1	280	10.1	2800	3215 G				25.15525	84.32441	Normal
26/11/20	14:38:18	96	0.1	240	10.1	2400	2815 G				25.15509	84.3254	Normal
26/11/20	14:39:0	96	0.1	230	10.1	2300	2715 G				25.15514	84.3264	Normal
26/11/20	14:40:4	96	0.1	180	11.3	1800	2215 G				25.15498	84.32739	Normal
26/11/20	14:41:0	96	0.1	240	12.3	2400	2815 G				25.1546	84.32825	Normal
26/11/20	14:41:50	96	0.1	290	10.4	2900	3315 G				25.155	84.32981	Normal
26/11/20	14:43:1	96	0.1	300	13.1	3000	3415 G				25.15572	84.33029	Normal
26/11/20	14:44:47	96	0.1	220	10.2	2200	2615 G				25.15651	84.33074	Normal
26/11/20	14:45:22	96	0.1	280	10.5	2800	3215 G				25.15728	84.3313	Normal
26/11/20	14:46:0	96	0.1	200	11.2	2000	2415 G				25.15802	84.33178	Normal
26/11/20	14:47:0	96	0.1	220	10.1	2200	2615 G				25.15752	84.33261	Normal
26/11/20	14:47:8	96	0.1	230	10.1	2300	2715 G				25.15716	84.33352	Normal
26/11/20	14:48:0	96	0.1	270	12.4	2700	3115 G				25.15669	84.33439	Normal
26/11/20	14:49:29	96	0.1	250	13.1	2500	2915 G				25.1563	84.33512	Normal
26/11/20	14:49:55	96	0.1	230	12.2	2300	2615 G				25.1573	84.33569	Normal
26/11/20	14:49:29	96	0.1	280	10.1	2400	2625 G				25.1579	84.33622	Normal
Total				4.7									

$$Y = 0.0 * X^2 + 1.000 * X + 415.2$$

$$X = 2400$$

$$Y = 2625$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

28/08/20
25/08/20

OFFICE OF THE EXECUTIVE ENGINEER

Regional Laboratory R.W.D, Sasaram

Second Tier Quality Control report

PHYSICAL AND GRADATION TEST COURSE AGGREGATE

Name of Road:- Lori bandh to Kirhini pul via gairachauli Road.

Name of Scheme :- MR(3054)

Name Of Agency:- Sushma Associates pvt. Ltd

Nature Of Sample:- SDBC-StoneChips-Gr-II

Location:- CH. 2.500 Km. Date Of Collection/ Recevied in Lab → 25/11/20

Sample collected :- AE R.W.D Works Sub Division Karakat Date Of Test → 26/11/20

Agreement No./Packege no.:- Letter No- 01 Comp Date - 25/11/20

Sl. No.	A.I.V.		Water Absorption		Remark
	Test Value	Required Value (Max)	Test Value	Required Value (Max) §	
	✓	✓	✓	✓	✓

Sl No.	Slewer Size in mm	Weight Of Sample Taken 7.731 Kg					Remark
		Weight Retained	%of wt. Retained	% of cumulative retained	% wt of Wt. Passing	Required value	
1.	13.2	0.0	0.0	0.0	100	100	Permissible
2.	9.5	0.530	6.85	6.85	93.15	90-100	
3.	4.75	4.396	56.85	63.70	36.30	35-51	
4.	2.36	0.779	10.07	73.77	26.23	24-39	
5.	1.18	0.614	7.93	81.70	18.30	15-30	
6.	0.30	0.398	5.14	86.84	13.16	9-19	
7.	0.075	0.702	9.08	95.92	4.08	3-8	
8.		✓	✓	✓	✓	✓	

26/11/20

L.A

Regional laboratory
R.W.D.,sasaram

26/11/20
E.E.

Regional laboratory-
R.W.D.,sasaram

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY R.W.D SASARAM

Bituminous mix

Name of Project/Road :- Levi Bandh to Kithuri pul via gaira chaudi Road

Name of Scheme :- MR (3054)

Name of Agency :-

Sushma Associates Pvt-Ltd

Nature of sample :-

SDBC. Bitumin Content

Location :-

Date of Collection/Received :- 25/11/20

Date of Test :- 26/11/20

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Karakat vide letter No. 01 Comp Dt. 25/11/20

Agreement No / Package No. :

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	502.41	507.20	501.61	Permissible
2	Wt. of Dry chips after extraction (b)	477.21	481.63	476.32	
3	Percentage of bitumen (in the mix) [(a-b)*100]/a (%)	5.01	5.04	5.04	
4	Average % bitumen	5.03 - /			—

(Sign)
26/11/20

L.A.
Regional Laboratory
R.W.D. SASARAM

26/11/20
E.E.
Regional Laboratory
R.W.D. SASARAM

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, SASARAM-2

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Sasaram-2

Sl no.	Package No MR-N/ 2019-20	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No& Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Allocated (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition done against work (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	1	Lori Bandh to Kirihri Pui Via Gaira Chandl Road	10301001045	Lt-5335/Date- 23.10.19	4.750	204.08990	152.69790	50.41100	28.05.20/R WD/SSM- 2/3054main t.17/20-21	27.05.21	-	2625	25.00	5.03%	0.00000	0.00000	152.69790	
Total					4.750	204.08990	152.69790	50.41100							0.00000	0.00000	152.69790	

Executive Engineer
Rural Works Department
Works Division, Sasaram-2

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilization Certificate up to 27 Nov 2020

Sl.No	Name of Scheme	Sanction No.&Date With Amount (In lace Rs.)	Amount Received (In lace Rs.)	Particulars
1	Construction of Rural roads Under MR	New Maintenance Policy-2018 MR (3054) BRRDA PATNA	Nil	Certified that out of Rs. Nil lakh of grants-in-aid sanctioned during the years 2020-21 Infavor of EE,RWD works division Sasaram-2 a sum of Rs Nil lakh has been utilized for the purpose of MR (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. NIL lakh remaining unutilized at the end of the period under report.
	Total:		Nil	


2. Certified that I have satisfied my self that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was utilized for the purpose for which it was sanctioned.

Kind of Checks exercised:-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other caudal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD works.



Executive Engineer
R.W.D, works Division
Sasaram-2

कार्यपालक अभियंता का कार्यालय

क्षेत्रीय प्रयोगशाला, ग्रामीण कार्य विभाग, सासाराम

पत्रांक 805 अ.प्र.

दिनांक 26/11/2020

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
क्षेत्रीय प्रयोगशाला, सासाराम।

सेवा में,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल

सासाराम-2

विषय:- मुख्यमंत्री ग्राम सड़क योजना/प्रधानमंत्री ग्राम सड़क योजना/राष्ट्रीय सम विकास योजना/शिक्षा एवं अन्य योजनाओं में चल रहे कार्यों के गुणवत्ता के जाँचफल प्रतिवेदन भेजने के सम्बन्ध में।

प्रसंग:- आपका पत्रांक

01 अ.प्र.

दिनांक 25/11/20

महाशय,

उपरोक्त विषयक पत्र में कहना है कि मुख्यमंत्री ग्राम सड़क योजना/प्रधानमंत्री ग्राम सड़क योजना/राष्ट्रीय सम विकास योजना शिक्षा एवं अन्य योजनाओं में चल रहे कार्यों के गुणवत्ता के निम्नलिखित पथों का जाँचफल प्रतिवेदन आपके अवलोकनार्थ एवं आवश्यक कारवाई हेतु भेजी जा रही है।

क्रम संख्या	पथ का नाम	पथ की लंबाई	नमूने के प्रकार
1	PWD Road Karup Itariya via ghanga/Prasi Baidway		SDBC-Stone Chip 3-Gr-II
2	Lori bandh to Kirhisi pul via gatra chandi		SDBC-Bitumin Cement
3	Maharaj ganj Sahada Road to Lewa		" " "
4	Karup Baidway Road to mazharian		" " "
5	PWD Road Karup Baidway to nano		" " "
6	Karakat Mahor to Sansar Dehari via Jagannpura - Bridge		" " "

अनु० - जाँचफल प्रतिवेदन 12 प्रतियों में

विश्वासभाजन

26/11/20

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
क्षेत्रीय प्रयोगशाला, सासाराम।
