

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, झाझा (जमुई)।

मोबाइल नं०- 8986915861 ईमेल- rwdjhajha0@gmail.com

प्रेषक,

पत्रांक- 1829 / झाझा दिनांक- 03.09.2020

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल झाझा।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- 3054(MR)/ नई अनुरक्षण नीति 2018 के अंतर्गत कराये गए निम्न कार्यों के विरुद्ध में आवंटन
उपलब्ध कराने के सम्बन्ध में।

महाशय,

उपरोक्त विषय के सम्बन्ध में सूचित करना है कि 3054(MR) / "नई अनुरक्षण नीति 2018" के अंतर्गत (1) Gonda to Chaukijore (2) Chakai-Simultala REO Road (Kewal) - Tilaiya Viaramsinghdih, Baghmara, Ghutwe (3) Nawadih R.E.O. Road to Akhane Road एवं (4) Near Gopidih - Basmata का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः सादर अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०-यथोक्त।

विश्वासभाजन


03.09.2020

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, झाझा।

पता:- पिपराडीह, शहीद सुनील चौक के नजदीक नवाव रोड, झाझा, जिला-जमुई, पिन कोड-811308

RWD Works Division, Jhajha (Dist :- Jamui)

Requisition Format for Scheme Head- MR (3054) Under Bihar Rural Road " New Manintenance Policy 2018" (Initial Rectification and Surface Renewal)

Name of Division:- Jhajha

S.N	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (A.A) Letter No. & Date	Administrative Approval (A.A)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI in MM/KM	Thickness of Bitumen Layer (in MM)	Value of Bitumen Content (in %)	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (K.M)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 JHAJHA/07	Gonda to Chaukijore	20804101023	1846 & 24.06.2019	2.00	67.130	39.31701	17.15594	28/MBD/MR-N/2019-20 & 19.12.2019	18.09.2020	19.08.2020	3090	25	5.20	0	0	39.31701	Surface Completed
2	MR-N/19-20 JHAJHA/12	Chakal-Simultala REO Road (Kewal) - Tilaiya Viaramsinghdih, Baghmara, Ghutwe	NEA22000699	1846 & 24.06.2019	6.750	245.817	151.4015	54.6456	30/MBD/MR-N/2019-20 & 27.12.2019	26.09.2020	20.08.2020	3180	25	5.10	0	0	151.40150	Surface Completed
3	MR-N/19-20 JHAJHA/14	Nawadth R.E.O. Road to Akhane Road	20804101063	1846 & 24.06.2019	2.600	90.951	54.81778	21.559	27/MBD/MR-N/2019-20 & 19.12.2019	18.09.2020	29.08.2020	3474	25	5.10	0	0	54.81778	Surface Completed
4	MR-N/19-20 JHAJHA/14	Near Gopidih - Basmata	20804102070	1846 & 24.06.2019	2.069	72.266	42.83424	17.5586	27/MBD/MR-N/2019-20 & 19.12.2019	18.09.2020	30.06.2020	3321	25	5.14	0	0	42.83424	Surface Completed

flw
03.09.2020

Executive Engineer
RWD Works Division, Jhajha

Name of Road :- Chakal-Simultala REO Road (Kewal) - Tilaiya Viaramsinghdih, Baghmara, Ghutwe (Length :- 6.750 KM)


$$Y = 0 * X^2 + 0.828 * X + 341.6$$

$$X = 5424$$

$$Y = 4832$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY	IRI	Latitude	Longitude	Event
2/9/20	13:18:0	99	0.1	250	0	2500	2411	ROAD	3.31	24.65128	86.4953	Normal
2/9/20	13:18:13	99	0.1	330	10.1	3300	3073	G	4.11	24.65111	86.49625	Normal
2/9/20	13:18:48	99	0.1	340	20.2	3400	3156	G	4.21	24.65084	86.49722	Normal
2/9/20	13:19:0	99	0.1	380	20.2	3800	3487	G	4.6	24.65041	86.49813	Normal
2/9/20	13:19:24	99	0.1	370	20.2	3700	3405	G	4.5	24.64994	86.49887	Normal
2/9/20	13:19:24	99	0.1	340	20.2	3400	3156	G	4.21	24.64914	86.49936	Normal
2/9/20	13:19:24	99	0.1	390	20.2	3900	3570	G	4.7	24.64874	86.50022	Normal
2/9/20	13:20:0	99	0.1	350	20.2	3500	3239	G	4.31	24.6485	86.50121	Normal
2/9/20	13:20:33	99	0.1	320	20.2	3200	2991	G	4.01	24.64822	86.5021	Normal
2/9/20	13:21:0	99	0.1	260	20.2	2600	2494	G	3.41	24.64834	86.50285	Normal
2/9/20	13:21:8	99	0.1	380	20.2	3800	3487	G	4.6	24.64892	86.50342	Normal
2/9/20	13:21:8	99	0.1	340	20.2	3400	3156	G	4.21	24.64851	86.50431	Normal
2/9/20	13:21:44	99	0.1	270	20.2	2700	2577	G	3.51	24.6486	86.50512	Normal
2/9/20	13:22:0	99	0.1	340	20.2	3400	3156	G	4.21	24.64938	86.50561	Normal
2/9/20	13:22:0	99	0.1	320	30.3	3200	2991	G	4.01	24.65015	86.50608	Normal
2/9/20	13:22:19	99	0.1	360	20.2	3600	3322	G	4.41	24.65096	86.50658	Normal
2/9/20	13:22:54	99	0.1	370	20.2	3700	3405	G	4.5	24.65179	86.50712	Normal
2/9/20	13:23:0	99	0.1	310	20.2	3100	2908	G	3.91	24.65254	86.50768	Normal
2/9/20	13:23:30	99	0.1	390	20.2	3900	3570	G	4.7	24.65327	86.5082	Bridge
2/9/20	13:23:30	99	0.1	350	20.2	3500	3239	G	4.31	24.65396	86.50887	Normal
2/9/20	13:24:0	99	0.1	380	20.2	3800	3487	G	4.6	24.65459	86.50963	Curve
2/9/20	13:24:5	99	0.1	300	20.2	3000	2825	G	3.81	24.65419	86.51049	Normal
2/9/20	13:24:5	99	0.1	280	30.3	2800	2659	G	3.61	24.65387	86.51143	Normal
2/9/20	13:24:40	99	0.1	390	20.2	3900	3570	G	4.7	24.65319	86.51204	Curve
2/9/20	13:25:0	99	0.1	360	30.3	3600	3322	G	4.41	24.65257	86.51273	Normal
2/9/20	13:25:0	99	0.1	370	30.3	3700	3405	G	4.5	24.65222	86.51355	Normal
2/9/20	13:25:15	99	0.1	390	30.3	3900	3570	G	4.7	24.65185	86.51456	Bridge
2/9/20	13:25:15	99	0.1	330	30.3	3300	3073	G	4.11	24.65123	86.51525	Normal
2/9/20	13:25:15	99	0.1	310	30.3	3100	2908	G	3.91	24.65069	86.51609	Normal
2/9/20	13:25:15	99	0.1	300	40.4	3000	2825	G	3.81	24.65031	86.5169	Normal
2/9/20	13:25:51	99	0.1	330	40.4	3300	3073	G	4.11	24.65011	86.51798	Normal
2/9/20	13:26:0	99	0.1	320	40.4	3200	2991	G	4.01	24.64996	86.51896	Normal
2/9/20	13:26:0	99	0.1	330	40.4	3300	3073	G	4.11	24.64975	86.52002	Normal
2/9/20	13:26:26	99	0.1	260	20.2	2600	2494	G	3.41	24.64947	86.52082	Normal
2/9/20	13:26:26	99	0.1	350	30.3	3500	3239	G	4.31	24.64871	86.5215	Normal
2/9/20	13:27:1	99	0.1	310	20.2	3100	2908	G	3.91	24.64789	86.5219	Normal
2/9/20	13:27:1	99	0.1	300	20.2	3000	2825	G	3.81	24.64698	86.52221	Normal
2/9/20	13:27:37	99	0.1	300	30.3	3000	2825	G	3.81	24.64619	86.52251	Normal
2/9/20	13:28:12	99	0.1	370	20.2	3700	3405	G	4.5	24.64537	86.52303	Normal


 03.09.2020
Executive Engineer
Rural Works Department
Works Division, Jhalha

2/9/20	13:28:47	99	0.1	360	20.2	3600	3322	G	4.41	24.64449	86.52315	Normal
2/9/20	13:29:0	99	0.1	350	20.2	3500	3239	G	4.31	24.6436	86.52288	Normal
2/9/20	13:29:22	99	0.1	360	20.2	3600	3322	G	4.41	24.64293	86.52315	Normal
2/9/20	13:29:22	99	0.1	290	20.2	2900	2742	G	3.71	24.64261	86.52414	Normal
2/9/20	13:30:0	99	0.1	380	30.3	3800	3487	G	4.6	24.64228	86.52508	Normal
2/9/20	13:30:0	99	0.1	340	30.3	3400	3156	G	4.21	24.64158	86.52569	Normal
2/9/20	13:30:0	99	0.1	320	30.3	3200	2991	G	4.01	24.64068	86.52591	Normal
2/9/20	13:30:33	99	0.1	390	30.3	3900	3570	G	4.7	24.63984	86.52601	Normal
2/9/20	13:30:33	99	0.1	330	40.4	3300	3073	G	4.11	24.63894	86.52609	Normal
2/9/20	13:30:33	99	0.1	390	40.4	3900	3570	G	4.7	24.63796	86.52628	Normal
2/9/20	13:31:0	99	0.1	380	30.3	3800	3487	G	4.6	24.63724	86.5267	Normal
2/9/20	13:31:8	99	0.1	320	20.2	3200	2991	G	4.01	24.63666	86.52763	Normal
2/9/20	13:31:44	99	0.1	360	20.2	3600	3322	G	4.41	24.63587	86.52801	Normal
2/9/20	13:32:0	99	0.1	380	20.2	3800	3487	G	4.6	24.63538	86.52877	Normal
2/9/20	13:32:19	99	0.1	320	20.2	3200	2991	G	4.01	24.63465	86.52933	Normal
2/9/20	13:32:19	99	0.1	270	20.2	2700	2577	G	3.51	24.63435	86.53022	Normal
2/9/20	13:33:29	99	0.1	380	10.1	3800	3487	G	4.6	24.63377	86.53076	Normal
2/9/20	13:34:5	99	0.1	390	20.2	3900	3570	G	4.7	24.63303	86.53022	Normal
2/9/20	13:34:5	99	0.1	380	20.2	3800	3487	G	4.6	24.63234	86.52956	Normal
2/9/20	13:35:0	99	0.1	370	20.2	3700	3405	G	4.5	24.63154	86.52909	Normal
2/9/20	13:35:15	99	0.1	390	20.2	3900	3570	G	4.7	24.63067	86.52875	Normal
2/9/20	13:36:0	99	0.1	380	30.3	3800	3487	G	4.6	24.62978	86.52843	Normal
2/9/20	13:36:26	99	0.1	360	30.3	3600	3322	G	4.41	24.6297	86.52923	Normal
2/9/20	13:37:1	99	0.1	390	20.2	3900	3570	G	4.7	24.6291	86.52993	Normal
2/9/20	13:37:1	99	0.1	370	20.2	3700	3405	G	4.5	24.62863	86.53076	Normal
2/9/20	13:37:1	99	0.1	380	20.2	3800	3487	G	4.6	24.62828	86.5317	Normal
2/9/20	13:37:36	99	0.1	340	30.3	3400	3156	G	4.21	24.62816	86.53271	Normal
2/9/20	13:38:12	99	0.1	320	20.2	3200	2991	G	4.01	24.6276	86.53347	Normal
2/9/20	13:38:12	99	0.059	290	20.2	2900	2742	G	3.71	24.62755	86.53355	Normal


 09.9.2020
 Executive Engineer
 Rural Works Department
 Works Division, Jhatha

☒ Stereo Analyzer


Name of Customer: Rajendra Prasad
Name of Work/Road: Jansingh, Baghmara, Ghutwa
Lab Job number:
Date: 9/2/2020
Section No. 39

Test Date: 9/2/2020
Machine No: 399
Start S No:
Start E No:
Weather:
Start Location: 0
End Location: 6.75
Road Name: Chakeri-Simultala REO Road (K
Road Type: (R) RURAL ROAD
Side:
Interval:
UIV Range: 1411 To 5000 mm/km
Dist Range: 0 To 6.9 = 1000 m
Equation: $Y = 0 * X^2 + 0.828 * X + 341.6$

Print

File: C:\OFFICIAL\Bump Machine\02.09.20\Ghutwa\0 to End\02091623.Xls, Section No.: 39, Eqn: $Y = 0 * X^2 +$

Name of Customer: Name of Work/Road: Lab Job number:

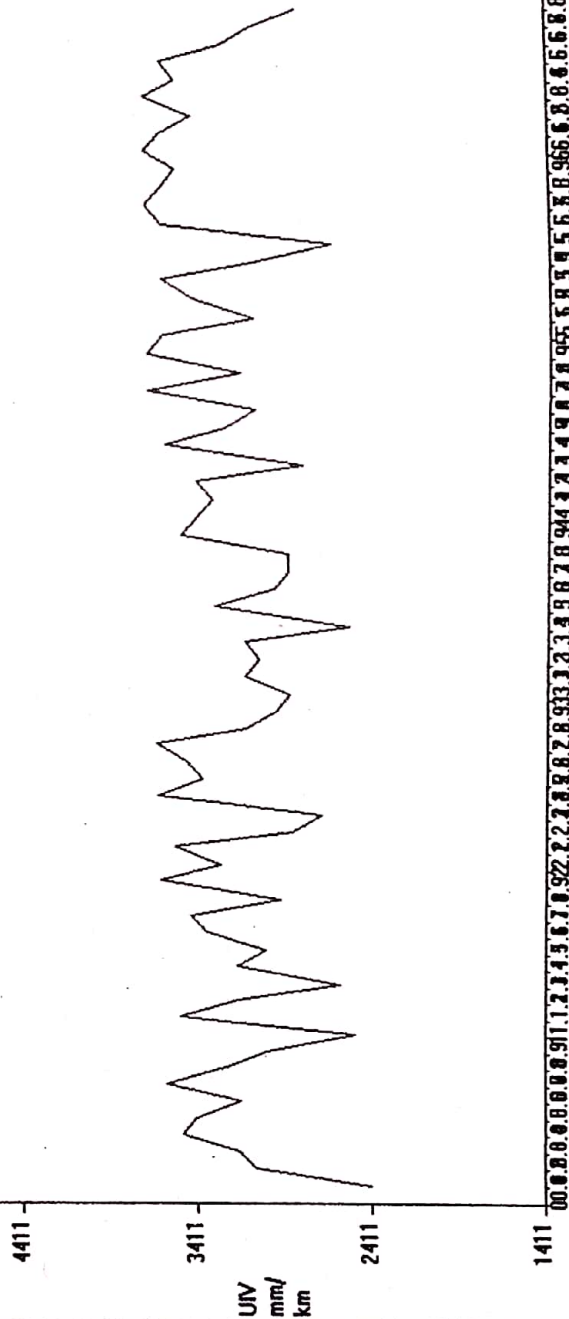

Distance = 10000 m

03.09.2020

Executive Engineer
Rural Works Department
Works Division, Jhalha
