

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक 510, 3130

रक्सौल, / दिनांक 28.04.21

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेन्सी,
ग्रामीण कार्य विभाग, बिहार, पटना।



विषय :- शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 के तहत आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक गैर योजना शीर्ष-3054 अन्तर्गत बिहार ग्रामीण पथ अनुक्षण नीति-2018 संलग्न सूची के अनुसार आवंटन अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।

विश्वासराजन,

28/4/2021
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

28.04.21

Requisition of Allotment under Head MR HEAD-3054 Under Bihar Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

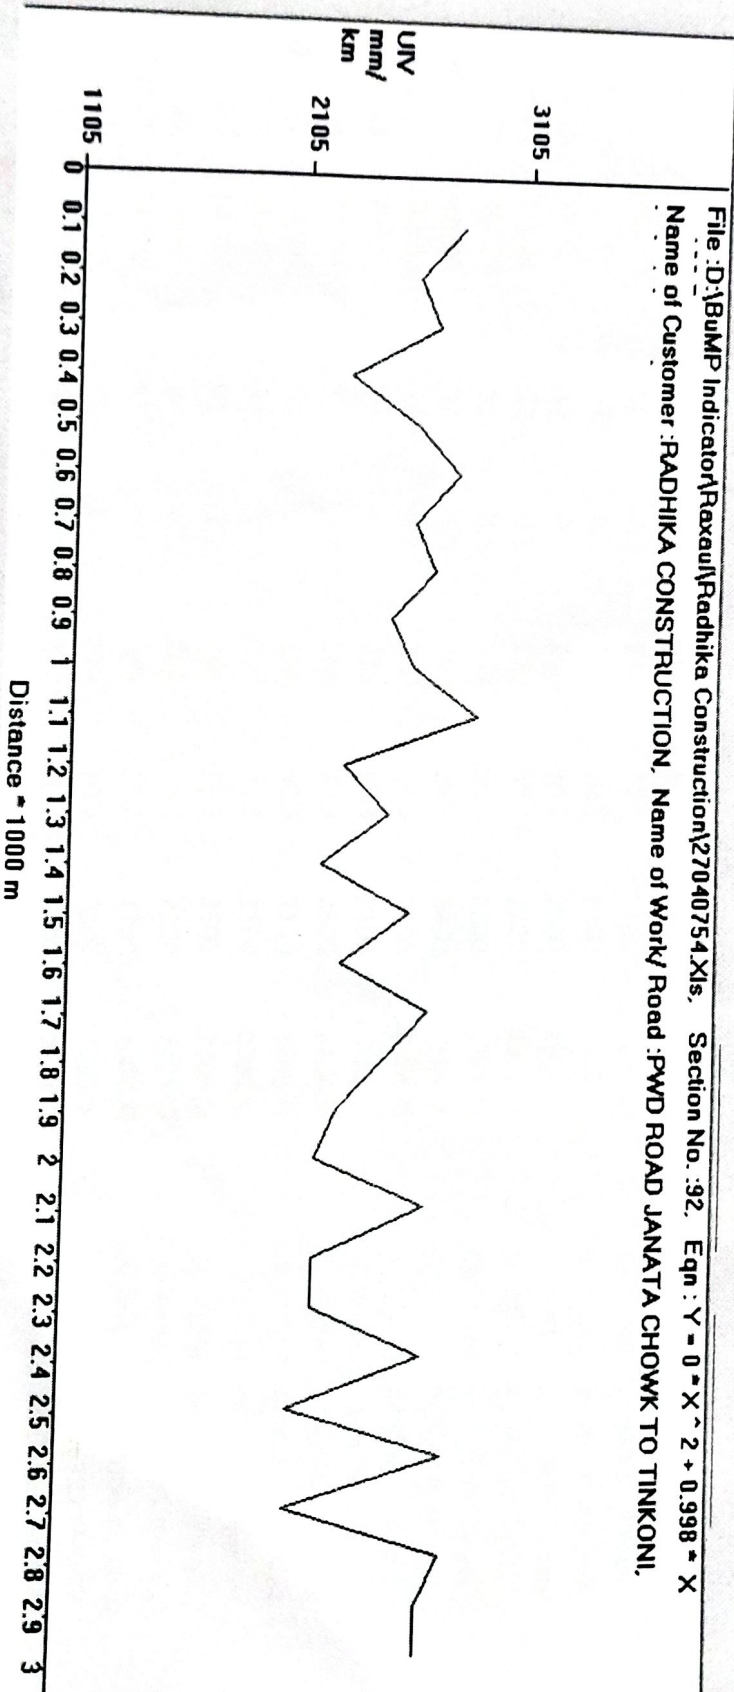
Division :-
Raxaul

Sl. No.	Package No.	Name of Road	Contractor Name	Project ID as per MIS	Administrative Approval (A.A) Letter No. & Date	A.A.		Agreement Value		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percent	Previous Total Allotted Amount	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
						Length (in Km)	Total (Amount) (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Yrs Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
1	MR-N/19-20/Raxaul/08	PWD Janta Chouk to tinkoni	Radhika Constructi on Co.	317851032014	3030-4 (70) 3054-04-117-2 019, 5128 / 4271, 2019	3.000	127.42050	85.52600	32.402	156SBD/19-20	07-05-2021	-	2527	25mm	5	0	0	85.52600	Work in Progress
																		85.52600	


 Executive Engineer,
 Rural Works Department,
 Works Division, Raxaul
 27.04.21

Name of Customer : RADHIKA CONSTRUCTION
 Name of Work : JANATA CHOWK TO TINKONI
 Road :
 Lab Job number :
 Date : 27-04-2021
 Section No. : 92

Test Date : 27-04-2021
 Road Name : JANATA CHOWK TO TINKONI
 Machine No : 378
 Road Type : (R) RURAL ROAD
 Start S No : 0.00 KM
 Side :
 Start E No : 3.00 KM
 Interval
 Weather : NORMAL
 UIV Range : 1105 To 4000
 Dist Range : 0 To 3.1
 mm/km
 Start Location : 26.853722
 End Location : 84.967978
 Equation : $Y = 0 * X^2 + 0.998 * X + 109.5$



Handwritten signature

ROAD NAME-PWD ROAD JANATA CHOWK TO TINKONI, CONTRACTOR-RADHIKA CONSTRUCTION

Date	Time	Section	Length	Bumps	Speed	OR	IRI In	CATEGO	Latitude	Longitu	Event
No.		in km	in mm	Rate	mm/km	UV	mm/km	RY	de		
27/4/21	7:46:0	92	0.1	270	0	2700	2804 G		26.85372	84.99377	Normal
27/4/21	7:46:27	92	0.1	250	30.3	2500	2604 G		26.8533	84.9929	Normal
27/4/21	7:46:27	92	0.1	260	20.2	2600	2704 G		26.85338	84.9919	Normal
27/4/21	7:47:3	92	0.1	220	20.2	2200	2305 G		26.85376	84.99113	Normal
27/4/21	7:47:3	92	0.1	250	20.2	2500	2604 G		26.85428	84.99051	Normal
27/4/21	7:47:3	92	0.1	270	30.3	2700	2804 G		26.85457	84.98955	Normal
27/4/21	7:47:38	92	0.1	250	30.3	2500	2604 G		26.85469	84.98855	Normal
27/4/21	7:47:38	92	0.1	260	30.3	2600	2704 G		26.85481	84.98753	Normal
27/4/21	7:48:0	92	0.1	240	30.3	2400	2504 G		26.85488	84.98658	Normal
27/4/21	7:48:13	92	0.1	250	30.3	2500	2604 G		26.85497	84.98562	Normal
27/4/21	7:48:13	92	0.1	280	20.2	2800	2903 G		26.85543	84.98476	Normal
27/4/21	7:48:13	92	0.1	220	30.3	2200	2305 G		26.85573	84.98387	Normal
27/4/21	7:48:13	92	0.1	240	30.3	2400	2504 G		26.85594	84.98286	Normal
27/4/21	7:48:48	92	0.1	210	30.3	2100	2205 G		26.85625	84.98189	Normal
27/4/21	7:49:0	92	0.1	250	30.3	2500	2604 G		26.85653	84.98096	Normal
27/4/21	7:49:0	92	0.1	220	30.3	2200	2305 G		26.85686	84.98003	Normal
27/4/21	7:49:24	92	0.1	260	20.2	2600	2704 G		26.85698	84.97914	Normal
27/4/21	7:49:24	92	0.1	240	20.2	2400	2504 G		26.85711	84.97816	Normal
27/4/21	7:49:24	92	0.1	220	30.3	2200	2305 G		26.85728	84.97715	Normal
27/4/21	7:50:0	92	0.1	210	30.3	2100	2205 G		26.85751	84.9762	Normal
27/4/21	7:50:0	92	0.1	260	30.3	2600	2704 G		26.85775	84.97513	Normal
27/4/21	7:50:34	92	0.1	210	30.3	2100	2205 G		26.85803	84.97431	Normal
27/4/21	7:51:10	92	0.1	210	20.2	2100	2205 G		26.8586	84.97357	Normal
27/4/21	7:51:10	92	0.1	260	20.2	2600	2704 G		26.85866	84.97261	Normal
27/4/21	7:51:45	92	0.1	200	20.2	2000	2105 G		26.85902	84.97175	Normal
27/4/21	7:52:0	92	0.1	270	20.2	2700	2804 G		26.85931	84.97086	Normal
27/4/21	7:52:20	92	0.1	200	20.2	2000	2105 G		26.8597	84.96993	Normal
27/4/21	7:52:20	92	0.1	270	20.2	2700	2804 G		26.86024	84.96923	Normal
27/4/21	7:53:0	92	0.1	260	20.2	2600	2704 G		26.86103	84.9688	Normal
27/4/21	7:53:0	92	0.1	260	10.1	2600	2704 G		26.8614	84.96798	Normal
		TOTAL IRI		75829							
		AVERAGE IRI		2527.63							

$$Y = 0 * X^2 + 0.998 * X + 109.5$$

$$X = 2830$$

$$Y = 2933$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Executive Engineer

Rural Works Department
Works Division, Raxaul

JE

Signature
27/04/21
