

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल पकड़ीदयाल।

पत्रांक.....620 8750

पकड़ीदयाल

दिनांक...28.4.21

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।



विषय :- (New Maintenance Policy 2018) अन्तर्गत चयनित पथों के लिए
प्राप्त राशि का उपयोगिता प्रमाण-पत्र एवं अधियाचना के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि (New Maintenance Policy 2018)
अन्तर्गत चयनित पथों के लिए उपयोगिता प्रमाण-पत्र एवं अधियाचना विहित प्रपत्र में तैयार
कर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

- अनु०- 1. उपयोगिता प्रमाण-पत्र Form GFR 19A
2. अधियाचना पत्र।
3. प्रतिवेदन की छायाप्रति।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पकड़ीदयाल।


Form.GFR 19-A Form.

(See Government of India's Decision (1) below Rule .150)
Form Of Utilisation Certificate up to the Month Of April 2021
(New Maintenance Policy 2018)

वर्ष 2018-19, 2019-20 एवं 2020-21 में चयनित पथों के लिए उपयोगिता प्रमाण पत्र

PIU -

SL. No.	Name Of Scheme	Sanction No. & Date With Amount	Amount Received (InRs.)	Particulars
1	Construction Of Rural roads Under (New Maintenance Policy 2018)	Lt. 37 (We) Dt. 27.05.2020 Amount. Rs. 75,00,000.00 Lt. 45 (We) Dt. 18.06.2020 Amount. Rs. 01,04,50,000.00 Lt. 47 (We) Dt. 24.06.2020 Amount. Rs. 96,00,000.00 Lt. 72 (We) Dt. 07.10.2020 Amount. Rs. 01,03,00,000.00 Lt. 77 (We) Dt. 14.10.2020 Amount. Rs. 01,45,00,000.00 Lt. 80 (We) Dt. 05.11.2020 Amount. Rs. 01,36,50,000.00 Lt. 82 (We) Dt. 13.11.2020 Amount. Rs. 01,35,50,000.00 Lt. 84 (We) Dt. 26.11.2020 Amount. Rs. 01,16,00,000.00 Lt. 86 (We) Dt. 11.12.2020 Amount. Rs. 04,71,14,000.00 Lt. 05 (We) Dt. 12.01.2021 Amount. Rs. 04,88,72,500.00 Lt. 17 (We) Dt. 26.02.2021 Amount. Rs. 04,47,26,500.00 Lt. 20 (We) Dt. 19.03.2021 Amount. Rs. 06,09,42,938.00	29,28,05,938.00	Certified that out of Rs. 29,28,05,938.00 received during the year 2017-18 in favour of EX. Engineer, R.W.D W.D Pakridayal sum of Rs. 28,97,16,625.00 has been utilized for the purpose of New Maintenance Policy 2018) schemes as given in the margin for which it was sanctioned and that the balance of Rs 03,08,91,313.00 remaining Unutilized at the end of the period under.
		29,28,05,938.00	29,28,05,938.00	


2. Certified that I have satisfied myself that the conditions on which the grant in aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was Sanctioned.


Kind Of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MB'S and test check conducted by the Assistant.
- All other codal Formalities have been Observed.

3. Physical Progress Achieved:

- Construction Of Road Works.
- Construction Of CD works.


D.A.O, Grade - 1,
Rural Works Department,
Works Division Pakridayal.


Executive Engineer,
Rural Works Department,
Works Division Pakridayal.

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Pakridayal.**

Name of Works Division : Pakridayal

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 [Initial Rectification and Surface Renewal]

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of R/I (in mm/Km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in lakh)	Up-to-date expenditure as per MIS (in lakh)	Requisition against work done (in lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 Pakridayal/06	Jihuli To Gonahi.	31708604005	Latter No. 3359 Date- 01.08.2019	6.200	231.54580	151.66628	62.78493	24 -MBD/2019-20 Date- 20.03.2020	14.11.2020	In Progress	3137.77	25	5.00	0.00000	0.00000	151.60000	
2	MR-N/19-20 Pakridayal/09	Jihuli To Jihuli Ghat Via Jamuniya Tola.	31708701001	Latter No. 3359 Date- 01.08.2019	3.600	153.26030	104.82395	36.77527	19 -MBD/2019-20 Date- 11.02.2020	10.11.2020	In Progress	3225.333	25	5.00	0.00000	0.00000	104.80000	
																	256.40000	

- Signed Hard Copy and Soft Copy (in excel) of recorded R/I is enclosed.
- Up-to-date Physical Progress has been uploaded in MIS.

D.A.O. Grade-I
R.W.D, Pakridayal

[Signature]
JE
28/11/21

[Signature]
A/E
28.04.21

Executive Engineer,
Rural Works Department,
Works Division, Pakridayal
[Signature]
28/11/21

NAME OF ROAD- JIHULI TO JIHULI GHAT VIA JAMUNIA TOLA, NAME OF CONTRACTOR-M/S UTTAR BIHAR CONSTRUCTION CO.

Date	Time	Section	No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/4/21	15:14:17	84	0.1	390	0	3900	3855		G	26.60761	85.244612	Curve
24/4/21	15:14:17	84	0.1	300	10.1	3000	2996		G	26.60746	85.244343	Curve
24/4/21	15:15:0	84	0.1	340	20.2	3400	3378		G	26.60678	85.244225	Normal
24/4/21	15:15:0	84	0.1	320	30.3	3200	3187		G	26.60599	85.243972	Normal
24/4/21	15:15:0	84	0.1	360	30.3	3600	3568		G	26.6052	85.24347	Normal
24/4/21	15:15:27	84	0.1	370	30.3	3700	3664		G	26.60435	85.243163	Normal
24/4/21	15:15:27	84	0.1	380	20.2	3800	3759		G	26.60378	85.24281	Curve
24/4/21	15:16:2	84	0.1	360	30.3	3600	3568		G	26.60351	85.243787	Normal
24/4/21	15:16:2	84	0.1	360	30.3	3600	3568		G	26.60328	85.24483	Normal
24/4/21	15:16:2	84	0.1	380	30.3	3800	3759		G	26.60287	85.24579	Normal
24/4/21	15:16:37	84	0.1	340	30.3	3400	3378		G	26.60206	85.246178	Culvert
24/4/21	15:16:37	84	0.1	240	30.3	2400	2424		G	26.60145	85.246852	Normal
24/4/21	15:16:37	84	0.1	280	30.3	2800	2805		G	26.60064	85.247272	Culvert
24/4/21	15:17:0	84	0.1	220	30.3	2200	2233		G	26.60006	85.24808	Culvert
24/4/21	15:17:11	84	0.1	310	30.3	3100	3091		G	26.5995	85.24882	Normal
24/4/21	15:17:11	84	0.1	320	30.3	3200	3187		G	26.59915	85.249713	Normal
24/4/21	15:17:11	84	0.1	310	30.3	3100	3091		G	26.59889	85.250707	Culvert
24/4/21	15:17:46	84	0.1	360	30.3	3600	3568		G	26.59866	85.25168	Normal
24/4/21	15:18:0	84	0.1	320	30.3	3200	3187		G	26.59886	85.252592	Normal
24/4/21	15:18:0	84	0.1	280	30.3	2800	2805		G	26.59907	85.253535	Normal
24/4/21	15:18:22	84	0.1	320	30.3	3200	3187		G	26.59914	85.254545	Normal
24/4/21	15:18:22	84	0.1	300	30.3	3000	2996		G	26.59924	85.255555	Normal
24/4/21	15:18:22	84	0.1	340	30.3	3400	3378		G	26.59951	85.256532	Normal
24/4/21	15:18:57	84	0.1	360	30.3	3600	3568		G	26.59979	85.257423	Curve
24/4/21	15:19:0	84	0.1	320	40.4	3200	3187		G	26.59979	85.25843	Normal
24/4/21	15:19:0	84	0.1	330	40.4	3300	3282		G	26.59974	85.259377	Normal
24/4/21	15:19:0	84	0.1	310	40.4	3100	3091		G	26.5996	85.260387	Normal
24/4/21	15:19:32	84	0.1	300	30.3	3000	2996		G	26.59939	85.261413	Curve
24/4/21	15:19:32	84	0.1	320	30.3	3200	3187		G	26.59848	85.261565	Normal
24/4/21	15:19:32	84	0.1	260	40.4	2600	2614		G	26.59757	85.261615	Normal
24/4/21	15:20:0	84	0.1	340	40.4	3400	3378		G	26.59688	85.262153	Normal
24/4/21	15:20:8	84	0.1	320	40.4	3200	3187		G	26.59617	85.262777	Normal
24/4/21	15:20:8	84	0.048	160	10.1	3333	3314		G	26.59586	85.263113	Normal
TOTAL IRI										106436		
AVERAGE IRI										3225.333		

Y=0 * X ^ 2 + 0.954 * X + 134.5

X = 3333

Y = 3314

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

Y=0 * X ^ 2 + 0.954 * X + 134.5

28/4/21
S.E

28.05.21
S.E

Executive Engineer
RWD Works Division
Pakardiyal

Name of Customer :	MS UTTAR BIHAR CONSTRU
Name of Work / Road :	JH GHAT VIA JAMUNIA TOLA
Lab Job number :	84
Date :	24-04-2021
Section No. :	84

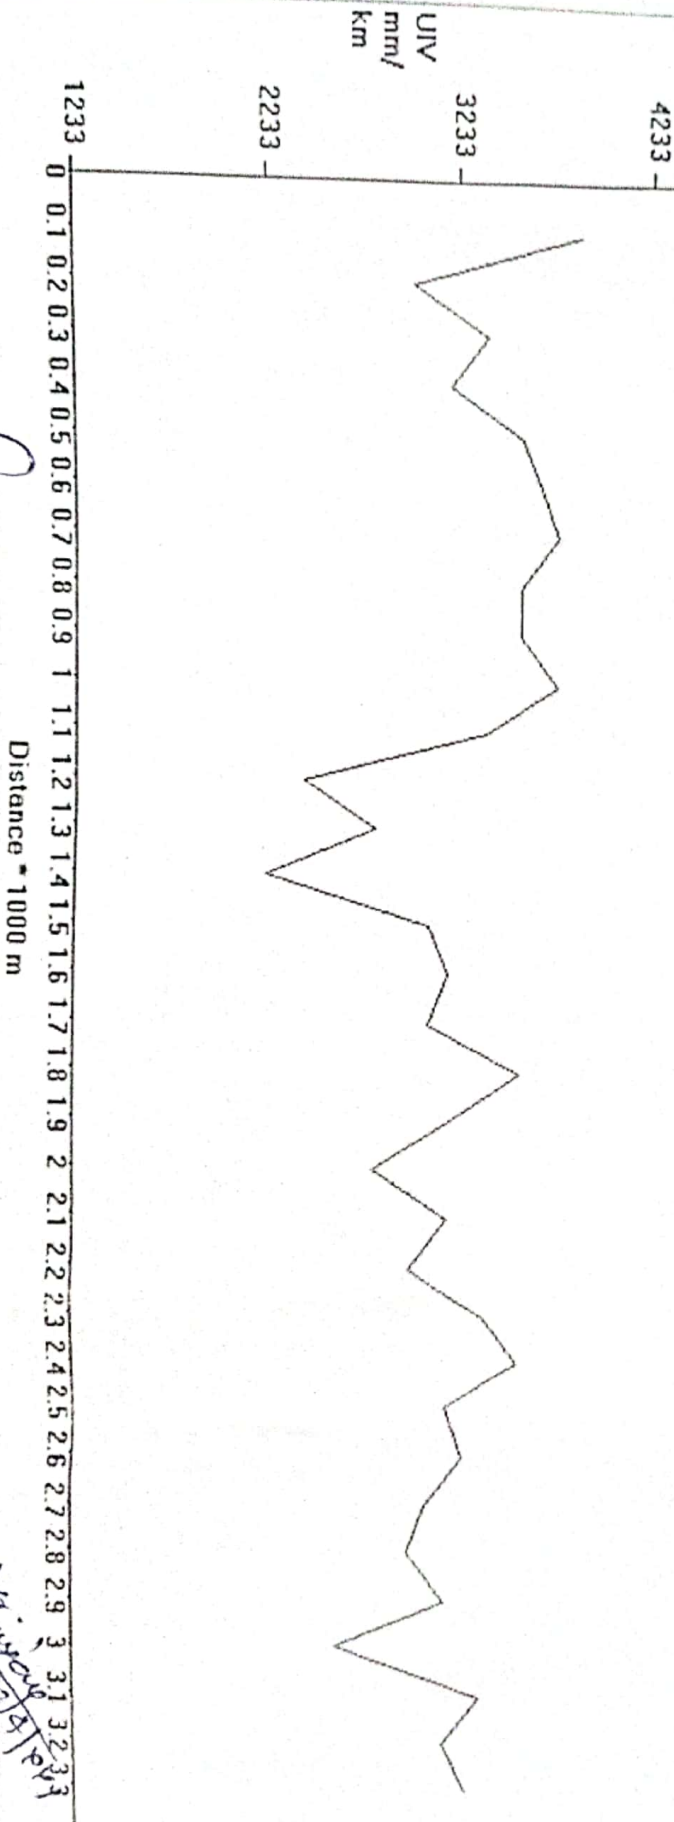
Print Generate Report and Graph

Test Date :	24-04-2021	Road Name :	JHUU TO JHUU GHAT VIA J
Machine No :	437	Road Type :	(R) RURAL ROAD
Start S No :	04	Side :	
Start E No :	36	Interval	
Weather :	NORMAL	UIV Range :	1233 To 5000 1000 mm/km
Start Location :	26.607608	Dist Range :	0 To 3.4 0.1 1000 m
End Location :	85.263113	Equation :	$Y = 0 * X^2 + 0.954 * X + 134.5$

Redraw Graph

Map View

File : D:\Pakaridayal Office\BUMP integrater (437)\UTTAR BIHAR\24.04.2021\24041532.Xls. Section No. : 84. Egn :
 Name of Customer : MS UTTAR BIHAR CONSTRUCTION CO., Name of Work/ Road : JHUU TO JHUU GHAT VIA



SA
28/4/21
S.E

28.04.21
A.E

Executive Engineer
RWD Works Division
Pakaridayal
