

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बायसी

पत्रांक1221..... / बायसी, दिनांक02/08/21.....

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बायसी।

सेवा में,

नोडल पदाधिकारी (MR-3054),
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय : गैर योजना मुख्य शीर्ष 3054 (नई अनुरक्षण नीति) सड़क अनुरक्षण ईकाई मद में वित्तीय वर्ष 2019-20 के लिए आवंटन निर्गत करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि गैर योजना मुख्य शीर्ष 3054 (नई अनुरक्षण नीति) योजनान्तर्गत मांग पत्र विहित प्रपत्र में तैयार कर आपके आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः अनुरोध है कि संवेदकों का भुगतान हेतु आवंटन निर्गत करने की कृपा की जाय।

अनु० - यथोक्त।

विश्वासभाजन

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बायसी।

वेद
02/08/21

Krishna
02/08/21

Requisition Format for scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Rural Works Department, Works Division, Baisi

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	Up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)									
1		Jantahat-Asjamobaiya	NEA220001731	Lt. 1840 Dt. 24.06.2019	1.58	70.089	48.28813	16.38892	17.02.2021	Comp.	1757.94	5.07	0.00000	0.00000	48.28813	
2	MR-N/19-20 BAISI/01	Improvement of road from kandarpul to Masandpur on Sonapur Chatangi Road	21105301019	Lt. 1840 Dt. 24.06.2019	1.04	45.2854	30.79040	11.09910	17.02.2021	Comp.	2949.3	5.04	30.79000	30.76386	0.00000	
3		Improvement of road from Chhatiyon Pokharia REO Road Road to Harichoura	21105301014	Lt. 1840 Dt. 24.06.2019	1.25	49.012	33.06735	11.76411	17.02.2021	Comp.	3066.75	5.00	33.06700	33.01502	0.00000	
4	MR-N/19-20 BAISI/11	Amour to Pathantoli	21105202206	Lt. 3029 dt. 16.07.2019	2.50	131.632	91.35228	30.83033	17.02.2021	In Progress	2511.72	5.07	0.00000	0.00000	91.35228	
5		Daripur To Ikra	21105202049	Lt. 3029 dt. 16.07.2020	2.28	145.923	106.74207	28.2324	17.02.2021	22.02.21	1811.22	5.02	106.74200	106.49481	0.00000	
6		Terdahi to Parasrai	21105202119	Lt. 3029 dt. 16.07.2021	2.10	101.980	68.85917	26.03829	17.02.2021	In Progress	2100.29	5.01	68.85900	68.66608	0.00000	

133.64041

- 1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed except SDBC Work.
- 2 Up-to-date Physical Progress has been uploade in MIS.

(Signature)
Divisional Accounts Officer,
Rural Works Department,
Works Division, Baisi

(Signature)
Executive Engineer,
Rural Works Department,
Works Division, Baisi

17/08/21
17/08/21

FORM GFR 19-A
(See Government of India's Decision (I) below Rule -150)
Form of Utilization Certificate upto the month of July 2021
MR 3054 [New Maintenance Policy]

PIU – RWD, Works Division, Baisi

Sl. No	Name of Scheme	Sanction No. & Date with Amount (in Rs. lacs)	Amount Received (in Rs. lacs)	Particulars
1	Construction of Rural roads under MR 3054 [New Maintenance Policy]		4370.93986	Certified that out of Rs.4370.93986 lacs received upto date in favour of Executive Engineer, RWD, Works Division, Baisi a sum of Rs.4335.10485 lacs has been utilized for the purpose of MMGSY Schemes as given in the margin for which it was sanctioned and that the balance of Rs.35.83501 lacs remaining unutilized at the end of the period under MR 3054 (New Maintenance Policy).
	Letter No.	Date	Amount	
1	45	18.06.2020	175.53902	CFMS
2	47	24.06.2020	193.33159	CFMS
3	69	24.09.2020	41.51000	CFMS
4	72	07.10.2020	332.55942	CFMS
5	84	26.11.2020	169.86125	CFMS
6	1	01.01.2021	151.00000	CFMS
7	5	12.01.2021	448.27349	CFMS
8	8	23.01.2021	357.97418	CFMS
9	17	26.02.2021	894.38077	CFMS
10	20	19.03.2021	1224.71825	CFMS
11	23	26.03.2021	63.85700	CFMS
12	27	04.05.2021	126.05097	CFMS
13	30	21.05.2021	126.97100	CFMS
14	40	14.06.2021	64.91292	CFMS
		Total	4370.93986	

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.


Kind of Checks exercised:-

- Works have been supervised by Executive engineer / Superintending Engineer.
- Periodical inspection has been conducted by Executive engineer / Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD works.


Divisional Accounts Officer,
RWD, Works Division, Baisi


Executive Engineer
RWD, Works Division, Baisi


Lab Job number :39
Date :30-07-2021

Name of Customer :Izhar Ahmad

Name of Work/ Road :Jantahat-Asjamobaiya

Date	Time	Section	No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI/TEGORY mm/km ROAD	Latitude_ongitude	Event
30/7/21	13:5:22	71		0.1	70	0	700	927 G	25.86023	87.7337 Normal
30/7/21	13:6:0	71		0.1	100	20.2	1000	1268 G	25.85986	87.73278 Normal
30/7/21	13:6:0	71		0.1	110	20.2	1100	1382 G	25.85955	87.73182 Normal
30/7/21	13:6:0	71		0.1	200	30.3	2000	2404 G	25.85929	87.73091 Normal
30/7/21	13:6:32	71		0.1	200	20.2	2000	2404 G	25.85902	87.72997 Normal
30/7/21	13:6:32	71		0.1	210	30.3	2100	2518 G	25.85878	87.72897 Normal
30/7/21	13:7:0	71		0.1	100	20.2	1000	1268 G	25.85858	87.72798 Normal
30/7/21	13:7:6	71		0.1	260	20.2	2600	3086 G	25.85843	87.72699 Normal
30/7/21	13:7:6	71		0.1	140	20.2	1400	1722 G	25.85831	87.72599 Curve
30/7/21	13:7:42	71		0.1	80	20.2	800	1041 G	25.85821	87.72503 Normal
30/7/21	13:8:0	71		0.1	130	20.2	1300	1609 G	25.8581	87.72402 Normal
30/7/21	13:8:0	71		0.1	100	20.2	1000	1268 G	25.858	87.72308 Normal
30/7/21	13:8:17	71		0.1	240	20.2	2400	2858 G	25.8579	87.72204 Bridge
30/7/21	13:8:17	71		0.1	160	20.2	1600	1950 G	25.85784	87.72113 Normal
30/7/21	13:8:52	71		0.1	100	20.2	1000	1268 G	25.85776	87.72005 Normal
30/7/21	13:9:0	71		0.1	90	20.2	900	1154 G	25.85768	87.71914 Normal

$Y = 0 * X^2 + 1.136 * X + 132.5$
 $X = 900$
 $Y = 1154$

(R) RURAL ROAD


Good Average Poor
<4000 4001-5000 >5001

Chand
30/7/21
ju

30/7/21
ju

File : FA30071312.Xls, Section No. : 71, Eqn : $Y = 0 * X^2 + 1.136 * X + 132.5$

Name of Customer : Izhar Ahmad, Name of Work/ Road : Jantahat-Asjamobaiya, Lab Job number : 39

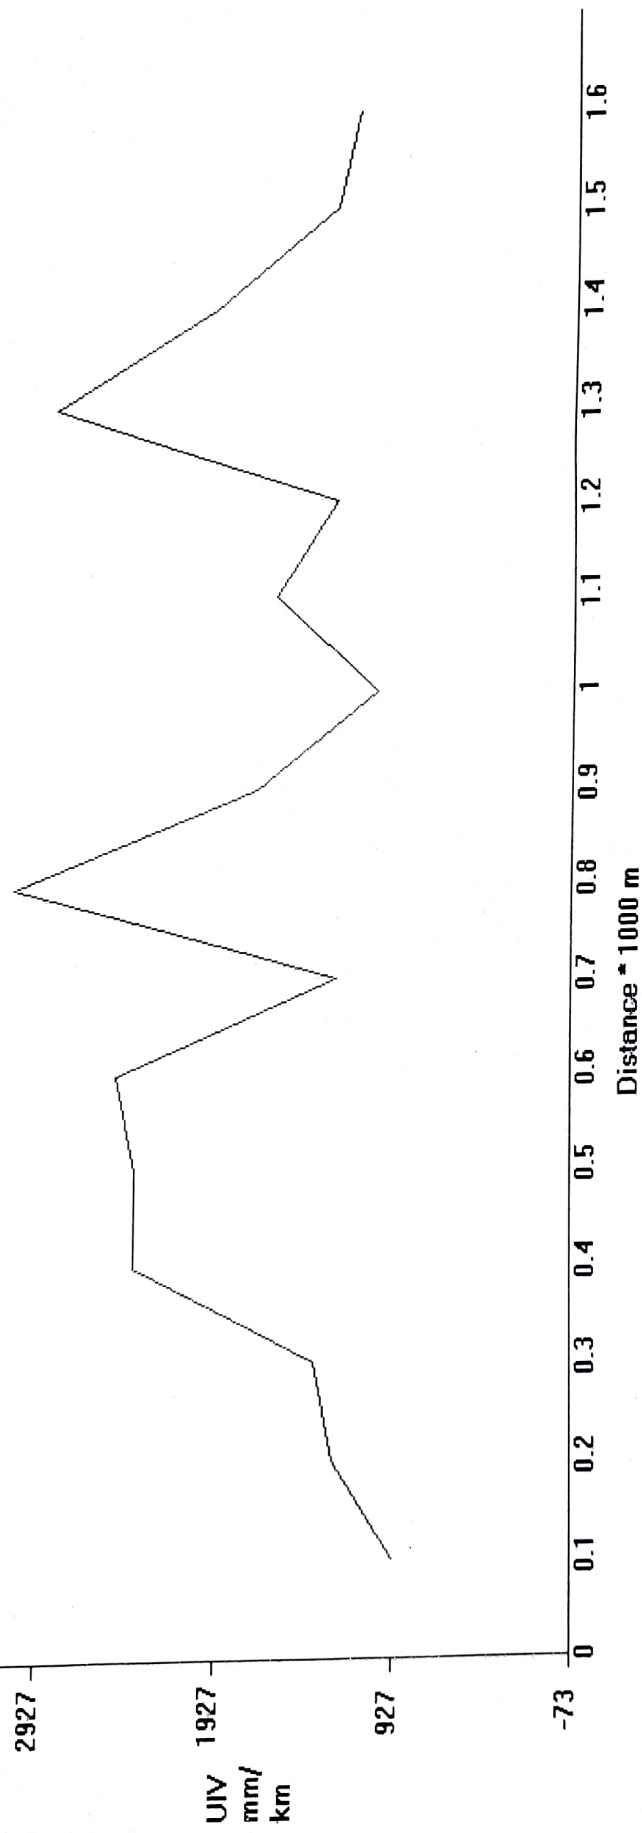

[Signature]
30/12/11
HE

[Signature]
30/12/11
JW

Lab Job number :39

Date :30-07-2021

Name of Customer :Izhar Ahmad

Name of Work/ Road :Jantahat-Asjamobaiya

Sr.no Location of Corrected U.I Road catagory
test(in km) value(mm/km)

5	0.1	927 G
6	0.2	1268 G
7	0.3	1382 G
8	0.4	2404 G
9	0.5	2404 G
10	0.6	2518 G
11	0.7	1268 G
12	0.8	3086 G
13	0.9	1722 G
14	1	1041 G
15	1.1	1609 G
16	1.2	1268 G
17	1.3	2858 G
18	1.4	1950 G
19	1.5	1268 G
20	1.6	1154 G

Chaudhary
30/7/21
JN

30/7/21
AE

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, पूर्णियाँ।

पत्रांक ११५६० / दिनांक ०८/०२/२०२१।

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
क्षेत्रीय प्रयोगशाला, पूर्णियाँ।

सेवा में,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल वागमती

विषय :- निर्माण कार्यों प्रयुक्त होने वाली सामग्रियों के नमूने की जाँच कर जाँच फल प्रतिवेदन भेजने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि निर्माण कार्यों में प्रयुक्त होनेवाली सामग्रियों के नमूने की जाँच कर जाँचफल प्रतिवेदन आपके आवश्यक कार्रवाई हेतु भेजी रही है।

क्र० सं०	पथ नाम	योजना का नाम	नमूने का जाँचफल
1.	Janta hat to Asra Mobaiys Road	MR13054	GSB-II, WBM WII, III SDBC (mix) Sample.

अनु०-यथोक्त।

विश्वासभाजन

११-३
०८/०२/२१
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
क्षेत्रीय प्रयोगशाला, पूर्णियाँ
जि०-६
०८/०२/२०२१

OFFICE OF THE EXECUTIVE ENGINEER

RURAL WORKS DEPARTMENT, REGIONAL LABORATORY, PURNEA

RESULT OF PHYSICAL TEST FOR GRADATION OF COARSE AGGREGATE

NAME OF THE ROAD :- Janta hut to Mohaiya Road.
 PACKAGE NO. UNDER P.M.G.S.Y. MR13054 NAME OF THE WORKS DIVISION Baisi
 NAME OF WORK :- WBM W.III NAME OF WORKS CIRCLE Purnea
 NATURE OF SAMPLE Stone metal W.III SAMPLE COLLECTED BY A.K. Wajid S.S. Div. Baisi
 NAME OF AGENCY Mr. Iqbal Ahmed LOCATION 3004

SI. NO	AIV		FLAKINESS INDEX		WATER ABSORPTION		REMARKS
	TEST VALUE	REQUIRED VALUE (MAX)	TEST VALUE	REQUIRED VALUE (MAX)	TEST VALUE	REQUIRED VALUE (MAX)	
1	1	2	3	4	5	6	
1	9.84	40%	—	—	0.68%	3.0%	Acceptable

SIEVE ANALYSIS FOR GRADATION OF Stone metal W.III
 WEIGHT OF SAMPLE TAKEN 10.0 Kg.

SI. NO	I.S. SIEVE SIZE DESIGNATION IN M.M	WT OF MIX RETAINED	% OF WEIGHT RETAINED	CUMULATIVE % OF WT. RETAINED	% OF WEIGHT PASSING	REQUIRED VALUE IN %	REMARKS
1	1	2	3	4	5	6	
1	63	0	0	0	100	100	
2	53	344	3.44	3.44	96.56	95-100	
3	45	3050	30.50	33.94	66.06	65-90	
4	22.4	5812	58.12	92.06	7.94	0-10	
5	11.2	702	7.02	99.08	0.92	0-5	
6							

LETTER NO.

COPY TO:-

E.E.R.W.D. WORKS DIVISION Baisi

S.E.R.W.D. WORKS CIRCLE

S.E. CUM STATE QUALITY CO-ORDINATOR, BIHAR, PATNA

CHIEF ENGINEER R.W.D. BIHAR, PATNA

LA 8/2/21
 REGIONAL LABORATORY,
 R.W.D. PURNEA

REGIONAL LABORATORY,
 R.W.D. PURNEA

EXECUTIVE ENGINEER,
 REGIONAL LABORATORY,
 R.W.D. PURNEA

OFFICE OF THE EXECUTIVE ENGINEER

RURAL WORKS DEPARTMENT, REGIONAL LABORATORY, PURNIA

RESULT OF PHYSICAL TEST FOR GRADATION OF COARSE AGGREGATE

NAME OF THE ROAD :- Janta hat to H39 Mobaiy 9. Road.

PACKAGE NO. UNDER P.M.S.S.V. MR/3054

NAME OF THE WORKS DIVISION Baisi

NAME OF WORK WBM WII

NAME OF WORKS CIRCLE Purnea

NATURE OF SAMPLE Stone metal WII

SAMPLE COLLECTED BY: A.F.R.W.D. (W) Sub. Div. Baisi 490.

NAME OF AGENCY Md. Azhar Ahmed.

LOCATION: 30.04.21

S.NO	S.S.		FLUORESCENCE		WATER ABSORPTION		REMARKS
	TEST VALUE	REQUIRED VALUE (MAX)	TEST VALUE	REQUIRED VALUE (MAX)	TEST VALUE	REQUIRED VALUE (MAX)	
1	1	2	3	4	5	6	
1	9.9%	40%	—	—	0.73%	3.0%	Acceptable

NOTE ANALYSIS FOR GRADATION OF Stone metal WII

WEIGHT OF SAMPLE TAKEN 1000

S.NO	I.S. SIEVE SIZE DESIGNATION IN MM	WT OF MIX RETAINED	% OF WEIGHT RETAINED	CUMULATIVE % OF WT. RETAINED	% OF WEIGHT PASSING	REQUIRED VALUE IN %	REMARKS
1	1	2	3	4	5	6	
1	90	0	0	0	100	100	
2	63	812	8.12	8.12	91.88	90-100	
3	53	4816	48.16	56.28	53.72	25-75	
4	45	3130	31.30	87.58	12.42	0-15	
5	22.4	1150	11.50	99.08	0.92	0-5	
6							

LETTER NO.

COPY TO:-

S.E. P.W.D. WORKS DIVISION Baisi

S.E. P.W.D. WORKS CIRCLE

S.E. CUM STATE QUALITY CO-ORDINATOR, BHAIR, PATNA

CHIEF ENGINEER R.W.D. BHAIR, PATNA

LA 85421

REGIONAL LABORATORY, R.W.D. PURNIA

8/8/21

REGIONAL LABORATORY, R.W.D. PURNIA

8/8/21

EXECUTIVE ENGINEER, REGIONAL LABORATORY, R.W.D. PURNIA

OFFICE OF THE EXECUTIVE ENGINEER R.W.D. REGIONAL
LABORATORY, PURNER, (BIHAR)
RESULT OF BITMEN CONTENT OF MIX SAMPLE

Name of work Janta hat to Asja Mobaiyya Name of Division Baisi
Package no./ngt.no. MR/3054 Name of Agency Md. Izhar Ahmad
Sample Collected by A.E.R.W.D (W) Sub-Div. Baisi U-110.01 dt-5.2.2021
Location SSOM Wt. of sample taken 1000 gm.

Sl.No.	Sample No.	Identification No.	Wt. of sample b.c.	Wt. of sample a.c.	Loss wt.	Average	% of bitmen content	Remark
1.	B	J1	314	299	15.0			
2.	C	J2	319	304	15.0	15.0	5.07%	
3.	D	J3	298	283	15.0			

Copy to Executive Engineer RWA (W) Div. Baisi

Suprntending Engineer

Chief Engineer Bihar Patna

LA 8/2/21

8/2/21

EXECUTIVE ENGINEER
RURAL WORKS DEPT.
REGIONAL LABORATORY
PURNER.

OFFICE OF THE EXECUTIVE ENGINEER
REGIONAL LABORATORY
RURAL WORK DEPARTMENT, PURNEA
GRADATION FOR GRANULAR SUB BASE MATERIAL

- (1) Name of Work: Janta khat to As Ja Mobaiya
(2) Name of Scheme: MR/3054
(3) Name of Agency: Md. Izzat Ahmad
(4) Sample Collected by: H.E.K.W. 2(W) Sub-Div. Baisi LHO-01 Campdt-5.2.21
(5) Nature of Sample: GISB-II
(6) Location: BOOM.
Date of Collection: 6/2/21
Date of Test: 8/2/21

Sl. No.	IS Sieve designation	Weight Retained	Wt of Sample Taken 23.810 kg			Weight passing the Sieve (Required Value)			Remarks
			% Wt retained	% of Cumulative retained	% of passing	Grading-I	Grading-II	Grading-III	
1	75 mm	—	—	—	—	100	—	—	Acceptable
2	50 mm	0	0	0	100	—	100	—	
3	20 mm	11347	47.65	47.65	52.35	55-75	50-80	100	
4	4.75 mm	4390	18.43	66.08	33.92	10-30	15-35	24.15	
5	0.075 mm	7852	32.97	99.05	0.95	0-10	<10	<10	

Copy for

- (1) ☒
(2) ☒
(3) ☒
(4) P.E.R.V.D WORKS DIVISION Baisi

Baisi
L.A. 8/2/21

[Signature]
8/2/21

[Signature]
8/2/21
E.E.
Regional Laboratory
R.W.D. Purnea
