

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पटना ।

पत्रांक 1559 (6/50)

दिनांक 27/08/2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बी.आर.आर.डी.ए.,
ग्रामीण कार्य विभाग,
बिहार, पटना ।

विषय :- शीर्ष-MR(3054) under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत पथों का आवंटन का अध्याचना के संबंध में।

प्रसंग :- भवदीय पत्रांक-मु0अ0-4(मु0)3054-04-04/2020 / पार्ट-4-3415
(अनु0) दिनांक-24.08.2021

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि शीर्ष-MR(3054) under Bihar Rural Road Maintenance Policy-2018 योजना अन्तर्गत भवदीय द्वारा दिए गए निदेशानुसार आवश्यक सुधार कर निम्नांकित 3 पथों एवं अन्य पथ का आवंटन का अध्याचना का मांग विहित-प्रपत्र में तैयार कर अध्याचना हेतु भेजी जा रही है। पथों का कार्य विशिष्टियों के अनुरूप किया जा चुका है।

क्र० सं०	पथ का नाम	आवश्यक सुधार
1	Dumri Daulatpur Road - Chak Sultanpur	Work Complete in 2.400 K.M. & in 0.600 K.M. work is not done due to Local People Hindrance. Public not allowing to do SDBC on existing PCC.
2	Fatuha Islampur Rd to Barki Kewai	Completed length entered in MIS.
3	NH-30A to Mureda Road (Mushari)	Completed length entered in MIS

अतः आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध कराने की कृपा की जाये ताकि सवेदक का भुगतान किया जा सके।

अनु० :- यथोक्त।

विश्वासभीजु

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पटना।

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Patna

Sl. No.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
		Dumri Daulapur Road - Chak Sultanpur	NEA220001347	Let No.-3024 dated 16.07.2019	3.30000	107.13000	72.71200	33.48614	09- NIBD/2019- 2020 dated 02-Dec-2019	01.09.2020	02.07.2021	2281.04100	25 mm	5%	0.00000	0.00000	58.25156	Work Complete in 2.400 K.M. (In 0.600 K.M. Work is not done due to Local People Hindrance)
2	2	Fatma Islampur Rd to Barhi Kewari	10100102310	1818 dated 24.06.2019	0.45000	19.03000	14.18500	4.16602	34- NIBD/2020- 2021 Dated 24.04.2020	03.11.2021	28.06.2021	3301	20 mm	4.5%	0.00000	0.00000	11.13909	Work Complete (Completed length entered in MIS)
3	13	NH-30A to Mureda Road (Mushari)	10100201029	Let No.-5548 dated 23.10.2019	0.80000	38.69100	33.88400	7.41220	12 NIBD/2020- 21 DATED 20.06.2020	09.03.2021	15.06.2021	1818.5	25 mm	5%	0.00000	0.00000	33.94333	Work Complete (Completed length entered in MIS)
4	13	PMGSY ROAD TO MASARHI	NEA22000957	Let No.-5548 dated 23.10.2019	2.35000	114.20700	101.20600	21.85282	12 NIBD/2020- 21 DATED 20.06.2020	19.03.2021	15.06.2021	1541.125	25 mm	5%	87.33760	87.33760	7.28289	Work Complete
Total																		110.61717

- Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- Up-to-Date Physical Progress has been uploaded in MIS.

Executive Engineer
RWD Works Division, Patna
21/8/21

Name of The Road : NH-30A To Mureda Road (Mushahri)

Length of The Road : 0.800

Package No. : MR-N/2019-2020/PATNA/13

Division : Patna

Block : Danyawan

Contractor Name : ASTHA CONSTRUCTION AND DEVELOPERS PVT.LTD.

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event			
13/6/21	15:37:38	30	0.1	270	0	2700	2805	G	25.454257	85.292608	Curve	$Y = 0 * X^2 + 0.936 * X + 278.4$		
13/6/21	15:38:0	30	0.1	140	20.2	1400	1588	G	25.453453	85.292222	Normal	$X = 1500$		
13/6/21	15:38:14	30	0.1	150	30.3	1500	1682	G	25.452573	85.292473	Normal	$Y = 1682$		
13/6/21	15:38:14	30	0.1	130	30.3	1300	1495	G	25.452142	85.291852	Curve			
13/6/21	15:38:14	30	0.1	130	30.3	1300	1495	G	25.452202	85.290842	Normal	(R)RURAL ROAD		
13/6/21	15:38:49	30	0.1	160	20.2	1600	1776	G	25.452135	85.28978	Curve	Good	Average	
13/6/21	15:39:24	30	0.1	140	10.1	1867	2025	G	25.452848	85.289747	Normal	<4000	4001-5000	Poor
13/6/21	15:45:34	31	0.1	150	0	1500	1682	G	25.45452	85.290673	Normal			>5001
Total			0.8	1270	141.4	13167	14548		203.62413	682.330197				
Average						1645.875	1818.5							

[Signature]
13.6.21
S. P. Mungar.

[Signature]
13.06.21
J. E.

[Signature]
13.06.21
M.

[Signature]
13.6.21
E.

De
1-1
2-1
3-E
4-T

Name of Customer: ASTHA CONSTRUCTION AND DEVELOPERS
 Name of Work: NH-30A To Mureda Road (Mureda)
 Road: NH-30A To Mureda Road (Mureda)
 Lab Job number:
 Date: 13-06-2021
 Section No. 30


Test Date: 13-06-2021
 Road Name: NH-30A To Mureda Road (Mureda)
 Machine No:
 Road Type: (R) RURAL ROAD
 Start S No:
 Side:
 Start E No:
 Interval:
 Weather:
 UV Range: 495 To 4000 1000 mm/km
 Dist Range: 0 To 0.8 0.1 - 1000 m
 Start Location:
 End Location:
 Equation: $Y = 0.0 \cdot X^2 + 0.936 \cdot X + 278.4$

Print Generate Report and Graph

Redraw Graph

Map View

File: C:\Users\Shadab Alam\Desktop\1623592887922.Xls, Section No: 30, Eqn: $Y = 0.0 \cdot X^2 + 0.936 \cdot X + 278.4$
 Name of Customer: ASTHA CONSTRUCTION AND DEVELOPERS PVT.LTD., Name of Work/ Road: NH-30A To

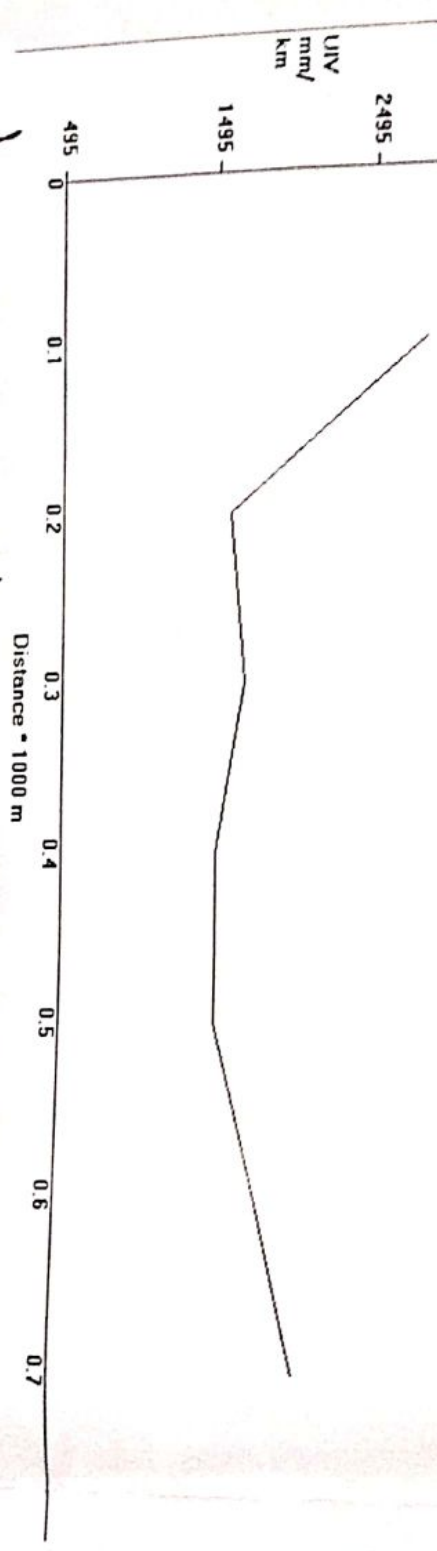

13.6.21
 2 T Mureda

13.06.21
 J.E.

13.06.21
 A.E.

13.6.21
 J.E.

Name of
 Owner :
 Name of Work/
 Road :
 Job Job number :
 Date :
 Section No. :
 31

Test Date :	13-06-2021	
Machine No :		
Start S No :		
Start E No :		
Weather :		
Start Location :		
End Location :		
Road Name :	Ilt+30A To Mareda Road (Mo	
Road Type :	(R) RUFAL ROAD	
Side :		
UV Range :	682 To 3000	Interval 1000 mm/km
Dist Range :	0 To 0.2	0.1 - 1000 m
Equation :	$Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$	

Map View

UV 1682 -
mm/
km

682 $\frac{1}{0}$

Distance = 1000 m

0.1

Handwritten: 12.8.21
17.8.21
19.8.21

John
13.06.2021.
J.E

Handwritten: 13.06.21 AK

~~14.6.2~~

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	202 m Mc Mill				
Name of work	Repair & Five years Maintenance of Road from NH-30 to Mnsada Road (Mnsada) under 3054 MK.				
Agency	Ashta Construction & Developers PVT. LTD, At. M. F. Sector - 6, Block-2, Phase-68, Bahad-urban Housing Colony, Bahut-nath Road, K. Bagh, Patna				
Agreement no	12/11/2020-21				
Date Approved	0.09/2 Below.				
Agreement value					
Date of Commencement	20-06-2020				
Date of Completion	19-09-2021				
Date of Measurement	15-06-2021.				
	<u>Work done</u>				
Item (i)	R.C.C. M-15 grade km. Stone do-etc.				
(i)	km. Stone	—			2.00 nos.
(ii)	200 m. Stone	—			4.00 nos.

Continuation

Qty = 9.00 nos.

Shah
15.08.21
J.E.

Himanshu
15.08.21
A.E.

ABSTRACT OF COST

① Clearing & grubbing
road land etc.

12.16 Hect. vide TMB page ⑨

@ Rs 51,161 = 75 Hect - Rs 8,86 = 0

② Construction of sub
grade & earth work
under etc.

480.00 m³ vide TMB page ⑨

@ Rs 161,556 m³ - Rs 77,549 = 0

Cum Rs 85,735 = 0

Continuation

P.T.O.

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				Off 27	37,274.00
(14) Paving of faces by the road sides - etc.					
48.00 m. vide TMB Page (13)					
at 818 = 84/each - 16					32,754.00
(15) Prov. & fixing of 4 ft. - 16 m. masonry information sign board with "Keep" - - - do - - - etc.					
2.00 m. vide TMB Page (11)					
1.00 m. vide TMB Page (14)					
(16) Prov. & Laying of hot applied thermoplastic compound - etc.					
170.00 m ² vide TMB Page (13)					
at 735 = 79/m ² - 13					1,25,085.00
(17) P/F of 4 m. road stone boundary pillars - etc.					
9.00 m. vide TMB Page (14)					
at 491 = 65/each - 14					44,250.00
					Rs 29,76,994.00
Add 12% GST (+)					Rs 3,57,239.00
Add 1% L. cess (+)					Rs 29,77,000.00
Add Signage fee					
vide TMB Page (9) (+)					Rs 33,388.00

Continuation

at 33,97,391.00

PTD

A blank sheet of white graph paper featuring a uniform grid of thin black horizontal and vertical lines. The grid consists of approximately 10 columns and 8 rows, creating a series of small squares across the page. There are no margins, text, or other markings on the paper.
