

**कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, मोतिहारी।**

पत्रांक 1804/अनु / दिनांक 12.7.2021।

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल मोतिहारी।

सेवा में

अपर मुख्य कार्यपालक पदाधिकारी,
—सह—सचिव BRRDA,
बिहार, पटना।


विषय

MR-3054(New Maintenance Policy 2018) के अन्तर्गत पथ के
अनुस्क्षण के लिए निधि उपलब्ध कराने के संबंध में।

नहाराय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054(New Maintenance Policy 2018) के अन्तर्गत पथ के अनुस्क्षण के निधि के लिए सूची बनाकर इस पत्र में संलग्न कर नवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।
अनु० यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, मोतिहारी।

Office of The Executive Engineer, Rural Works Department, Works Division Motihari

Requisition formate for Scheme Head- MR-3054 Under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification with Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID As per MIS	A.A. Letter No & Date	Administrative Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-Date Expenditure as per MIS (in lakh)	Requisition against work done (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance										
1	MR N/19-20; Motihari/19	N/128 To Sapahi	Project ID: 41708201226	6136 Dt: 20.11.2019	10.500	428.19130	305.93842	92.56432	47 MHD 2020-21 Dt: 31.08.2020	30.05.2021	10.07.2021	2488.076	25	5.00	0.00000	0.00000	304.93000	

[Signature]
Junior Engineer

[Signature]
Asst. Engineer

[Signature]
Sr. Divisional Accounts Officer
Rural Works Department,

[Signature]
Executive Engineer,
Rural Works Department,

R.W.D Work Division Motihari

FORM GFR 19A

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 25.06.2021
MR HEAD-3054 (Initial Rectification with Surface Renewal)

Sl. No.	Name of Scheme	Selection No. of Date with Amount (in Rs. In Laacs)	Amount Received (in Rs. In Laacs)	Particulars
1	Construction of Rural Roads under MR HEAD-3054 (Initial Rectification with Surface Renewal)		4329.29827	Certified that out of Rs.4329.29827 Laacs received during the years 2020-21 in favour of Executive Engineer, R.W.D. Works Division, Motihari A sum of Rs.4154.54928 Laacs has been utilised for the purpose of MR HEAD-3054 (Initial Rectification with Surface Renewal) Scheme as given in the margin or whichever sanctioned and that the balance Rs.174.74899 Laacs remaining unutilised at the end of the period under.
			4329.29827	


- 2 Certified that I have satisfied myself that the conditions on which the grant-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilised for the purpose for which it was sanctioned.

Kinds of exercised :-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction Material have been testes.
- Measurement have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

3 Physical Progress achieved : _

- Construction of Road Works.
- Construction of CD Works.



Sr. Divisional Accounts Officer
Rural Works Department,
Works Division, Motihari


Executive Engineer,
Rural Works Department,
Works Division, Motihari

Steco Analyzer

Name of Customer : Ranjeet Kumar
Name of Work/ Road : Motihari Chhapwa NH28 to Sapahi
Lab Job number : 31708202120
Date : 09 Jul -21
Section No. : 1

Test Date : 09- Jul -21 Road Name : Motihari Chhapwa NH28 to Sapahi
Machine No : 378 Road Type : (R) RURAL ROAD
Start S No : 0.00 KM Side :
Start E No : 10.5 KM Interval
Weather : Normal UIV Range : 806 To 5000 1000 mm/km
Start Location : 26.6748669 Dist Range : 0 To 10.6 0.1 * 1000 m
End Location : 84.847608 Equation : $Y = 0 * X^2 + 0.998 * X + 109.5$

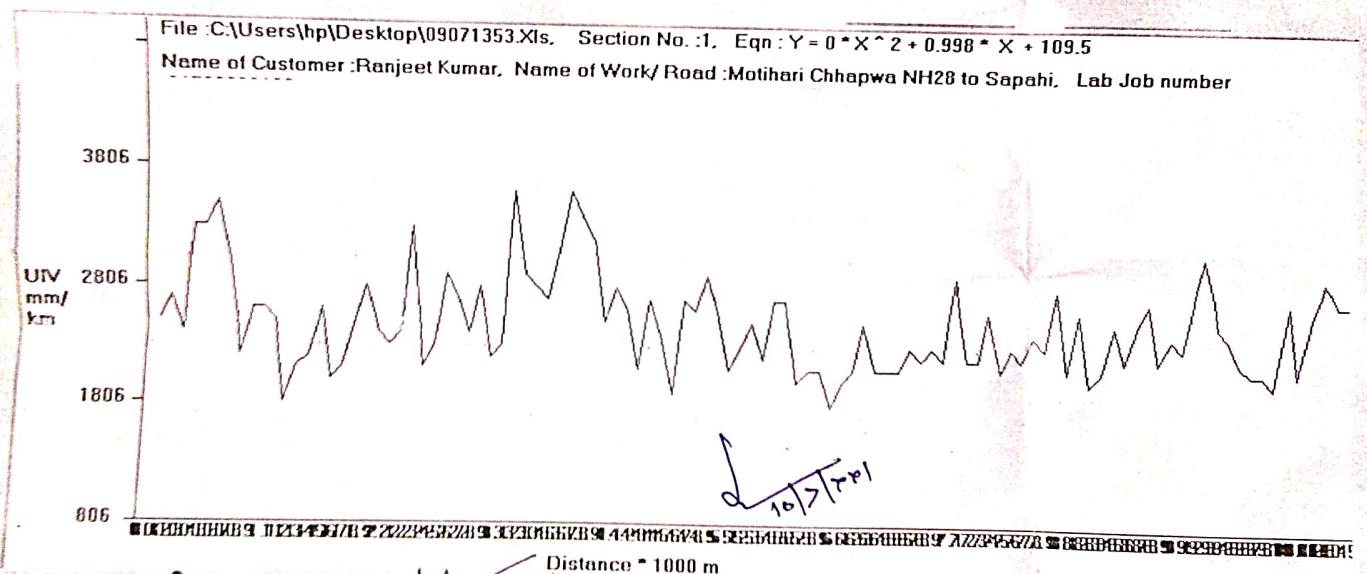

21/7/21
SE

10/07/21
AB

Road Name- Motihari Chhapwa NH28 to Sapahi, Contractor-Ranjeet Kumar

Project ID-31708202120

Date	Time	Section	Length	Bumps	Speed	OR	IRI in	CATEGO	Latitude	Longitud	Event	
No.			in km	in mm	Rate	mm/km	mm/km	RY		e		
							UIV	ROAD				$Y = 0 * X^2 + 0.998 * X + 109.5$
9/7/21	13:28:0	1	0.1	240	0	2400	2504	G	26.67487	84.88689	Normal	X = 2600
9/7/21	13:28:0	1	0.1	260	20.2	2600	2704	G	26.67474	84.88677	Normal	Y = 2704
9/7/21	13:31:10	1	0.1	230	30.3	2300	2404	G	26.67408	84.88508	Normal	
9/7/21	13:32:0	1	0.1	320	20.2	3200	3303	G	26.67357	84.88426	Normal	
9/7/21	13:32:19	1	0.1	320	30.3	3200	3303	G	26.67282	84.8838	Normal	
9/7/21	13:32:19	1	0.1	340	20.2	3400	3502	G	26.67201	84.88342	Normal	(R) RURAL ROAD
9/7/21	13:32:54	1	0.1	290	20.2	2900	3003	G	26.67125	84.88293	Normal	Good Average Poor
9/7/21	13:33:0	1	0.1	210	20.2	2100	2205	G	26.67051	84.88234	Normal	<4000 4001-5000 >5001
9/7/21	13:33:0	1	0.1	250	30.3	2500	2604	G	26.66982	84.8818	Culvert	
9/7/21	13:33:30	1	0.1	250	30.3	2500	2604	G	26.66904	84.88123	Normal	
9/7/21	13:33:30	1	0.1	240	30.3	2400	2504	G	26.66826	84.88088	Culvert	
9/7/21	13:33:30	1	0.1	170	30.3	1700	1806	G	26.66742	84.88052	Culvert	
9/7/21	13:34:5	1	0.1	200	30.3	2000	2105	G	26.66652	84.88056	Normal	
9/7/21	13:34:5	1	0.1	210	30.3	2100	2205	G	26.6658	84.88109	Normal	
9/7/21	13:34:5	1	0.1	250	20.2	2500	2604	G	26.66504	84.88172	Curve	
9/7/21	13:34:40	1	0.1	190	30.3	1900	2005	G	26.66425	84.88155	Normal	
9/7/21	13:34:40	1	0.1	200	40.4	2000	2105	G	26.66336	84.8815	Normal	
9/7/21	13:35:0	1	0.1	240	20.2	2400	2504	G	26.66242	84.8815	Curve	
9/7/21	13:35:16	1	0.1	270	20.2	2700	2804	G	26.66231	84.88057	Culvert	
9/7/21	13:35:16	1	0.1	230	30.3	2300	2404	G	26.66271	84.87971	Normal	
9/7/21	13:35:16	1	0.1	220	30.3	2200	2305	G	26.66299	84.87877	Normal	
9/7/21	13:35:51	1	0.1	230	30.3	2300	2404	G	26.66352	84.87786	Normal	
9/7/21	13:36:0	1	0.1	320	10.1	3200	3303	G	26.6638	84.877	Normal	
9/7/21	13:36:0	1	0.1	200	30.3	2000	2105	G	26.66408	84.87608	Normal	
9/7/21	13:36:26	1	0.1	220	30.3	2200	2305	G	26.66438	84.87513	Normal	
9/7/21	13:36:26	1	0.1	280	20.2	2800	2903	G	26.66487	84.87419	Culvert	
9/7/21	13:37:0	1	0.1	260	30.3	2600	2704	G	26.66523	84.87338	Normal	
9/7/21	13:37:1	1	0.1	230	20.2	2300	2404	G	26.66523	84.87239	Normal	
9/7/21	13:37:1	1	0.1	270	20.2	2700	2804	G	26.66483	84.8716	Normal	
9/7/21	13:37:37	1	0.1	210	30.3	2100	2205	G	26.66438	84.87076	Normal	
9/7/21	13:37:37	1	0.1	220	30.3	2200	2305	G	26.66391	84.86993	Normal	
9/7/21	13:38:0	1	0.1	350	20.2	3500	3602	G	26.66348	84.86901	Normal	
9/7/21	13:38:12	1	0.1	280	20.2	2800	2903	G	26.66285	84.86827	Normal	
9/7/21	13:38:12	1	0.1	270	20.2	2700	2804	G	26.66216	84.86754	Culvert	
9/7/21	13:38:47	1	0.1	260	20.2	2600	2704	G	26.66212	84.86658	Normal	

10/7/21
RC

9/7/21	13:39:0	1	0.1	300	20.2	3000	3103 G	26.66185	84.86584	Normal
9/7/21	13:39:23	1	0.1	350	10.1	3500	3602 G	26.66137	84.86471	Normal
9/7/21	13:40:0	1	0.1	330	10.1	3300	3402 G	26.66085	84.86369	Normal
9/7/21	13:40:33	1	0.1	310	10.1	3100	3203 G	26.66053	84.86293	Normal
9/7/21	13:40:33	1	0.1	240	30.3	2400	2504 G	26.65979	84.86241	Normal
9/7/21	13:40:33	1	0.1	270	30.3	2700	2804 G	26.65895	84.86197	Normal
9/7/21	13:41:0	1	0.1	250	30.3	2500	2604 G	26.6581	84.86167	Normal
9/7/21	13:41:8	1	0.1	200	40.4	2000	2105 G	26.65729	84.86128	Normal
9/7/21	13:41:8	1	0.1	260	30.3	2600	2704 G	26.65644	84.86091	Normal
9/7/21	13:41:8	1	0.1	230	30.3	2300	2404 G	26.6556	84.86062	Normal
9/7/21	13:41:44	1	0.1	180	40.4	1800	1905 G	26.6547	84.86037	Normal
9/7/21	13:41:44	1	0.1	260	40.4	2600	2704 G	26.65384	84.86003	Normal
9/7/21	13:42:0	1	0.1	250	40.4	2500	2604 G	26.65291	84.85966	Normal
9/7/21	13:42:19	1	0.1	280	10.1	2800	2903 G	26.65206	84.85934	Normal
9/7/21	13:42:19	1	0.1	250	20.2	2500	2604 G	26.65121	84.85907	Normal
9/7/21	13:42:54	1	0.1	200	30.3	2000	2105 G	26.65044	84.85874	Normal
9/7/21	13:43:0	1	0.1	220	40.4	2200	2305 G	26.64957	84.85832	Normal
9/7/21	13:43:0	1	0.1	240	30.3	2400	2504 G	26.64882	84.85771	Normal
9/7/21	13:43:0	1	0.1	210	30.3	2100	2205 G	26.64816	84.85707	Normal
9/7/21	13:43:30	1	0.1	260	30.3	2600	2704 G	26.64742	84.85648	Normal
9/7/21	13:43:30	1	0.1	260	30.3	2600	2704 G	26.64667	84.85594	Normal
9/7/21	13:43:30	1	0.1	190	40.4	1900	2005 G	26.64586	84.85561	Normal
9/7/21	13:44:5	1	0.1	200	30.3	2000	2105 G	26.64494	84.85545	Normal
9/7/21	13:44:5	1	0.1	200	40.4	2000	2105 G	26.64405	84.85527	Normal
9/7/21	13:44:5	1	0.1	170	40.4	1700	1806 G	26.64321	84.85508	Normal
9/7/21	13:44:5	1	0.1	190	40.4	1900	2005 G	26.64224	84.85492	Normal
9/7/21	13:44:40	1	0.1	200	30.3	2000	2105 G	26.6414	84.85458	Normal
9/7/21	13:44:40	1	0.1	240	30.3	2400	2504 G	26.64068	84.85399	Normal
9/7/21	13:45:0	1	0.1	200	30.3	2000	2105 G	26.64001	84.85342	Normal
9/7/21	13:45:0	1	0.1	200	40.4	2000	2105 G	26.63926	84.85281	Normal
9/7/21	13:45:15	1	0.1	200	30.3	2000	2105 G	26.63845	84.85224	Normal
9/7/21	13:45:15	1	0.1	220	40.4	2200	2305 G	26.63775	84.85172	Normal
9/7/21	13:45:15	1	0.1	210	40.4	2100	2205 G	26.63697	84.85118	Normal
9/7/21	13:45:51	1	0.1	220	20.2	2200	2305 G	26.63613	84.85066	Normal
9/7/21	13:46:0	1	0.1	210	30.3	2100	2205 G	26.6353	84.85024	Normal
9/7/21	13:46:0	1	0.1	280	30.3	2800	2903 G	26.63449	84.85005	Normal
9/7/21	13:46:0	1	0.1	210	40.4	2100	2205 G	26.63356	84.84993	Normal
9/7/21	13:46:26	1	0.1	210	40.4	2100	2205 G	26.63267	84.84971	Normal
9/7/21	13:46:26	1	0.1	250	20.2	2500	2604 G	26.6318	84.84949	Normal
9/7/21	13:47:0	1	0.1	200	40.4	2000	2105 G	26.63095	84.84919	Normal

10/7
cc

9/7/21	13:47:0	1	0.1	220	30.3	2200	2305 G	26.63006	84.84896	Normal
9/7/21	13:47:0	1	0.1	210	30.3	2100	2205 G	26.62918	84.84884	Normal
9/7/21	13:47:0	1	0.1	230	30.3	2300	2404 G	26.62824	84.84875	Normal
9/7/21	13:47:27	1	0.1	220	30.3	2200	2305 G	26.62744	84.84902	Normal
9/7/21	13:47:27	1	0.1	270	20.2	2700	2804 G	26.62649	84.84902	Normal
9/7/21	13:48:0	1	0.1	200	30.3	2000	2105 G	26.62563	84.84906	Normal
9/7/21	13:48:12	1	0.1	250	30.3	2500	2604 G	26.62474	84.84914	Normal
9/7/21	13:48:12	1	0.1	190	40.4	1900	2005 G	26.62407	84.84973	Normal
9/7/21	13:48:12	1	0.1	200	40.4	2000	2105 G	26.62361	84.85059	Normal
9/7/21	13:48:12	1	0.1	240	30.3	2400	2504 G	26.62269	84.85069	Normal
9/7/21	13:48:46	1	0.1	210	30.3	2100	2205 G	26.6218	84.85057	Normal
9/7/21	13:49:0	1	0.1	240	20.2	2400	2504 G	26.62096	84.85061	Normal
9/7/21	13:49:22	1	0.1	260	20.2	2600	2704 G	26.62015	84.85052	Normal
9/7/21	13:49:22	1	0.1	210	30.3	2100	2205 G	26.61934	84.85003	Normal
9/7/21	13:49:22	1	0.1	230	20.2	2300	2404 G	26.61845	84.84976	Normal
9/7/21	13:50:0	1	0.1	220	30.3	2200	2305 G	26.61755	84.84948	Normal
9/7/21	13:50:0	1	0.1	270	20.2	2700	2804 G	26.61675	84.84909	Normal
9/7/21	13:50:33	1	0.1	300	20.2	3000	3103 G	26.61595	84.84867	Normal
9/7/21	13:50:33	1	0.1	240	30.3	2400	2504 G	26.61516	84.84828	Normal
9/7/21	13:50:33	1	0.1	230	30.3	2300	2404 G	26.61435	84.84785	Normal
9/7/21	13:51:8	1	0.1	210	30.3	2100	2205 G	26.61355	84.84727	Normal
9/7/21	13:51:8	1	0.1	200	30.3	2000	2105 G	26.61292	84.84665	Normal
9/7/21	13:51:8	1	0.1	200	40.4	2000	2105 G	26.61228	84.84591	Normal
9/7/21	13:51:8	1	0.1	190	40.4	1900	2005 G	26.61164	84.84522	Normal
9/7/21	13:51:44	1	0.1	260	30.3	2600	2704 G	26.61097	84.84449	Normal
9/7/21	13:52:19	1	0.1	200	10.1	2000	2105 G	26.61068	84.84456	Normal
9/7/21	13:52:19	1	0.1	250	20.2	2500	2604 G	26.61107	84.84547	Normal
9/7/21	13:52:19	1	0.1	280	30.3	2800	2903 G	26.61144	84.84635	Normal
9/7/21	13:53:0	1	0.1	260	30.3	2600	2704 G	26.61181	84.84726	Normal
9/7/21	13:53:0	1	0.1	260	20.2	2600	2704 G	26.61197	84.84761	Normal

Total IRI 261248
Average IRI 2488.076

JE

AE

Executive Engineer
Rural Works Department
Works Division, Motihari
