

Inspection Report For Flood Damage Work

Date:

1. Name of PIUs: R.W.D Gopalgarh-2
2. Name of Block/Road: Barauli / Piprahiya to Nauri P.C.C Path.

A For Road

1. Damage Location/ Chainage: CH-100M to 1230M.
2. Damage Length: 110.00 m
3. Nature of Damage: Flood damaged.
4. Details of Restoration Works:

- i. Material being used in Restoration Works: Brick Bats.
- ii. Equipments / Tools being used in Restoration Works: Tractor labour Etc.
- iii. Procedure taken up in Restoration Works: As per S.O.P.
- iv. Restored Length: 110.00 m

B For Bridge

1. Damage Location / Chainage: N.A
2. Damage Length: N.A.
3. Nature of Damage: N.A.
4. Details of Restoration Works:
- i. Material being used in Restoration Works:
- ii. Equipments / Tools being used in Restoration Works:
- iii. Procedure taken up in Restoration Works:
- iv. Restored Length:

Rajesh
24/11/2020
JE

AE

24/11/20
EE

Signature
(Name of inspector)



Edit with WPS Office



ग्रामीण कार्य विभाग

Rural Works Department, Govt. of Bihar

बिहार सरकार

FLOOD DAMAGED REPAIR (F.D.R.)

STATE :- BIHAR
DISTRICT :- GOPALGANJ
BLOCK :- BARAULI

Piprahiya To Neuri PCC Path

ESTIMATED COST - RS.

~~609475.00~~
~~659700.00~~
6,49,500.00

SUBMITTED BY :-
EXECUTIVE ENGINEER
RWD (W) DIVISION
GOPALGANJ-2

Report

Name of Work

:- Motorable work of Piprahiya To Neuri PCC Path

Estimated Cost

:- ~~604475.00~~
~~659700.00~~
6,09,500.00

Total length of Road


:- 1.230 km


Description


:- The present estimate has been farmed under the supervision of Assistant engineer in accordance with the order of Executive Engineer, RWD, WD Gopalganj-2, letter No. - 1574 dated 18-08-2020. The part of above mentioned road has been damaged due to heavy rain/flood. And due to this damage the transporation has been obstructed. The immediate motorable work is necessary in public interest. Villagers will be benefitted by the completion of this motorable work.

In the estimate there has been a provision of repairing the damaged part of the road & making it motorable by filling brickbats. In the context of post flood scenario there is still the flow of water which prevails through the damaged part of the road. Hence there has been a provision of laying R.C.C. NP3 1000 MM Dia hume pipe.

In this estimate the rate of raw materials and labour wages has been prepared after the analysis of new rate. This estimate is as per the specifications. The estimate is devoted to technical and administrative acceptance.


J.E.


A.E.


E.E.

Estimated Estimate For Motorable Work in Road from Piprahiya To Neuri PCC Path damaged due to Heavy rain/flood for year 2020-2021

Items	No.	L (M.)	W (M.)	D (M.)	Qty.	Unit	Rate	Amount
Providing brick bats billed in latches including all cost of labour & material with all complete job.								
CH -100 M to 1230 M	1	6.00	1.05	0.45	2.84	M3		
	1	10.00	1.00	0.25	2.50	M3		
	1	4.00	2.00	0.25	2.00	M3		
	1	15.00	0.25	1.90	7.13	M3		
	1	3.00	0.20	1.00	0.60	M3		
	1	15.00	0.25	1.80	6.75	M3		
	1	11.00	1.00	1.60	17.60	M3		
	1	6.00	1.20	1.50	10.80	M3		
	1	3.00	1.30	2.10	8.19	M3		
	1	4.00	1.40	2.00	11.20	M3		
	1	11.00	2.20	2.10	50.82	M3		
	1	15.00	2.50	3.00	112.50	M3		
	1	4.00	2.00	2.60	20.80	M3		
	1	3.00	2.50	2.50	18.75	M3		599578- 628403-4
Less for H.P.	1.58	1.23	1.23	5.00	11.95	M3	2412-11	603441=60
					260.52		2427.65	632446.74
Providing & laying 1000 MM Dia NP3 Hume Pipe in single row -do-do- complete job.	2	2.50			5.00	M	2744.50 4159.56	1372320 20797.80
							613307	603441=60
							6421260	653244.54
							6421260	603441=60
							6421260	6532.45
Add 1 % Contingency							613307	603441=60
							Total	659776.99
							Say	659700.00

Rajesh
24/11/2020
J.E.

S. M. 24/11/2020
A.E.

P. 24/11/20
E.E.

Damit
24/11/2020
J.E.

Technically approved for Rs 6,194,500 (Rupees Six Lacs
Nineteen Thousand & Four Hundred & Fifty) only
25/11/21

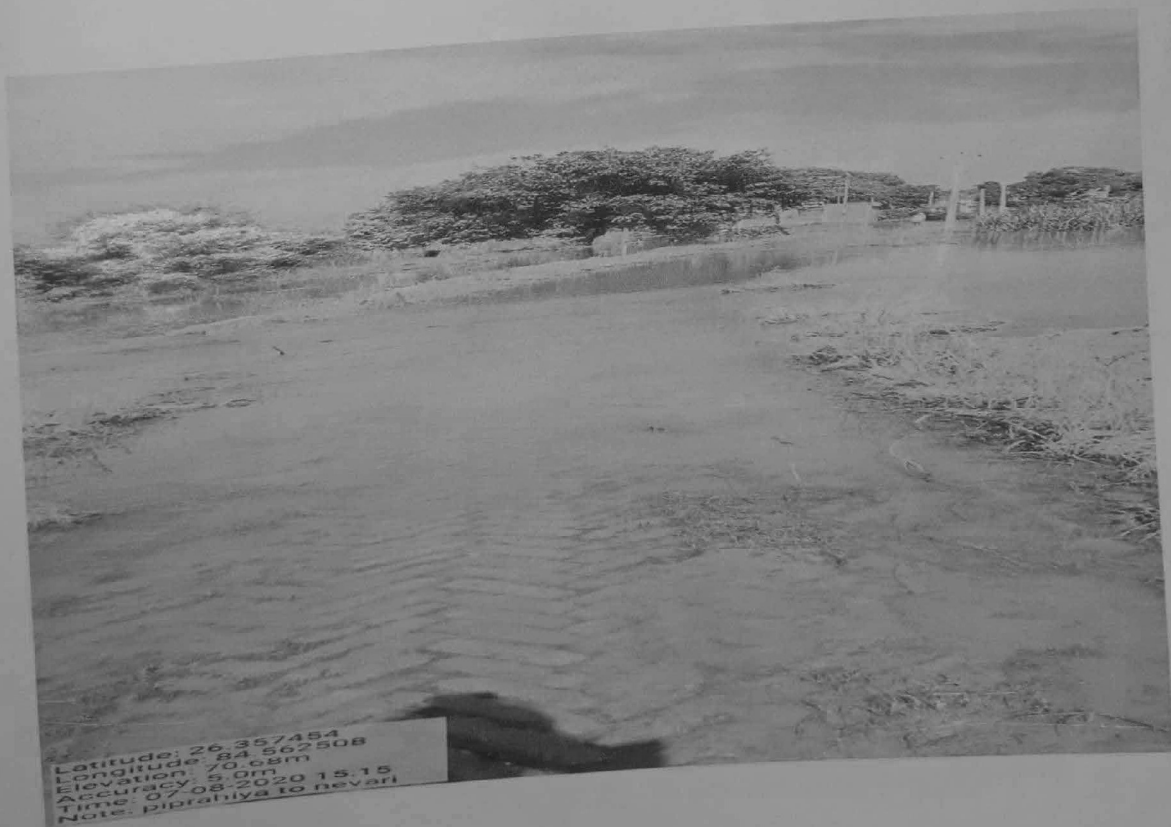
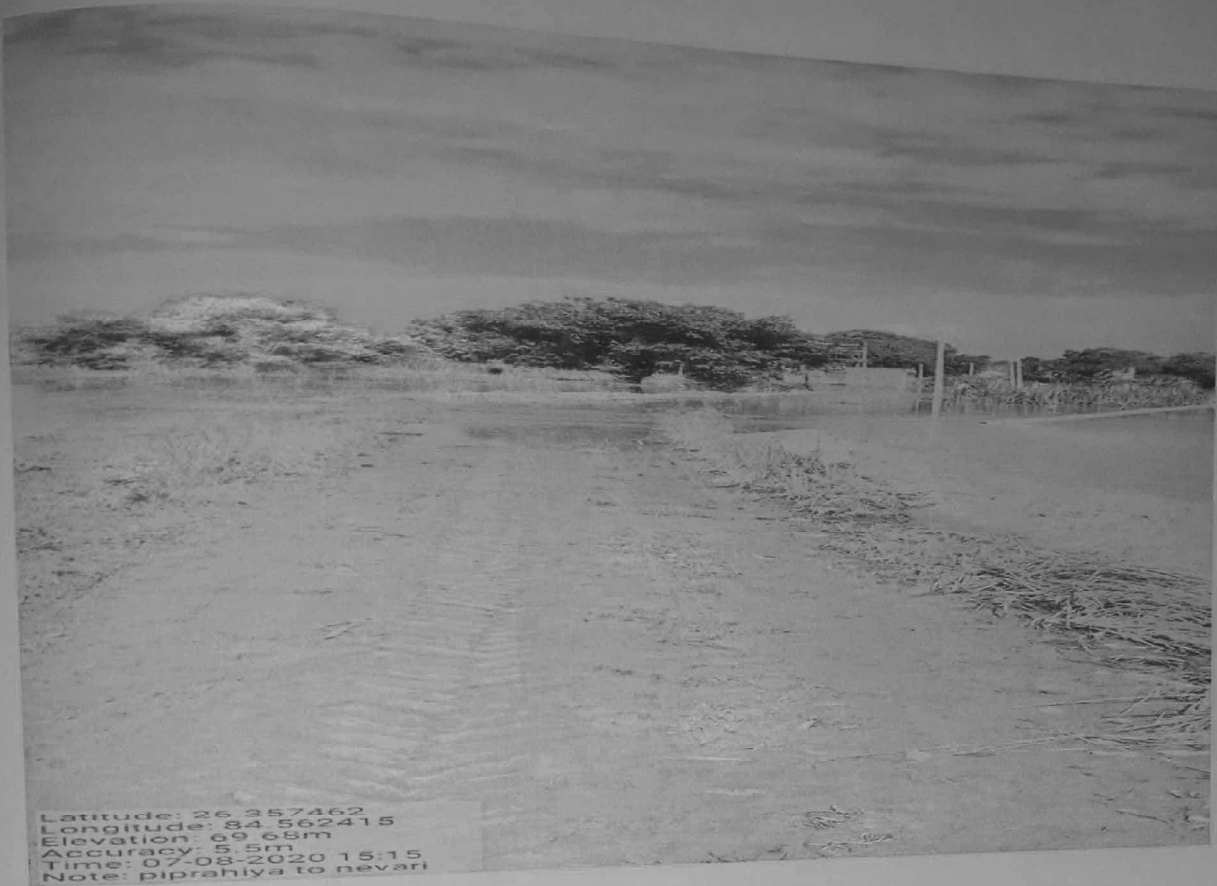
अधीक्षण अभियंता
प्रमाणन कार्य विभाग कार्य अंशक-सका
25/11/21



Piprahiya
20/09/20

20/09/20

Name of Road :- Piprahiya To Nevari



Rajesh
J.E.

24/11/2020
102
