

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल मसौढ़ी।

पत्रांक.....19...[Signature]... मसौढ़ी .

दिनांक27.01.2021

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल मसौढ़ी

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
ब्राडा पटना।

विषय:— New Maintenance Policy-2018 योजनान्तर्गत चल रहे कार्यों के भुगतान हेतु
आवंटन अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में इस प्रमंडल के अंतर्गत New Maintenance Policy-2018 अंतर्गत पथों में चल रहे कार्यों पर किये गये व्ययों के भुगतान हेतु आवंटन की आवश्यकता है।

अतः आग्रह है कि संलग्न विवरणी के अनुसार विभिन्न पथों में आवंटन शीघ्र उपलब्ध कारने की कृपा की जाए।

अनु० यथोक्त

विश्वासभाजन

कार्यपालक अभियंता
[Signature]

ग्रामीण कार्य विभाग, कार्य प्रमंडल मसौढ़ी।

Requisition Formate for Scheme Head - MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :
Masaurhi

Name of Works Division : Masaurhi										Agreement Details																	
Road Details				A A Details																							
SL no.	Pkg no.	Road Name	Project ID	Main Work Amount	Maintenanc e Amount	Total Amount	Total Length	Administrative Approval (AA) Itno.	AA Date	Main Work Amount	Maintenanc e	Date	Date Of Completion	Ref.No.	Length	Actual Date of Completion	Value of IRI (in MM/Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	Upto Date expenditu re as Per MIS (In Lakh)	Requisition Against Work done (In Lakh)	Remarks				
1	MR-N/19-20 Masaurhi/0	Sain Kadirganj Road to Lodeepur via Tarma	1.01E+10	50.983	14.618	70.699	2	539	08-Feb-19	49.59	13.7516	22-Jan-20	21-Oct-20	15/MBD/19-2020	2	04.12.2020	28.445 (Avg)	25mm	5%	26.0834	26.08341	23.50659					
2	MR-N/19-20 Masaurhi/0	MUSNAPAR MASAUHRI PATH - TELHARA (BR-26R 246)	1.01E+10	66.046	17.491	90.142	2.4	539	08-Feb-19	64.94	15.4915	22-Jan-20	21-Oct-20	15/MBD/19-2020	2.4	30.11.2020	28.204 (Avg)	25mm	5%	36.3192	36.31918	28.61782					
3	MR-N/19-20 Masaurhi/0	KISTIPUR MADHUBAN VIA KOSUT	1.01E+10	230.41	61.562	291.97	8.66	539	08-Feb-19	227.1	56.2904	22-Jan-20	21-Oct-20	15/MBD/19-2020	8.66	22.12.2020	29.87(Avg)	25mm	5%	106.907	106.9071	120.1429					
				347.44	93.671	457.82	13.10			341.6	65.5335				13.06	0		0		169.31	169.3062	172.26728					

1. Signed Hard Copy and Soft copy (in Excel) of recorded IRI is Enclosed
2. Upto Date Physical Progress has been Uploaded in MIS

Handwritten signature
27.01.21

Handwritten signature
EXECUTIVE ENGINEER
RURAL WORKS DEPARTMENT
WORKS DIVISION, MASAUHRI

NAME OF THE ROAD : MUSNAPUR MASOURHI PATH TO TELHARA

LENGTH OF THE ROAD : 2.4 KM

PACKAGE NO. : MR-N/19-20/MASOURHI/01

DIVISION : MASOURHI

BLOCK : DHANARUA

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV mm/km	CATEGORY ROAD	IRI	Latitude	Longitude	Event			
22/10/20	11:56:6	45	0.1	320	0	3200	3273	G	4.34	25.35861	85.101665	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
22/10/20	11:56:26	45	0.1	150	30.3	1500	1682	G	2.4	25.35943	85.101935	Normal	$X = 2800$		
22/10/20	11:56:41	45	0.1	250	20.2	2500	2618	G	3.56	25.36015	85.1017	Normal	$Y = 2899$		
22/10/20	11:57:0	45	0.1	230	30.3	2300	2431	G	3.13	25.36043	85.100757	Curve			
22/10/20	11:57:10	45	0.1	150	20.2	1500	1682	G	2.4	25.36122	85.100975	Normal	(R) RURAL ROAD		
22/10/20	11:57:18	45	0.1	190	30.3	1900	2056	G	2.87	25.36216	85.101262	Normal	Good	Average	Poor
22/10/20	11:57:28	45	0.1	110	30.3	1100	1308	G	1.91	25.36301	85.101548	Normal	<4000	4001-5000	>5001
22/10/20	11:57:40	45	0.1	200	30.3	2000	2150	G	2.98	25.36381	85.101985	Normal			
22/10/20	11:58:0	45	0.1	210	20.2	2100	2244	G	3.1	25.3647	85.102272	Normal			
22/10/20	11:58:10	45	0.1	140	30.3	1400	1588	G	2.28	25.36551	85.101935	Normal			
22/10/20	11:58:25	45	0.1	260	30.3	2600	2712	G	3.67	25.36605	85.101143	Normal			
22/10/20	11:58:39	45	0.1	260	30.3	2600	2712	G	3.67	25.36633	85.10015	Normal			
22/10/20	11:58:45	45	0.1	180	30.3	1800	1963	G	2.75	25.3665	85.99192	Normal			
22/10/20	11:58:59	45	0.1	160	30.3	1600	1776	G	2.52	25.36672	85.98248	Normal			
22/10/20	11:59:4	45	0.1	190	20.2	1900	2056	G	2.87	25.36722	85.97677	Normal			
22/10/20	11:59:24	45	0.1	130	30.3	1300	1495	G	2.16	25.36811	85.97862	Normal			
22/10/20	11:59:38	45	0.1	170	30.3	1700	1869	G	2.63	25.36906	85.9803	Normal			
22/10/20	11:59:45	45	0.1	130	30.3	1300	1495	G	2.16	25.36997	85.98248	Normal			
22/10/20	11:59:51	45	0.1	100	20.2	1000	1214	G	1.8	25.37083	85.9838	Normal			
22/10/20	12:0:0	45	0.1	190	30.3	1900	2056	G	2.87	25.37176	85.98518	Normal			
22/10/20	12:0:14	45	0.1	120	30.3	1200	1401	G	2.03	25.37262	85.9877	Normal			
22/10/20	12:0:24	45	0.1	190	20.2	1900	2056	G	2.87	25.37346	85.99225	Normal			
22/10/20	12:0:50	45	0.1	280	20.2	2800	2899	G	3.9	25.37413	85.98737	Normal			
TOTAL			2.3	4310	595.9	43100	46736		64.87	583.4218	1967.046197				

22.10.20
J.E. Dhanarua

22/10/20
H.E.
Dhanarua

Arch
22/10
R.W.D. WORKS DR. MESSINA

Name of Customer : M/S A K BROTHER'S
 Name of Work/ Road : MUSNAPUR MASAUHRI PATH
 Lab Job number :
 Date : 22-10-2020
 Section No. : 45


Test Date : 22-10-2020 Road Name : SAURHI PATH TO TELHADA
 Machine No :
 Road Type : (R) RURAL ROAD
 Start S No :
 Side :
 Start E No :
 Interval :
 Weather :
 UV Range : 214 To 5000 1000 mm/km
 Start Location :
 Dist Range : 0 To 2.4 0.1 * 1000 m
 End Location :
 Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View

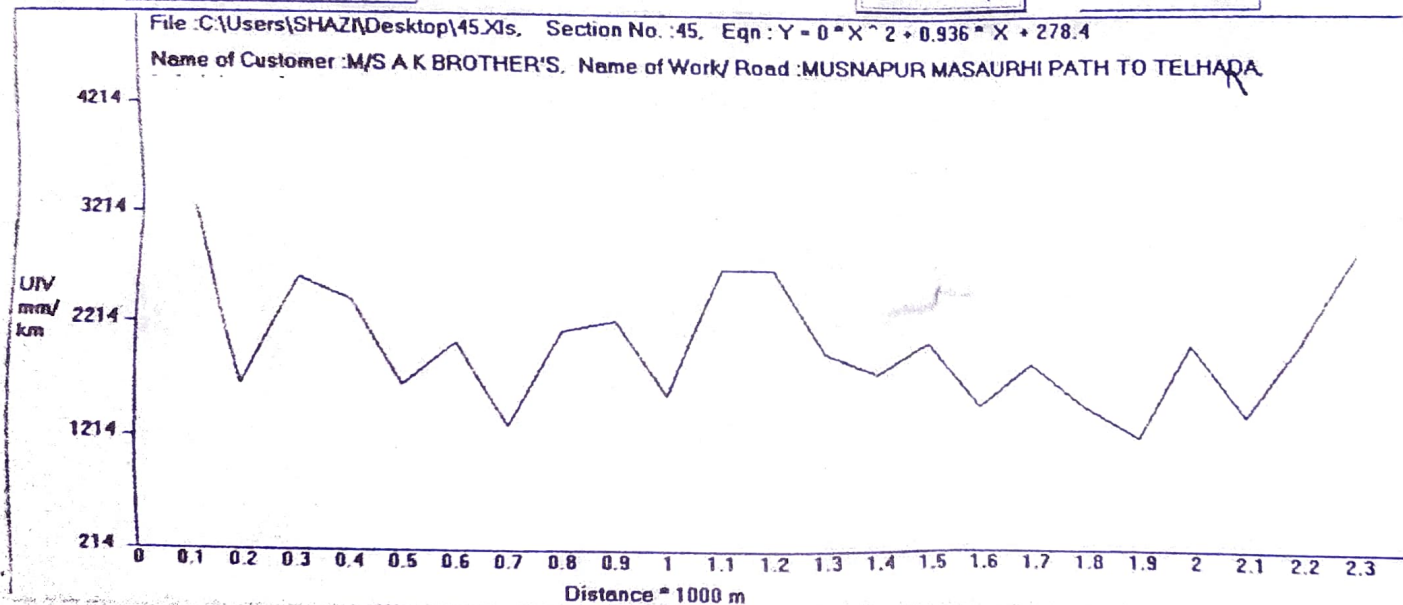

22.10.20
 J.E. Dharam

22/10/20
 A.E.

22/10
 Executive Engineer
 R.W.D. Works Div. Masaurhi
