

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, सीवान-01

पत्रांक 2043236

दिनांक 11/2/2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सीवान-01

सेवा में,

नोडल पदाधिकारी (3054) MR
ग्रामीण कार्य विभाग,
बिहार पटना


विषय:- योजना शीर्ष नई अनुरक्षण नीति 2018 MR/3054 अंतर्गत पथो मे मरम्मती हेतु अधियाचना के
संबंध मे ।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के आलोक मे कहना है कि इस प्रमंडल अंतर्गत योजना शीर्ष नई
अनुरक्षण नीति 2018 MR/3054 अंतर्गत संलग्न विहित प्रपत्र मे 21.60000 लाख रुपए मात्र आवंटन
दने की कृपा की जाय ।

अनु0- अधियाचना पत्र, Bump Integrator Equipment Report की छाया प्रति, एकरारनामा की छाया
प्रति ।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सीवान-01
10-02-21

Requisition Format for Scheme Head MR (3054) under Bihar Rural Road Maintenance Policy 2018 (Initial Rectification & Surface Renewal)

Name of the Works Division :- Siwan-01

Sl. No.	Package No.	Name of Road	Project_ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in percentage)	Previous Total Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km.)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SI/SIW/19/01	Madhopur se Suraiya	31406702014	1880/24.06.2019	3.400	99.9	55.84	28.42	44MBD/2019-20/23.01.2020	22-10-20	05-12-20	2902	25mm	5.00%	32.40000	32.40000	21.60000	

- 1 Signed Hard Copy and Soft Copy (in excell) or recorded IRI is enclosed.
- 2 Up- to- date Physical Progress has been uploaded in MIS.


Executive Engineer
RWD, Siwan
10.02.21

Road Name :- Madhopur to surahiya

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD	Latitude	Longitude	Event
26/11/20	10:23:2	68	0.1	320	0	3200	3203	G	26.33008	84.47064	Culvert
26/11/20	10:23:38	68	0.1	210	10.1	2100	2243	G	26.33096	84.47069	Normal
26/11/20	10:24:0	68	0.1	260	10.1	2600	2679	G	26.33179	84.47057	Normal
26/11/20	10:24:12	68	0.1	250	10.1	2500	2592	G	26.33263	84.47057	Normal
26/11/20	10:24:47	68	0.1	230	10.1	2300	2418	G	26.33347	84.47045	Culvert
26/11/20	10:25:0	68	0.1	280	10.1	2800	2854	G	26.33431	84.47034	Normal
26/11/20	10:25:22	68	0.1	400	10.1	4000	3902	G	26.33522	84.4704	Normal
26/11/20	10:26:0	68	0.1	370	10.1	3700	3640	G	26.33608	84.47059	Normal
26/11/20	10:26:33	68	0.1	310	10.1	3100	3116	G	26.3369	84.47066	Curve
26/11/20	10:27:0	68	0.1	290	10.1	2900	2941	G	26.33777	84.47086	Normal
26/11/20	10:27:8	68	0.1	270	10.1	2700	2767	G	26.3386	84.47111	Curve
26/11/20	10:27:44	68	0.1	310	10.1	3100	3116	G	26.33939	84.47094	Culvert
26/11/20	10:28:19	68	0.1	300	10.1	3000	3029	G	26.34006	84.47089	Curve
26/11/20	10:28:19	68	0.1	330	10.1	3300	3291	G	26.34072	84.47069	Normal
26/11/20	10:29:0	68	0.1	240	10.1	2400	2505	G	26.34147	84.47114	Normal
26/11/20	10:29:29	68	0.1	340	10.1	3400	3378	G	26.34206	84.47131	Curve
26/11/20	10:30:5	68	0.1	310	10.1	3100	3116	G	26.34245	84.47045	Normal
26/11/20	10:30:5	68	0.1	310	10.1	3100	3116	G	26.34296	84.46966	Normal
26/11/20	10:30:40	68	0.1	320	10.1	3200	3203	G	26.34351	84.46896	Normal
26/11/20	10:31:15	68	0.1	340	10.1	3400	3378	G	26.3437	84.46805	Normal
26/11/20	10:31:15	68	0.1	340	10.1	3400	3378	G	26.34412	84.46724	Culvert
26/11/20	10:32:0	68	0.1	280	10.1	2800	2854	G	26.34457	84.46643	Normal
26/11/20	10:32:26	68	0.1	230	10.1	2300	2418	G	26.34491	84.46557	Normal
26/11/20	10:33:1	68	0.1	250	10.1	2500	2592	G	26.3452	84.46465	Normal
26/11/20	10:33:1	68	0.1	300	10.1	3000	3029	G	26.34531	84.46369	Normal
26/11/20	10:34:0	68	0.1	270	10.1	2700	2767	G	26.34549	84.46274	Speed Breaker
26/11/20	10:34:12	68	0.1	320	10.1	3200	3203	G	26.34563	84.4618	Normal
26/11/20	10:34:47	68	0.1	240	10.1	2400	2505	G	26.34578	84.46088	Curve
26/11/20	10:35:22	68	0.1	230	10.1	2300	2418	G	26.34553	84.45995	Normal
26/11/20	10:35:22	68	0.1	180	10.1	1800	1981	G	26.34551	84.45897	Normal
26/11/20	10:36:0	68	0.1	190	10.1	1900	2068	G	26.34547	84.45808	Culvert
26/11/20	10:36:33	68	0.1	300	10.1	3000	3029	G	26.34544	84.45709	Normal
26/11/20	10:37:8	68	0.1	180	10.1	1800	1981	G	26.34552	84.45613	Culvert
26/11/20	10:37:43	68	0.076	310	10.1	4079	3971	G	26.34562	84.45535	Normal

$$Y = 0 * X^2 + 0.873 * X + 410.1$$

$$X = 4079$$

$$Y = 3971$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

15/11/20

15/11/20

Steco Analyzer


Name of Customer : Shailcon Construction
 Name of Work/ Road : Madhopur to Surahaiya
 Lab Job number :
 Date : 02-Jun-09
 Section No : 68

Test Date : 28-Apr-10 Road Name : Madhopur to Surahaiya
 Machine No : 390 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UIV Range : 981 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 35 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.073 * X + 410.1$

Print Generate Report and Graph

Redraw Graph

Map View

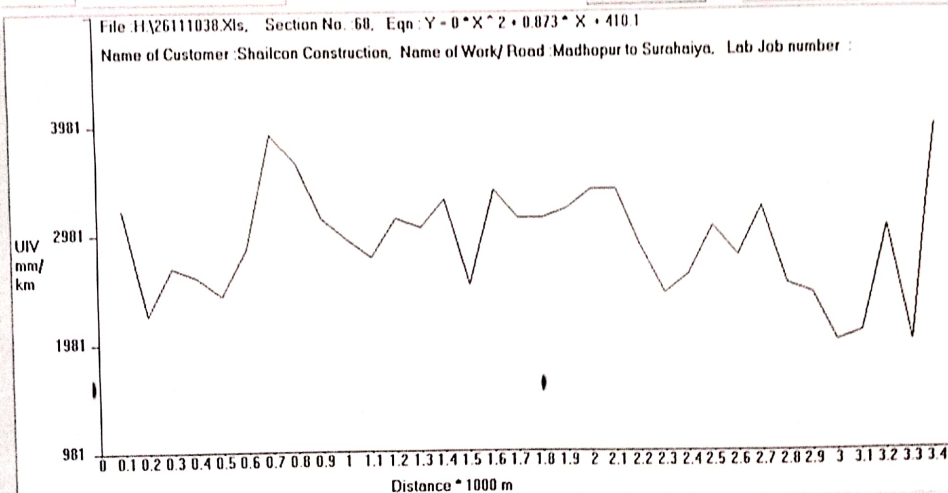

Handwritten signature
 15/11/09

Handwritten signature
 15/11/09

ONE THOUSAND RUPEES

AGREEMENT

Agreement No. M/R-N/19-20

Date: 10.12.2019

This agreement made the _____ day of _____ 2020 between Executive Engineer, R.W.D. Works Division, Siwan-01 (hereinafter called "the Employer"), of the one part, and M/s Shailcon Construction, Vill.- Rasauti, Po. Katoya Dist.-Gopalganj (hereinafter called "the Contractor"), of the other part.

Whereas the Employer is desirous that the Contractor execute M/R-N/19-20 Siwan-1/01 (Tender ID: 79246) and their maintenance for five years in Block-Baraharia, Dist.- Siwan, State Bihar (hereinafter called the works") and the Employer has accepted the bid by the Contractor for the execution and completion of such Works and the remedying of any defects therein at a cost of Rs. 2,52,90,955.00 (Rupees two Corer fifty two lacs Ninty thousand nine hundred fifty five only) (Below 10% from S.O.R.) vide LOA No.2275, Dt. 10.12.2019

Road	Length (K.M.)
1. Haradiya to Sundarpur	5.500
2. Mathpuri to Surahiya	3.400
