

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक- 239(05/0)

पालीगंज/दिनांक-18/2/21

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
सह- सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- MR (3054) under Bihar Rural Road Maintenance Policy -2018 अन्तर्गत
कार्यन्वित की जा रही योजना का आवंटन हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि निम्नलिखित योजना का कुल राशि रुपये
21,70,842.00 मात्र का आवंटन हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई
समर्पित किया जाता है।

अनु० :- (1) अधियाचना विहित प्रपत्र में


विश्वासभाजन

18/2/21
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।
5/2/21

Requisition Format for Scheme Head - MR (3054) under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification and Surface Renewal)

Name of Work Division:- Paliganj

Name of Work Division:- Paliganj																		
Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 Paliganj/10	Karapura to Murka path	NEA220001640	Lt no. 6459 dt. 13.12.2019	2.23	31.57500	56.762	23.61932	07/MBD/20 20-21 dt. 23.06.20	22.03.2021	-	Details Attached	25	5.12%	48.82817	48.82817	3.15468	
2	MR-N/19-20 Paliganj/10	Pali Chandos path to Karapura via Karhra path	10100104046	Lt no. 6459 dt. 13.12.2019	3.15	105.19900	72.018	33.4193	07/MBD/20 20-21 dt. 23.06.20	22.03.2021	-	Details Attached	25	5.05%	48.47585	48.47585	18.55374	
Total																21.70842		


 Executive Engineer
 RWD Works Division Paliganj

LENGTH OF THE ROAD : 3.150 KM

NAME OF THE ROAD : PALI CHANDAU PATH TO KARANPURA VIA KARHARA PATH

BLOCK : PALIGANJ

DIVISION : PALIGANJ

PACKAGE NO : MR-N/19-20/PALIGANJ/10

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event	Y = 0 * X ^ 2 + 0.936 * X + 278.4 X = 588 Y = 864	Good <4000	Average 4001-5000	Poor >5001
19/10/20	11:18:13	41	0.1	290	0	2900	3035	G	4.05	25.29766	84.866868	Normal				
19/10/20	11:18:13	41	0.1	190	20.2	1900	2096	G	2.92	25.29851	84.867053	Normal				
19/10/20	11:18:48	41	0.1	60	30.3	600	875	G	1.33	25.29936	84.86749	Normal				
19/10/20	11:19:0	41	0.1	160	30.3	1600	1814	G	2.57	25.30006	84.867978	Normal				
19/10/20	11:19:0	41	0.1	120	30.3	1200	1438	G	2.08	25.30067	84.86872	Normal				
19/10/20	11:19:23	41	0.1	140	30.3	1400	1626	G	2.32	25.30128	84.869528	Normal				
19/10/20	11:19:23	41	0.1	230	30.3	2300	2471	G	3.38	25.30204	84.869898	Normal				
19/10/20	11:19:23	41	0.1	280	10.1	2800	2941	G	3.94	25.30282	84.870302	Normal				
19/10/20	11:20:0	41	0.1	160	30.3	1600	1814	G	2.56	25.30351	84.870908	Normal				
19/10/20	11:20:0	41	0.1	160	40.4	1600	1814	G	2.56	25.30422	84.871548	Normal				
19/10/20	11:20:0	41	0.1	100	20.2	1000	1251	G	1.84	25.3048	84.872272	Normal				
19/10/20	11:21:9	41	0.1	330	0	3300	3410	G	4.5	25.3052	84.873282	Speed Breaker				
19/10/20	11:22:20	41	0.1	170	10.1	1700	1908	G	2.68	25.30528	84.87505	Curve				
19/10/20	11:23:0	41	0.1	200	10.1	2000	2190	G	3.04	25.30599	84.875505	Normal				
19/10/20	11:23:0	41	0.1	140	10.1	1400	1626	G	2.32	25.30676	84.875773	Normal				
19/10/20	11:23:30	41	0.1	280	20.2	2800	2941	G	3.94	25.30761	84.875622	Normal				
19/10/20	11:23:30	41	0.1	240	30.3	2400	2565	G	3.5	25.30848	84.87574	Normal				
19/10/20	11:24:0	41	0.1	160	30.3	1600	1814	G	2.57	25.30937	84.87601	Normal				
19/10/20	11:24:6	41	0.1	140	30.3	1400	1626	G	2.33	25.31028	84.87638	Normal				
19/10/20	11:24:6	41	0.1	100	20.2	1000	1251	G	1.84	25.31113	84.87668	Normal				
19/10/20	11:24:6	41	0.1	180	30.3	1800	2002	G	2.8	25.31198	84.876952	Normal				
19/10/20	11:24:41	41	0.1	180	30.3	1800	2002	G	2.8	25.31286	84.877222	Normal				
19/10/20	11:25:0	41	0.1	190	30.3	1900	2096	G	2.92	25.31359	84.877827	Normal				
19/10/20	11:25:0	41	0.1	140	30.3	1400	1626	G	2.33	25.3144	84.87835	Normal				
19/10/20	11:25:16	41	0.1	150	30.3	1500	1720	G	2.45	25.31527	84.878618	Normal				
19/10/20	11:25:16	41	0.1	90	30.3	900	1157	G	1.72	25.31614	84.87882	Normal				
19/10/20	11:25:16	41	0.1	190	30.3	1900	2096	G	2.92	25.317	84.879007	Normal				
19/10/20	11:25:52	41	0.1	150	30.3	1500	1720	G	2.45	25.31786	84.879123	Normal				
19/10/20	11:26:0	41	0.1	120	20.2	1200	1438	G	2.08	25.31881	84.879325	Normal				
19/10/20	11:26:0	41	0.1	100	30.3	1000	1251	G	1.84	25.31971	84.879612	Normal				
19/10/20	11:27:2	41	0.034	20	0	588	864	G	1.32	25.32009	84.87968	Curve				
TOTAL									81.9	784.5627	2631.107143					

Executive Engineer
Rural Works Deptt.
Work Division Paliganj

19/10/20
11:27:2

Name of Customer : RAM SEWAK PRASAD
 Name of Work / Road : PALI CHANDLAUS PATH TO K/
 Lab Job number :
 Date : 19-10-2020
 Section No. : 41


Test Date : 19-10-2020 Road Name : WPUA VIA KARHARA PATH
 Machine No. : Road Type : (R) RURAL ROAD
 Start S No. : Side :
 Start E No. : Interval
 Weather : UIV Range : -136 To 4000 mm/km
 Start Location : Dist Range : 0 To 32 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print Generate Report and Graph

Redraw Graph

Map View

File : C:\Users\Shazia\Desktop\41 DATA.xlsx Section No. : 41, Eqn : $Y = 0 * X^2 + 0.936 * X + 278.4$
 Name of Customer : RAM SEWAK PRASAD, Name of Work / Road : PALI CHANDLAUS PATH TO KARANPURA VIA

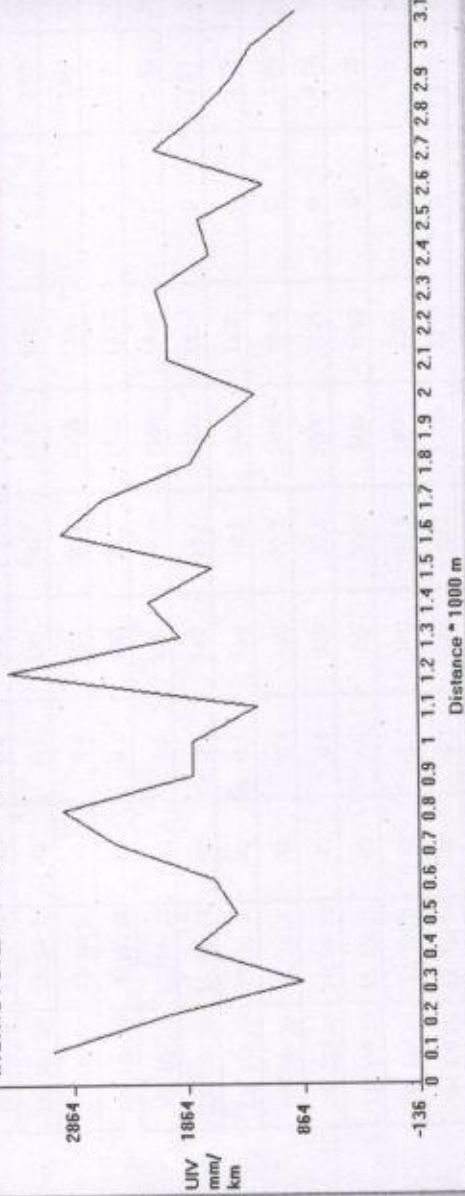

Er. Anshu Engineer
 Rural Works Deptt.
 Work Division Pali Ganj

19/10/20
 Anshu

PACKAGE NO. : MR-N/19-20/PALIGANJ/10

LENGTH OF THE ROAD : 2.230 KM

NAME OF THE ROAD : KARANPURA TO MURKA PATH

BLOCK : PALIGANJ

DIVISION : PALIGANJ

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY	IRI	Latitude	Longitude	Event			
		No.						ROAD							
19/10/20	11:52:7	42	0.1	300	0	3000	3129	G	4.17	25.31928	84.875555	Normal			$Y = 0 * X^2 + 0.936 * X + 278.4$
19/10/20	11:52:42	42	0.1	150	20.2	1500	1720	G	2.45	25.31998	84.875925	Normal			X = 2308
19/10/20	11:53:0	42	0.1	210	30.3	2100	2283	G	3.15	25.31983	84.876952	Normal			Y = 2479
19/10/20	11:53:0	42	0.1	220	30.3	2200	2377	G	3.26	25.32022	84.877827	Normal			
19/10/20	11:53:18	42	0.1	80	30.3	800	1063	G	1.58	25.32016	84.87882	Normal			RURAL ROAD
19/10/20	11:53:18	42	0.1	180	20.2	1800	2002	G	2.8	25.32017	84.879763	Normal			
19/10/20	11:53:18	42	0.1	260	30.3	2600	2753	G	3.72	25.32102	84.88005	Normal			
19/10/20	11:54:0	42	0.1	300	30.3	3000	3129	G	4.17	25.32173	84.880555	Normal			
19/10/20	11:54:0	42	0.1	170	30.3	1700	1908	G	2.68	25.32268	84.88079	Curve			
19/10/20	11:54:0	42	0.1	110	30.3	1100	1344	G	1.96	25.32304	84.881532	Normal			
19/10/20	11:54:28	42	0.1	130	30.3	1300	1532	G	2.2	25.32321	84.882525	Normal			
19/10/20	11:54:28	42	0.1	110	30.3	1100	1344	G	1.96	25.32345	84.88348	Normal			
19/10/20	11:54:28	42	0.1	160	30.3	1600	1814	G	2.57	25.3235	84.884512	Normal			
19/10/20	11:55:4	42	0.1	140	20.2	1400	1626	G	2.33	25.32382	84.885453	Normal			
19/10/20	11:55:4	42	0.1	110	20.2	1100	1344	G	1.96	25.32324	84.885908	Normal			
19/10/20	11:55:39	42	0.1	300	20.2	3000	3129	G	4.17	25.32291	84.886532	Normal			
19/10/20	11:55:39	42	0.1	80	30.3	800	1063	G	1.58	25.32166	84.887407	Normal			
19/10/20	11:56:0	42	0.1	180	30.3	1800	2002	G	2.8	25.32176	84.887423	Normal			
19/10/20	11:56:14	42	0.1	220	30.3	2200	2377	G	3.26	25.32093	84.887743	Normal			
19/10/20	11:56:14	42	0.1	130	30.3	1300	1532	G	2.2	25.32031	84.88842	Normal			
19/10/20	11:56:14	42	0.1	210	20.2	2100	2283	G	3.15	25.31961	84.88909	Normal			
19/10/20	11:56:50	42	0.013	30	30.3	2308	2479	G	3.38	25.31959	84.889275	Normal			
TOTAL			2.113	3780	575.7	39808	44233		61.5	557.0731	1867.425537				

Signature
Rural Works Deptt.
Work Division Paliganj

Executive Engineer
Rural Works Deptt.
Work Division Paliganj

29/11/15
De

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक - 1180/अ.क.

पटना/दिनांक- 31.10.20

प्रेषक,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7
सेवा में,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल पालीगंज

विषय :- जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :- A.E. Paligani vide letter no - 85 dt 14.10.2020

महाशय,

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Karanpura to Munke Path
Bitumen Content for SOR

निम्नलिखित

Executive Engineer
Rural Works Deptt.
Work Division Paliganj
03/11/2020

अनु:-यथोक्त

विश्वासभाजन

29/10/2020
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

Date 31/10/20

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Karanpura to murka path

Name of Scheme:- MR-3054

Name of Agency :- Ram sevan Prasad

Nature of sample :- Bitumen Content for SDGE

Location :- 500 M

Date of Collection/Received :- 19.10.2020

Date of Test :- 29.10.2020

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Paliganj vide letter No. 85-Dt. 14.10.2020

Agreement No / Package No. :

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	501.76	505.23	506.88	
2	Wt. of Dry chips after extraction (b)	476.27	479.58	480.53	
3	Percentage of bitumen (in the mix) $[(a-b)*100] / a$	5.08	5.08	5.20	
4	Average % bitumen	5.12			

[Signature]
A.D.
25/10/2020
Regional Laboratory
R.W.D. Guljarbagh patna - 7

[Signature]
A.E.
29/10/2020
Regional Laboratory
R.W.D. Guljarbagh patna - 7

[Signature]
E.E.
29/10/2020
Regional Laboratory
R.W.D. Guljarbagh patna - 7

Executive Engineer
Rural Works Deptt.
Paliganj

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, क्षेत्रीय प्रयोगशाला, गुलजारबाग
पटना-800007

पत्रांक - 1181/31-2

पटना/दिनांक-31.10.20

प्रेषक,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7
सेवा में,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल पालीगंज।

विषय :- जाँचफल प्रतिवेदन के संबंध में।

प्रसंग :- A.E. Paliganj vide letter no- 84 dt 14.10.2020

महाशय,

उपर्युक्त विषयक के संबंध में जाँचफल प्रतिवेदन इस पत्र के साथ संलग्न कर आवश्यक कारवाई हेतु भेजा जा रहा है जो निम्न प्रकार है:-

Pali Chandos Path to Karanpura via Karhra
Bitumen Content for S.D.C

बिनिधमावित

03/12
Executive Engineer
Rural Works Deptt.
Work Division Paliganj
03/12/20

अनु:-यथोक्त

विश्वासभाजन
29/10/20
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, गुलजारबाग पटना -7

Date 31/10/2020

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Pali Chandos Path to Karanpura via Karkha Path

Name of Scheme :- MR-3054

Name of Agency :- Sri Ram Sevak Prasad

Nature of sample :- Bitumen Content for SDR

Location :- 400M

Date of Collection/Received :- 19/10/2020

Date of Test :- 29/10/2020

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Paliganj vide letter No. 84 Dt. 14/10/2020

Agreement No / Package No. :- 07/M30/2020-21

Executive Engineer
Rural Works Dept.
Work Division Paliganj
03/12/2020

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	506.87	502.21	506.32	
2	Wt. of Dry chips after extraction (b)	481.37	476.78	480.69	
3	Percentage of bitumen (in the mix) $[(a-b)*100] / a$ (%)	5.04	5.06	5.06	
4	Average % bitumen	5.05			

R. W. D. Guljarbagh
L.A.
Regional Laboratory
R.W.D. Guljarbagh patna - 7

R. W. D. Guljarbagh
A.E.
Regional Laboratory
R.W.D Guljarbagh patna - 7

R. W. D. Guljarbagh
E.E.
Regional Laboratory
R.W.D. Guljarbagh patna - 7
