

Inspection Report For Flood Damage Work

Date :

1 Name of PIUs: Gopalganj-2

2 Name of Block/Road: Mangal Brit P.S TO Dhubi Tola, Mangalpur
BKipuri

A For Road

1 Damage Location / Chainage: 150 m to 320 m, 1000 m to 1220 m, 1430 m to 1670 m

2 Damage Length: 324 m

3 Nature of Damage: Heavy Rain / Flood

4 Details of Restoration Works:

i. Material being used in Restoration Works: Brick Ball

ii Equipments / Tools being used in Restoration Works: JCB, Tractor, Pallet, Pallet, Stacker

iii Procedure taken up in Restoration Works: Yes

iv Restored Length: 324 m

B For Bridge

N/A

1 Damage Location / Chainage:

2 Damage Length:

3 Nature of Damage:

4 Details of Restoration Works:


i. Material being used in Restoration Works :

ii Equipments / Tools being used in Restoration Works :

iii Procedure taken up in Restoration Works:

iv Restored Length :


 JE


 AE


 EE
 Executive Engineer
 (Name of Inspector)
 R.W.D. W.D.
 Hathua

Report

Name of Work :- Motorable work of Mangal Brit P.S To Dhobi Tola , Mangalpur

Estimated Cost :- ~~3016500.00~~ 27,28,000.00

Total length of Road :- 1.775 km

Description :- The present estimate has been farmed under the supervision of Assistant engineer in accordance with the order of Executive Engineer, RWD, WD Gopalganj-2, letter No. - 1574 dated 18-08-2020. The part of above mentioned road has been damaged due to heavy rain/flood. And due to this damage the transporation has been obstructed. The immediate motorable work is necessary in public interest. Villagers will be benefitted by the completion of this motorable work.

In the estimate there has been a provision of repairing the damaged part of the road & making it motorable by filling brickbats. In the context of post flood scenario there is still the flow of water which prevails through the damaged part of the road.

In this estimate the rate of raw materials and labour wages has been prepared after the analysis of new rate. This estimate is as per the specifications. The estimate is devoted to technical and administrative acceptance.


19/9/2020
J.E.


19.09.2020
A.E.


19/9/20
E.E.

**Detailed Estimate For Motorable Work in Road from Mangal Brit P.S To Dhobi Tola ,
Mangalpur damaged due to Heavy rain/flood for year 2020-2021**

Sr.	Items	No.	L (M.)	W (M.)	D (M.)	Qty.	Unit	Rate	Amount
1	Providing brick bats billed in ditches including all cost of labour & material with all complete job.								
	CH - 150 M to 320 M	2	30.00	2.10	0.65	81.90	M3		
		1	24.00	1.95	1.50	70.20	M3		
		1	26.00	1.30	1.40	47.32	M3		
		1	30.00	1.10	1.20	39.60	M3		
		1	28.00	1.00	1.30	36.40	M3		
		1	26.00	1.62	0.50	21.06	M3		
	CH - 1000 M to 1220 M	1	25.00	1.65	1.05	43.31	M3		
		1	24.00	1.30	1.00	31.20	M3		
		1	16.00	1.00	1.35	21.60	M3		
		1	28.00	1.20	1.20	40.32	M3		
		1	26.00	2.00	0.80	41.60	M3		
		1	12.00	1.30	0.85	13.26	M3		
		1	11.00	1.05	1.30	15.02	M3		
	CH - 1430 M to 1670 M	1	16.00	1.45	1.20	27.84	M3		
		1	18.00	1.30	0.40	9.36	M3		
		1	23.00	1.40	1.85	59.57	M3		
		1	26.00	2.00	1.40	72.80	M3		
		3	30.00	2.50	1.60	360.00	M3		
		2	30.00	2.20	1.50	198.00	M3		
	Less for H.P.	0	1.23	1.23	0.60	0.00	M3	2412.11	26837.02
						1230.36		2427.65	2986877.38
2	Providing & laying 1000 MM Dia NP3 Hume Pipe in single row -do-do- complete job.	0	2.50			112.62	M	2744.50	2701045.87
						0.00	M	4159.56	0.00
									2986877.38
	Add 1 % Contingency							26838.20	29868.77
									3016746.16
									3016500.00
								Total	3016746.16
								Say	3016500.00

[Signature]
19/9/2020
J.E.


[Signature]
19.09.2020
A.E.

[Signature]
19/9/20
E.E.


27,28,000.00

Technically Approved for Rs 30.165 Lacs (Rupees Thirty Lacs
Sixteen Thousand & Five Hundred only)

Technically Sanctioned for Rs 27.106 Lacs (Rupees
Twenty Seven Lacs Ten Thousand & Six Hundred only)



अधीक्षण अभियंता
प्रमाणित कार्य विभाग कार्य अंकल-सिक्का



Name of Road :- Mangal Brit P.S. to Dhobi Tola, Mangalpur




(Signature)
19/9/2020
N

(Signature)
19-09-2020
AE

Name of Road :- Mangal Brit P.S. to Dhobi Tola, Mangalpur



Name of Road :- Mangal Brit P.S. to Dhobi Tola, Mangalpur

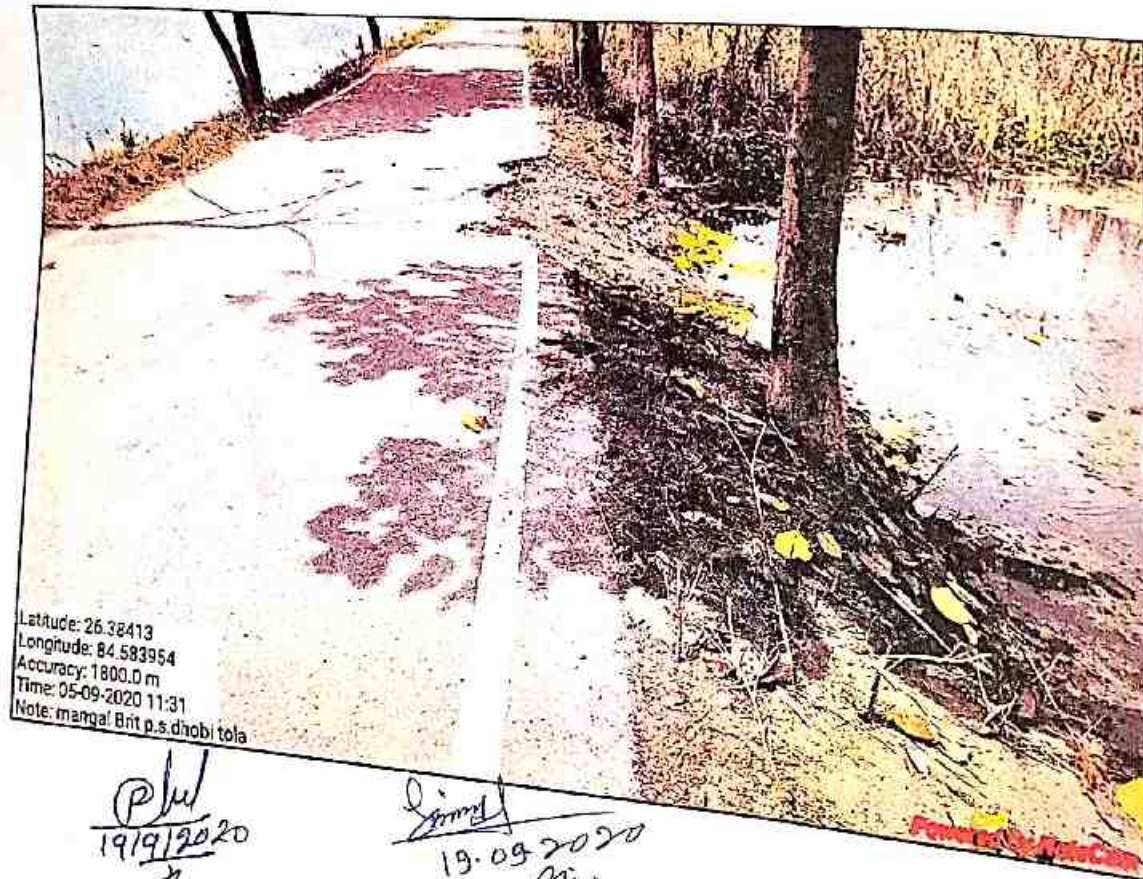

Plu
19/9/2020
2

Simul
19.09.2020
Plu
