

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, दाउदनगर

पत्रांक.....1822..... दाउदनगर / दिनांक.....23.12.2020

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद दाउदनगर

सेवा में,

नोडल पदाधिकारी (MR 3054)
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :- नई अनुरक्षण नीति-2018MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति-2018 MR (3054) योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :- यथोक्त।

विश्वास भाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दाउदनगर

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Daudnagar

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division: Aurangabad																		
Sl.no.	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative				Agreement No.& Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	RM/AU/DAL/19/0011	Goh Gaya Road - Bajid Pur	10602802041	2124/06.07.2019	2.93	154.26	57.991	25.03	76/MBD/2019-2020 29.02.2020	23.10.20	20.12.2020	3259	25mm	5.000%	0.00000	0.00000	57.99	Comp.
	RM/AU/DAL/19/0011	Goh Uphar Road - Mohidin Pur	10602802048	2124/06.07.2019	9.92	317.52	199.566	86.13	76/MBD/2019-2020 29.02.2020	23.10.20	20.12.2020	3259	25mm	5.000%	0.00000	0.00000	199.566	Comp.
	RM/AU/DAL/19/0011	Const of Rd from Goh Ratiganj Rd to Motha	10602801011	2124/06.07.2019	1.8	58.02	34.871	21.01	76/MBD/2019-2020 29.02.2020	23.10.20	20.12.2020	3259	25mm	5.000%	0.00000	0.00000	34.871	Comp.
TOTAL																292.43		

Divisional Accounts Officer
Rural Works Department, works
Division, Daudnagar

23/12/2020

Executive Engineer
Rural Works Department
Works Division, Daudnagar

23/12/20

Name Of Road Const of Rd from Goh Rafiganj Rd to Motha

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	Ulv	CATEGORY ROAD	IRI	Latitude	Longitude	Event
20/12/20	11:27:36	91	0.1	290	10.1	2900	3426 G		4.53	24.922232	84.651565	Speed Breaker
20/12/20	11:28:0	91	0.1	240	20.2	2400	2858 G		3.85	24.92206	84.652558	Normal
20/12/20	11:28:10	91	0.1	260	20.2	2600	3086 G		3.13	24.921952	84.65348	Normal
20/12/20	11:28:10	91	0.1	310	20.2	3100	3654 G		3.8	24.920872	84.65404	Normal
20/12/20	11:28:45	91	0.1	360	20.2	3200	3822 G		3.46	24.921778	84.654175	Normal
20/12/20	11:29:0	91	0.1	340	20.2	3400	3994 G		3.19	24.922263	84.65478	Normal
20/12/20	11:29:0	91	0.1	280	20.2	2800	3313 G		3.4	24.922122	84.65579	Normal
20/12/20	11:29:20	91	0.1	270	20.2	2700	3199 G		4.26	24.921947	84.65677	Speed Breaker
20/12/20	11:29:20	91	0.1	300	20.2	3000	3540 G		3.66	24.928498	84.657793	Normal
20/12/20	11:29:20	91	0.1	360	20.2	3200	3822 G		3.46	24.921023	84.65803	Normal
20/12/20	11:30:0	91	0.1	340	20.2	3400	3994 G		3.19	24.92231	84.658803	Normal
20/12/20	11:30:0	91	0.1	220	30.3	2200	2631 G		3.58	24.923082	84.65872	Normal
20/12/20	11:30:31	91	0.1	320	10.1	3200	3767 G		3.93	24.92213	84.658618	Normal
20/12/20	11:31:0	91	0.1	330	20.2	3300	3881 G		3.06	24.923193	84.659023	Normal
20/12/20	11:31:6	91	0.1	290	20.2	2900	3426 G		4.53	24.922828	84.659915	Speed Breaker
20/12/20	11:31:41	91	0.1	280	30.3	2800	3313 G		3.4	24.921955	84.659915	Normal
20/12/20	11:33:27	91	0.1	230	20.2	2300	2745 G		3.72	24.92319	84.659477	Normal
Total Length			1.7									

21/12/2020
J.E

21/12/2020
A.E


E" E

Y = 0 * X ^ 2 + 1.136 * X + 132.5
X = 2905
Y = 3439
(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Name of Customer:
 Name of Work/ Road:
 Lab Job number:
 Date:
 Section No.

Print Generate Report and Graph

Test Date:
 Machine No.:
 Start S. No.:
 Start E. No.:
 Weather:
 Start Location:
 End Location:
 Road Name:
 Road Type:
 Side:
 UHV Range: To
 Dist Range: To
 Elevation:
 Interval: mm/km
 Map View

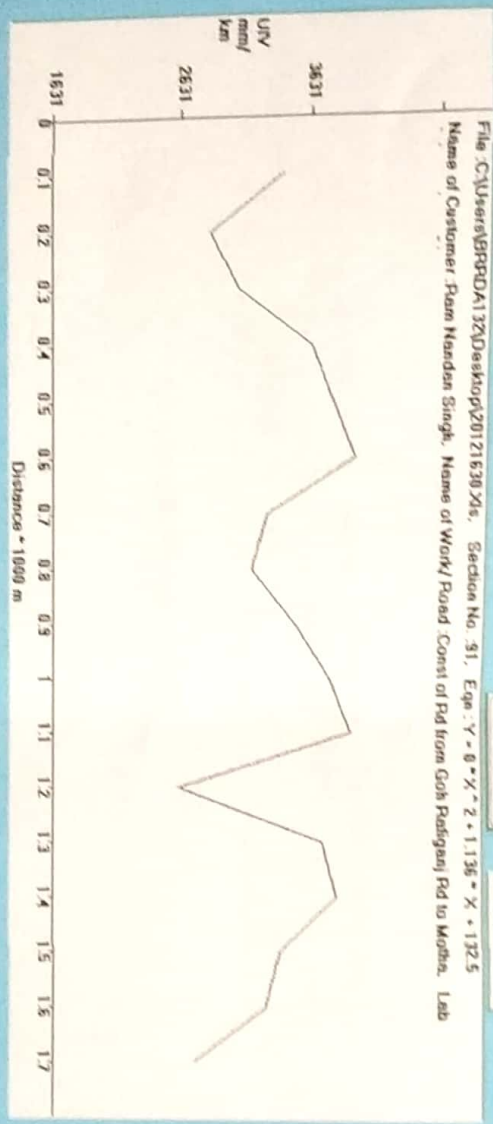

Redraw Graph



OM SAI CONSULTANTS

(AN ISO 9001:2015 & ISO/IEC 17025:2017 CERTIFIED NABL ACCREDITED LAB)
Address: - Bank of India Colony, Near Jai Shree Gas Godown, South D/S,
P.O.-B.V. College Raja Bazar, Patna-800014, Contact No. +919472909287
Email- omisaiconsultantspatna@gmail.com

Rep. No.: OSC/7/18/41

TEST REPORT

Issue To:
EXECUTIVE ENGINEER
R.W.D., Works Division,
Daudnagar

Report No.: OSC/BR/160620/24

Date of Receiving: 16/11/2020

Testing Period: 16/11/2020 TO 18/11/2020

Date of Reporting: 18/11/2020

Project Name: CONSTRUCTION OF ROAD FROM GOH RAFIGANJ ROAD TO MOTH

Sample Description Semi Dense Bituminous Concrete (S.D.B.C.)

Sample Condition: Good (Packed in Bag).

BITUMEN CONTENT TEST

S. No.	Test Parameter	Test Method	Result	Requirements MORTH Specification Table- 500-7	Conformity
1.	Binder Content (%)	IRC SP-11	5.08	5.0 Min.	Yes

.....End of Report.....

Checked By

Authorized Signatory

The result listed refers only to the tested samples and applicable parameters endorsement of product is neither inferred nor implied.
Total Liability of our Lab. is limited to the invoiced amount.
Samples will be destroyed after 90 days from the date of issue of test report.
This report is not to be reproduced wholly or in part and cannot be used as an evidence in the court of law and should not be used in any advertising media without our special permission in writing.

NABL ACCREDITED
LABORATORY
