

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा।

पत्रांक: ८२७ (३१०८)

/ हिलसा, दिनांक: ०६.११.२०२० /

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

सेवा में,

नोडल पदाधिकारी,
नई अनुरक्षण निति-2018 (3054),
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु संलग्न विवरणी के अनुसार रु० 49.96845 (रु० उनचांस लाख छियानवे हजार आठ सौ पैतालीस मात्र) रुपये का आवंटन उपलब्ध कराने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके।
अनुलग्नक :- विहित प्रपत्र में अधिवाचना।

विश्वासभाजन

[Signature]
4.11.2021

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

[Signature]
9/11/20

Station Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
 Division of Works Division :- Hilsa

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Length (In km)	Administrative Amount of (In Lakh)	Agreement Amount (In Lakh)	5 Years Routine Maintenance (In Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
2	RM/NA/HIL/19/0006	Hilsa Chikseura main road to Chamarigha	1281033303	5275/04.10.19	0.415	32.53	32.5139459	3.96021	01/MBD/20-21	02.12.2020	27.11.2020	3390	25.04	5.16	0.00		32.51395	
3	RM/NA/HIL/19/0006	Hilsa Fatima bannan road to Kamta village upto herode	1281033302	5275/04.10.19	0.350	28.38	17.45451	3.23235	01/MBD/20-21	02.12.2020	28.11.2020	2079	25.03	5.16	0.00		17.45451	
TOTAL																	49.96845	

1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
 2 Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer

RWD, Works Division,

Hilsa

[Signature]

09/01/20

6/1/2021
 5/1/2021

Name of Customer: SUNNY CONTR AND ENGGS
 Name of Work: HILSA FATUHA BANWARI RD
 Road:
 Lab Job number:
 Date: 21.12.2020
 Section No: 27

Test Date: 21.12.2020	Road Name: KANTAVILL UP TO TEMPLE
Machine No:	Road Type: (R) RURAL ROAD
Start S No:	Side:
Start E No:	Interval:
Weather:	UIV Range: 495 To 4000 mm/km
Start Location:	Dist Range: 5 To 35 0.1 * 1000 m
End Location:	Equation: $Y = 0 \cdot X^2 + 0.936 \cdot X + 270.4$


Print General Report and Graph

Redraw Graph

Map View

File: C:\Users\SHAZN\Desktop\27.xls, Section No: 27, Eqn: $Y = 0 \cdot X^2 + 0.936 \cdot X + 270.4$

Name of Customer: SUNNY CONTR AND ENG PVT LTD, Name of Work: Road HILSA FATUHA BANWARI RD TO

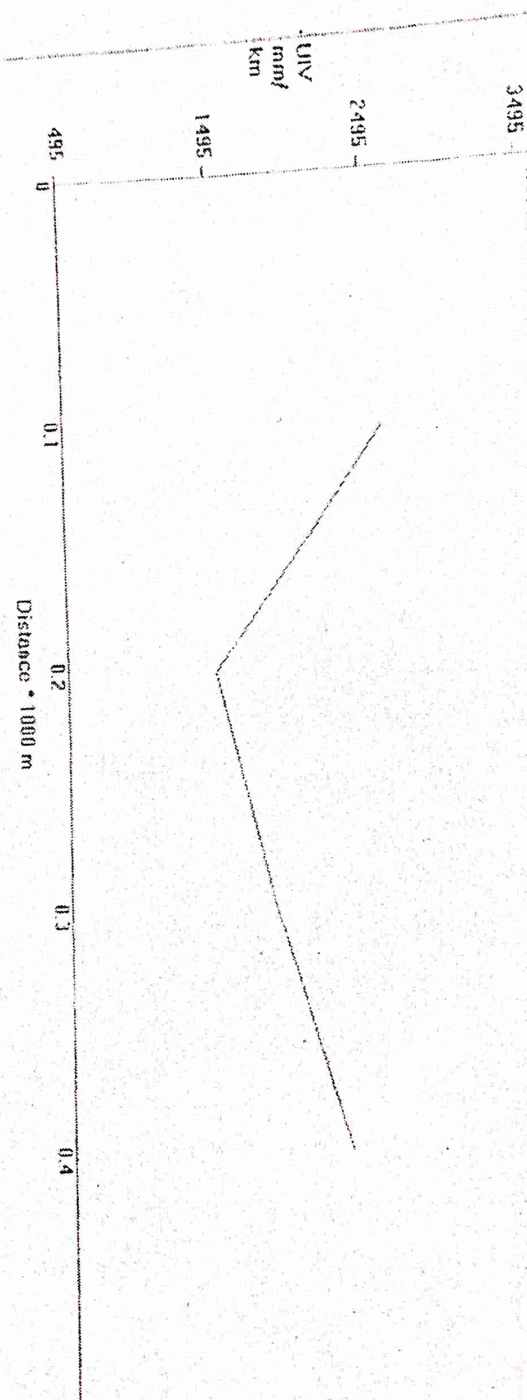

21.12.2020
 5.13

21/12/2020
 21/12/2020

21/12/2020

NAME OF THE ROAD : HILSA FATUHA BANWARI ROAD TO KAMTA VILLAGE UPTO TEMPLE

LENGTH OF THE ROAD : 0.350 KM

PACKAGE NO. : MR-N/19-20/HILSA/04

DIVISION : HILSA

BLOCK : HILSA

CONTRACTOR : SUNNY CONTRACTOR AND ENGINEERS PVT LTD

Date	Time	Section	Length	Bumps	Speed	OR	UIV	CATEGORY	IRI	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD							
21/12/20	11:30:15	27	0.1	250	0	2500	2618	G	3.56	25.335865	85.283113	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
21/12/20	11:30:39	27	0.1	130	20.2	1300	1495	G	2.16	25.336365	85.283618	Normal	$X = 2200$		
21/12/20	11:31:10	27	0.1	170	20.2	1700	1869	G	2.64	25.336397	85.283787	Normal	$Y = 2337$		
21/12/20	11:31:29	27	0.045	220	20.2	2200	2337	G	3.22	25.336432	85.283802	Normal	(R) RURAL ROAD		
TOTAL			0.345	770	60.6	7700	8319		11.58	101.345059	341.13432		Good	Average	
AVERAGE							1925		2.895	25.3362648	85.28358		<4000	4001-5000	>5001

Done
21.12.20

Sub
21/12/20

6/12

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D, GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Hilsa Fatuha Barwari Road Je Kanta Village

Name of Scheme :- 354-MR

Name of Agency :- Sunny Contractors and Engineers Pvt Ltd.

Nature of sample :- Bitumen Content for SORC

Location :- 500 M

Ref :- Material sent by E.E./A.E./R.W.D. WORKS Division/Sub Division

Hilsa

vide letter No. 331

Dt.

Date of Collection/Received :- 01/12/2020

Date of Test :- 02/12/2020

25.11.2020

Agreement No / Package No. :

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	506.98	509.33	514.89	
2	Wt. of Dry chips after extraction (b)	480.38	482.15	488.66	
3	Percentage of bitumen (in the mix) $[(a-b)*100]/a$ (%)	5.25	5.14	5.09	
4	Average % bitumen	5.16			

17/12/20
02.12.2020
L.A.

A.D.

Regional Laboratory
Guljarbagh patna - 7

Regional Laboratory
R.W.D Guljarbagh patna - 7

Regional Laboratory
R.W.D Guljarbagh patna - 7

Regional Laboratory
R.W.D. Guljarbagh patna - 7

E.E.
