

दक्षिण पूर्वांचल विकास निगम
मुख्य कार्यालय, नवलपरासी, भारत

ईमेल: info@nvl.org 1630

फोन: 031-222222

16/12/2020

प्रति,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल बाँका - 1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण पटना।

विषय : -गैर योजना मद भीर्ष 3054 एम0आर0 योजना अन्तर्गत आवंटन के संबंध में।

महोदय,

उपर्युक्त विषयक से संबंधित एम0आर0 योजना अन्तर्गत संवेदक द्वारा कराए गये कार्यों के भुगतान हेतु विहित प्रपत्र में अधियाचित राशि रूपया 110.198@&लाख का आवंटन उपलब्ध कराने की कृपा की जाय। ताकि संवेदक को भुगतान किया जा सके।

अनु0:-

1. अधियाचनाप्रपत्र
2. IRI Report

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल बाँका-1

दक्षिण पूर्वांचल विकास क्षेत्र;
खैरखोली फौजदारी क्षेत्र, ईमर चक्र & 1

ईमर चक्र @ 16 30

तारीख 16/12/2020

प्रेशक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल बाँका - 1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण पटना।

विशय : -गैर योजना मद भीर्ष 3054 एम0आर0 योजना अन्तर्गत आवंटन के संबंध में।

महाशय,

उपर्युक्त विषयक से संबंधित एम0आर0 योजना अन्तर्गत संवेदक द्वारा कराए गये कार्यों के भुगतान हेतु विहित प्रपत्र में अधियाचित राशि रूपया 110.198@&लाख का आवंटन उपलब्ध कराने की कृपा की जाय। ताकि संवेदक को भुगतान किया जा सके।

अनु0:-

1. अधियाचनाप्रपत्र
2. IRI Report

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल बाँका-1

ज्ञापांक- /बाँका, 16 30 दिनांक- 16/12/2020


प्रतिलिपि-मुख्य अभियंता-4, ग्रामीण कार्य विभाग, बिहार पटना को सूचनार्थ एवं आव यक कार्रवाई हेतु समर्पित।

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल बाँका-1

Requisition format for Scheme Head - MR 3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and Surface Renewal)

Name of Division : Banka-I

Sl.No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual of Completion Date	Value of IRI (In Km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in %	Previous Total Allotted Amount (In Lac)	Up to date expenditure as per MIS (In Lac)	Requisition Against work done (In Lac)	Remarks
					Length (In Km.)	Amount (In Lac)	Initial Rectification on with Surface Renewal (in Lac)	5 Years Routine Maintenance (in Lac)										
1	MR-N/20-21 BANKA-1/17	Banka Belhar PWD Road (Beldiha More) to Bishanpur	27351036034	6274 & 02.12.2019	4.620	167.028	110.198	45.810	6 MBD / 2020-21	03-05-2021	10-12-2020	3.75	25	5	0	0	110.198	Completed
		Belhar Sahebganj RCD Road (Pachrukhi more) to Pasia.	20703501006	6274 & 02.12.2019	9.050	393.658	276.256	89.776	6 MBD / 2020-21	03-05-2021	06-12-2020	3.53	25	5	0	0	276.256	Completed



**Executive Engineer
Rural Works Department
Works Division, Banka-I**

Name of Customer : Anil Kumar Singh

Name of Work/ Road : Banka Belhar PWD Road (Beldiha More) to Bishanpur

Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
												$Y = 0 * X^2 + 0.789 * X + 100.5$
10-12-2020	12: 33: 15	53	0.1	340	20.2	3200	3168	G	4.62	25.57728	86.76121	Normal
10-12-2020	12: 34: 0	53	0.2	350	20.2	3500	3466	G	4.58	25.58593	86.76141	Normal
10-12-2020	12: 34: 0	53	0.3	380	20.2	3800	3850	G	4.14	25.59487	86.76162	Normal
10-12-2020	12: 35: 0	53	0.4	340	30.3	3400	3369	G	4.46	25.60348	86.76180	Normal
10-12-2020	12: 35: 2	53	0.5	300	20.2	3000	2981	G	4	25.61220	86.76202	Normal
10-12-2020	12: 35: 37	53	0.6	280	20.2	2800	2787	G	3.77	25.62100	86.76224	Normal
10-12-2020	12: 36: 12	53	0.7	230	20.2	2300	2303	G	3.18	25.62970	86.76247	Normal
10-12-2020	12: 38: 0	53	0.8	340	30.3	3400	3369	G	4.46	25.63905	86.76269	Normal
10-12-2020	12: 38: 33	53	0.9	350	20.2	3500	3466	G	4.58	25.64725	86.76290	Normal
10-12-2020	12: 39: 9	53	1	340	20.2	3400	3369	G	4.46	25.65620	86.76310	Normal
10-12-2020	12: 40: 18	53	1.1	330	30.3	3300	3272	G	4.35	25.66538	86.76330	Normal
10-12-2020	12: 41: 0	53	1.2	270	30.3	2700	2690	G	3.65	25.67455	86.76348	Normal
10-12-2020	12: 41: 29	53	1.3	350	20.2	3500	3466	G	4.58	25.67455	86.76348	Normal
10-12-2020	12: 42: 4	53	1.4	270	30.3	2700	2690	G	3.65	25.68315	86.76367	Normal
10-12-2020	12: 43: 14	53	1.5	330	20.2	3300	3272	G	4.35	25.69232	86.76384	Normal

X = 6800

Y = 5465

(B) BITUMINOUS CONC.

Good Average Poor

<2000 2000-3000 >3000

10-12-2020	12: 44: 0	53	1.6	310	30.3	3100	3078	G	4.12	25.70175	86.76401	Normal
10-12-2020	12: 44: 25	53	1.7	330	30.3	3300	3272	G	4.35	25.70935	86.76419	Normal
10-12-2020	12: 45: 0	53	1.8	310	30.3	3100	3012	G	2.82	25.71887	86.76438	Normal
10-12-2020	12: 45: 36	53	1.9	290	30.3	2400	2400	G	3.3	25.72793	86.76455	Normal
10-12-2020	12: 46: 0	53	2	300	20.2	3000	2981	G	4	25.73635	86.76471	Normal
10-12-2020	12: 46: 11	53	2.1	270	30.3	2700	2690	G	3.65	25.74520	86.76487	Normal
10-12-2020	12: 46: 11	53	2.2	270	30.3	2700	2690	G	3.65	25.74520	86.76487	Normal
10-12-2020	12: 46: 46	53	2.3	330	30.3	3300	3272	G	4.35	25.75465	86.76498	Normal
10-12-2020	12: 47: 0	53	2.4	250	30.3	2500	2497	G	3.42	25.76358	86.76508	Normal
10-12-2020	12: 47: 0	53	2.5	350	20.2	3200	3169	G	4.15	25.76358	86.76508	Normal
10-12-2020	12: 47: 21	53	2.6	340	30.3	3400	3369	G	4.46	25.79007	86.76549	Normal
10-12-2020	12: 47: 21	53	2.7	390	30.3	3900	3853	G	5.03	25.79898	86.76562	Normal
10-12-2020	12: 48: 0	53	2.8	350	20.2	3500	3466	G	4.58	25.80842	86.76576	Normal
10-12-2020	12: 48: 32	53	2.9	250	30.3	2500	2497	G	3.42	25.81690	86.76591	Normal
10-12-2020	12: 48: 32	53	3	300	30.3	3000	2962	G	2.82	25.82587	86.76606	Normal
10-12-2020	12: 49: 7	53	3.1	360	30.3	3600	3524	G	2.33	25.83442	86.76625	Normal
10-12-2020	12: 49: 7	53	3.2	310	30.3	3100	3009	G	2.94	25.84358	86.76641	Normal
10-12-2020	12: 50: 0	53	3.3	260	30.3	2600	2593	G	3.53	25.84697	86.76646	Normal
10-12-2020	12: 50: 18	53	3.4	310	30.3	3100	3078	G	4.12	25.85718	86.76668	Normal

10-12-2020	12: 50: 18	53	3.5	340	30.3	3400	3369	G	4.46	25.86920	86.76684	Normal
10-12-2020	12: 50: 53	53	3.6	280	30.3	2800	2787	G	3.77	25.87312	86.76687	Normal
10-12-2020	12: 51: 0	53	3.7	320	30.3	3200	3175	G	4.23	25.88835	86.76710	Normal
10-12-2020	12: 51: 28	53	3.8	300	20.2	3000	2981	G	4	25.89418	86.76727	Normal
10-12-2020	12: 51: 28	53	3.9	360	30.3	3600	3562	G	4.69	25.89418	86.76727	Normal
10-12-2020	12: 52: 4	53	4	280	10.1	2800	2787	G	3.77	25.91232	86.76751	Normal
10-12-2020	12: 52: 39	53	4.1	300	20.2	3000	2981	G	4	25.91232	86.76751	Normal
10-12-2020	12: 53: 14	53	4.2	280	20.2	2800	2787	G	3.77	25.93345	86.76786	Normal
10-12-2020	12: 53: 14	53	4.3	290	20.2	2900	2867	G	3.77	25.93346	86.76791	Normal
10-12-2020	12: 54: 0	53	4.4	340	30.3	3400	3352	G	4.17	25.93348	86.76793	Normal
10-12-2020	12: 54: 12	53	4.5	350	30.3	3500	3452	G	3.17	25.93352	86.76794	Normal
10-12-2020	12: 54: 16	53	4.6	360	10.1	3500	3424	G	2.33	25.93355	86.76795	Normal

S. Kumar
14.12.2020
J.E.

Junior Engineer

Prifam
14.12.2020

Asstt. Engineer
Rural Works Department
Works Division, Banka-I

S. S. S.
14.12.20

Executive Engineer
Rural Works Department
Works Division, Banka-I

Lab Job number :53

Date :10-12-2020

Customer :Anil Kumar Singh

a Belhar PWD Road (Beldiha More) to Bishanpur

Sr.no	Location of test(in km)	Corrected U.I value(mm/km)	Road catagory
1	0.1	3168	G
2	0.2	3466	G
3	0.3	3850	G
4	0.4	3369	G
5	0.5	2981	G
6	0.6	2787	G
7	0.7	2303	G
8	0.8	3369	G
9	0.9	3466	G
10	1	3369	G
11	1.1	3272	G
12	1.2	2690	G
13	1.3	3466	G
14	1.4	2690	G
15	1.5	3272	G
16	1.6	3078	G
17	1.7	3272	G
18	1.8	3012	G
19	1.9	2400	G
20	2	2981	G
21	2.1	2690	G
22	2.2	2690	G
23	2.3	3272	G
24	2.4	2497	G
25	2.5	3168	G
26	2.6	3369	G
27	2.7	3853	G
28	2.8	3466	G
29	2.9	2497	G
30	3	2962	G
31	3.1	3524	G
32	3.2	3009	G
33	3.3	2593	G
34	3.4	3078	G
35	3.5	3369	G
36	3.6	2787	G
37	3.7	3175	G
38	3.8	2981	G
39	3.9	3562	G
40	4	2787	G
41	4.1	2981	G
42	4.2	2787	G
43	4.3	2867	G
44	4.4	3352	G
45	4.5	3452	G
46	4.6	3424	G

Prifam
14.12.2020
J.E.

Junior Engineer

Prifam
14.12.2020

Asstt. Engineer
Rural Works Department
Works Division, Banka-I

Prifam
14.12.2020

Executive Engineer
Rural Works Department
Works Division, Banka-I

Name of Customer : Anil Kumar Singh
 Name of Work/ Road : ad (Beldiha More) to Bishanpur
 Lab Job number : 53
 Date : 10-12-2020
 Section No. : 53


Test Date : 10-12-2020 Road Name : ad (Beldiha More) to Bishanpur
 Machine No : 407 Road Type : (B) BITUMINOUS CONC.
 Start S No : Side : Interval
 Start E No :
 Weather : UIV Range : 1303 To 5000 1000 mm/km
 Start Location : Dist Range : 0 To 4.7 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.789 * X + 100.5$

Print

Generate Report and Graph

Redraw Graph


Map View

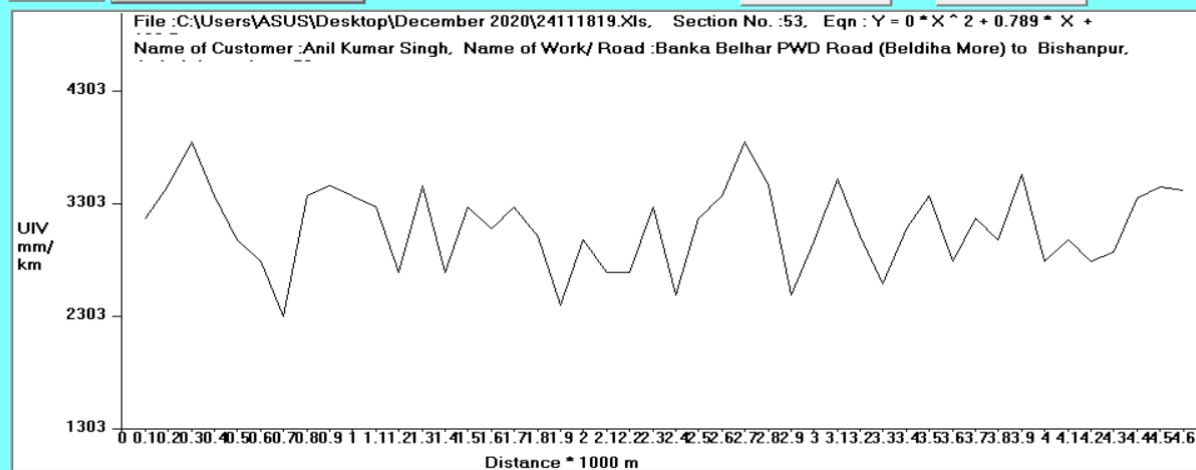

Skumar
 14.12.2020
 J.E.

Prifam
 14.12.2020

S. L. Das
 14.12.20

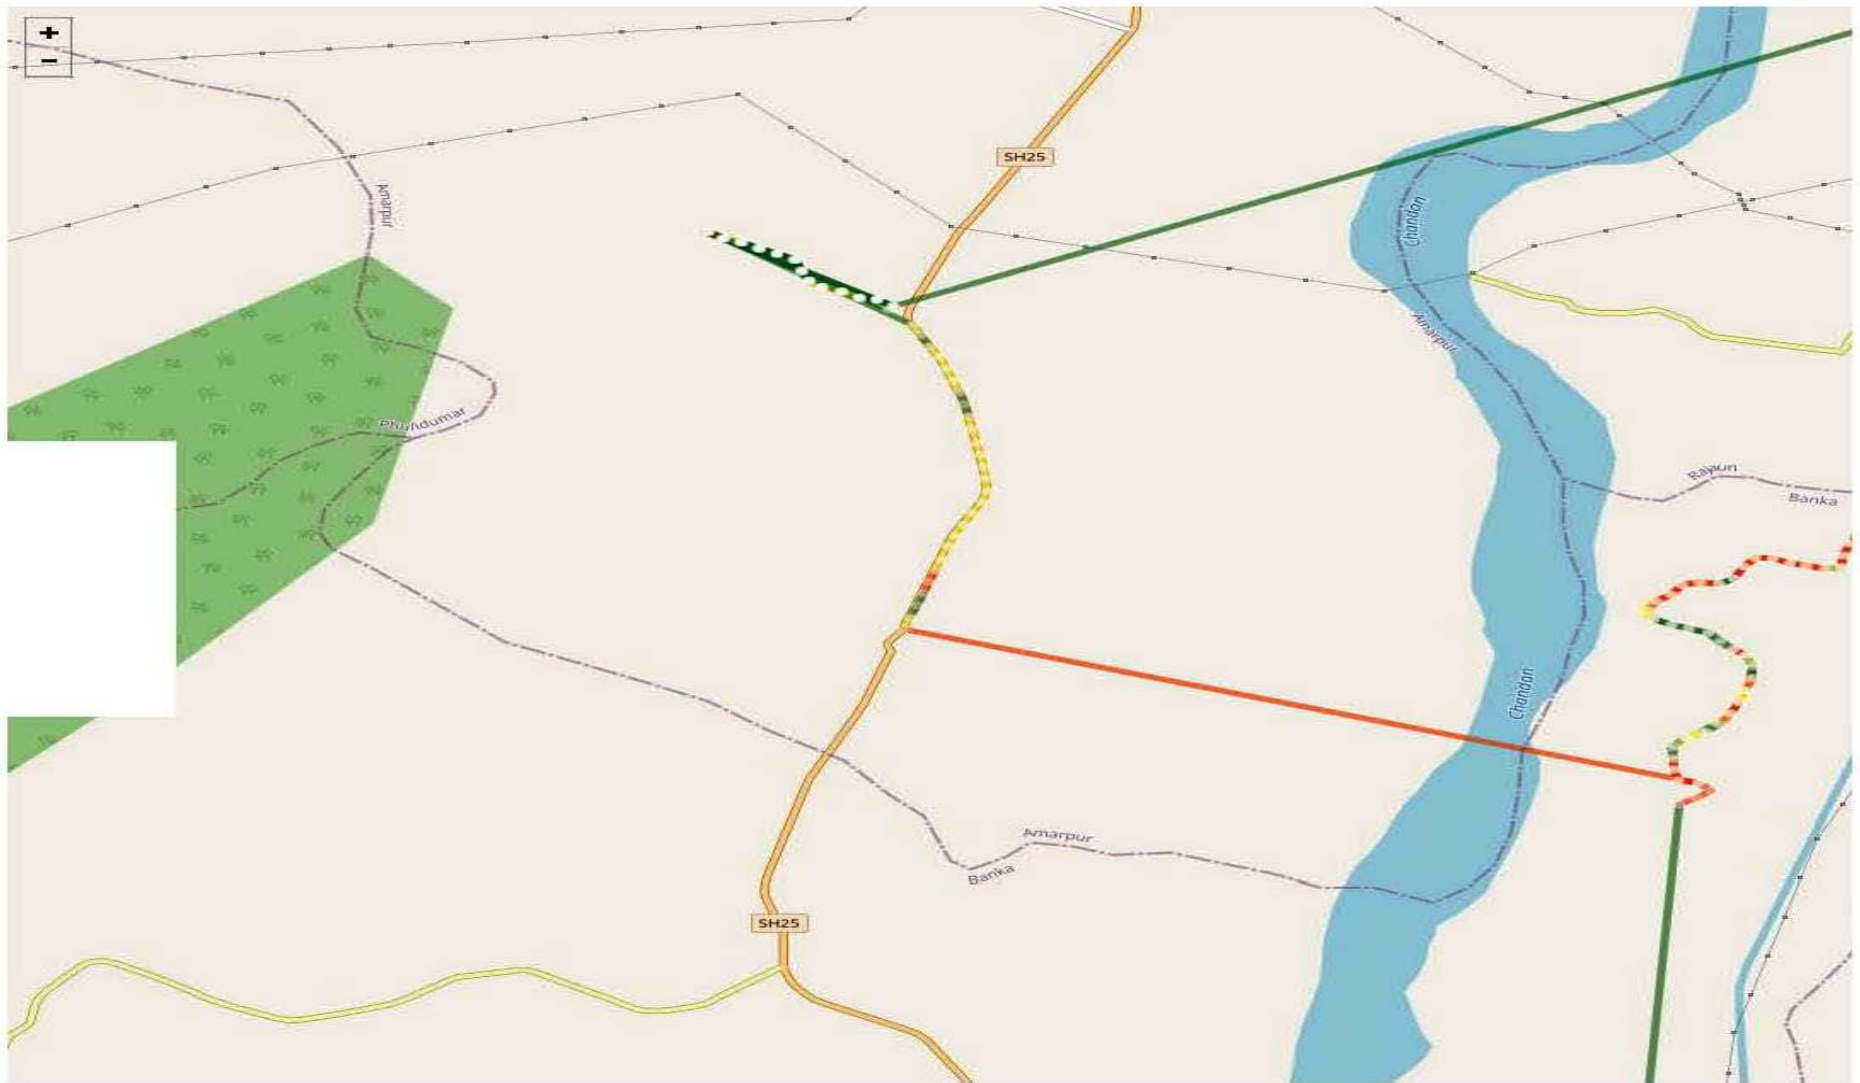

Skumar
14.12.2020
J.E.

Prifam
14.12.2020

S. S. S.
14.12.20
