

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, सीतामढ़ी

पत्रांक.....५९३१७ / दिनांक.....०७/०१/२१

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सीतामढ़ी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- शीर्ष बिहार नई अनुरक्षण नीति 2018 (MR 3054) में आवंटन देने के संबंध में।

महाशय,

उपर्युक्त विषयक इस प्रमंडल अंतर्गत चल रहे नई अनुरक्षण नीति 2018 (MR 3054) में स्वीकृत योजनाओं के विभिन्न कार्यों के लिए संलग्न विवरणी अनुसार भुगतान हेतु आवंटन देने की कृपा की जाय।

अनु०:- यथोक्त।

विश्वासभाजन

०७/०१/२१
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, सीतामढ़ी।

Requisition Format for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division RWD, Works Division- Sitamarhi

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Length (In KM)	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. Date	Date of Completion as per Agreement	Value of IRI (In mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	Up-to Date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
						Amount (In Lakh)	5 Years Routine Maintenance (In Lakh)	Initial Rectification With Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)									
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/2019-20/Sitamarhi/11	Balua Chowk - Balua School Path	NEA220001841	Lt. No.-525SDt.-04.10.19	2.500	52.41700	21.23300	50.27771	20.34294	13/ MBD/20-21	25.03.21	2992	25mm	5.00%	0.00000	0.00000	50.27771	
2	MR-N/2019-20/Sitamarhi/11	Lagma Chowk to Beli Road	31607901043	Lt. No.-525SDt.-04.10.19	4.000	80.63000	34.11000	77.37517	32.73706	13/ MBD/20-21	25.03.21	3485	25mm	5.00%	0.00000	0.00000	77.37517	
					6.500	133.04700	55.34300	127.65288	53.08000						0.00	0.00	127.65288	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed
2. Up-to date Physical Progress has been uploaded in MIS


 Executive Engineer
 RWD (W) Division,
 Sitamarhi
 7.1.21

Steco Analyzer


Name of Customer : KABBU KHIRHAR
Name of Work/ Road : Balua Chowk - Malua high Scho
Lab Job number : 394
Date : 07-01-2021
Section No. : 34

Test Date : 07-01-2020 Road Name : Balua Chowk - Malua high Scho
Machine No : 394 Road Type : (R) RURAL ROAD
Start S No : Side : Interval
Start E No :
Weather :
Ultraviolet Range : 1261 To 5000 1000 mm/km
Start Location : Dist Range : 0 To 25 0.1 * 1000 m
End Location : Equation : $Y = 2700 * X^2 + 0.989 * X - 13.58$

Print Generate Report and Graph

Redraw Graph

Map View

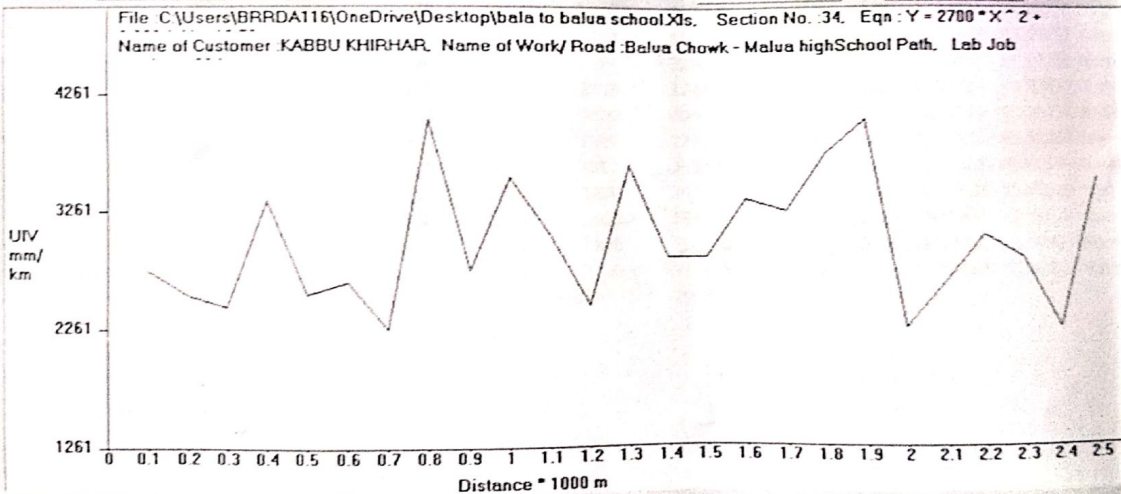

7/1/21
EE

7/1/21
EE

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UUV	TEGORY ROAD	IRI	Latitude	Longitude	Event
7/1/21	13:13:26	34	0.1	280	0	2800	2755	G	3.73	26.51385	85.51374	Normal
7/1/21	13:13:26	34	0.1	260	10.1	2600	2557	G	3.49	26.51422	85.51283	Normal
7/1/21	13:13:26	34	0.1	250	20.2	2500	2458	G	3.37	26.51473	85.512	Normal
7/1/21	13:14:1	34	0.1	340	20.2	3400	3349	G	4.44	26.51521	85.51113	Curve
7/1/21	13:14:1	34	0.1	260	30.3	2600	2557	G	3.49	26.51612	85.51104	Normal
7/1/21	13:14:37	34	0.1	270	30.3	2700	2656	G	3.61	26.51701	85.51066	Curve
7/1/21	13:15:0	34	0.1	230	30.3	2300	2261	G	3.13	26.51778	85.51109	Normal
7/1/21	13:15:11	34	0.1	410	40.4	4100	4041	A	5.25	26.5186	85.51146	Bridge
7/1/21	13:15:11	34	0.1	280	30.3	2800	2755	G	3.73	26.51946	85.51178	Normal
7/1/21	13:15:46	34	0.1	360	20.2	3600	3546	G	4.67	26.52041	85.51192	Curve
7/1/21	13:16:0	34	0.1	310	30.3	3100	3052	G	4.09	26.52124	85.51158	Curve
7/1/21	13:16:0	34	0.1	250	20.2	2500	2458	G	3.37	26.52213	85.51146	Normal
7/1/21	13:16:21	34	0.1	370	10.1	3700	3645	G	4.79	26.52296	85.51114	Curve
7/1/21	13:16:21	34	0.1	290	10.1	2900	2854	G	3.85	26.52335	85.5102	Normal
7/1/21	13:17:0	34	0.1	290	10.1	2900	2854	G	3.85	26.52381	85.50936	Normal
7/1/21	13:17:32	34	0.1	340	10.1	3400	3349	G	4.44	26.52435	85.50852	Normal
7/1/21	13:18:0	34	0.1	330	10.1	3300	3250	G	4.32	26.5247	85.50759	Normal
7/1/21	13:19:0	34	0.1	380	20.2	3800	3744	G	4.9	26.52498	85.50657	Culvert
7/1/21	13:19:18	34	0.1	410	10.1	4100	4041	A	5.25	26.52528	85.50556	Bridge
7/1/21	13:19:18	34	0.1	230	20.2	2300	2261	G	3.13	26.52557	85.50463	Normal
7/1/21	13:21:0	35	0.1	270	20.2	2700	2656	G	3.61	26.52573	85.50599	Normal
7/1/21	13:21:9	35	0.1	310	20.2	3100	3052	G	4.09	26.52538	85.50529	Normal
7/1/21	13:21:9	35	0.1	290	20.2	2900	2854	G	3.85	26.5251	85.50631	Normal
7/1/21	13:21:44	35	0.1	230	10.1	2300	2261	G	3.13	26.52482	85.50721	Normal
7/1/21	13:22:0	35	0.1	360	20.2	3600	3546	G	4.67	26.52448	85.50823	Normal
average								2992				

$$Y = 2700 * X^2 + 0.989 * X - 13.58$$

$$X = 3600$$

$$Y = 3546$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

Handwritten signature
7/1/21

Handwritten signature
7/1/21
EE
