

कार्यपालक अभियंता का कार्यालय,

ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बायसी ।

पत्रांक:.....66.3130

बायसी / दिनांक:.....14/01/2021

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बायसी ।

सेवा में,

नोडल पदाधिकारी,
नई अनुरक्षण निति-2018 (3054),
ग्रामीण कार्य विभाग, बिहार, पटना ।

विषय- नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन की मांग ।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु संलग्न विवरणी के अनुसार रु० 619.99900 (रु० छः करोड़ उन्नीस लाख निन्नानवे हजार नौ सौ मात्र) रुपये का आवंटन उपलब्ध कराने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके ।

अनुलग्नक :- विहित प्रपत्र में अधियाचना ।

विश्वासभाजन


14/01/21

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बायसी ।

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :-Baist.

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Length (In km)	Administrative Amount of (In Lakh)	Agreement Amount Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/PU/BAI/20/0001	Ganesh to Pothiya	21105202053	5271/04.10.19	2.170	135.716	119.054	26.32000	16/NMBD/2020-21	17.02.2021	04.01.2021	2987	25.03	5.06	0.000000	0.00	119.05400	
2	RM/PU/BAI/20/0001	Bishanpur to Khameela	21105202038	5271/04.10.19	4.330	224.712	185.14	54.02000	16/NMBD/2020-21	17.02.2021	05.01.2021	3031	25.02	5.05	0.000000	0.00	185.14000	
3	RM/PU/BAI/20/0001	Gurua to Manuware	21105202054	5271/04.10.19	3.450	229.935	198.72	45.33000	16/NMBD/2020-21	17.02.2021	04.01.2021	2993	25.03	5.05	0.000000	0.00	198.72000	
4	RM/PU/BAI/20/0001	T04 Approach Road to Barbatta	21105402004	5271/04.10.19	2.640	141.083	117.085	33.09800	16/NMBD/2020-21	17.02.2021	04.01.2021	3080	25.02	5.04	0.000000	0.00	117.08500	
TOTAL																	619.99900	

- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer
RWD, Works Division,
Baist

14/01/24

Name of Customer:

Name of Work:

Road:

Lab Job number:

Date:

Section No.

Test Date:

Road Name:

Machine No:

Road Type:

Start S No:

Side:

Interval:

Weather:

UV Range: To mm/km


Start Location:

Dist Range: To 0.1 * 1000 m

End Location:

Equation:

Print Generate Report and Graph Redraw Graph Map View

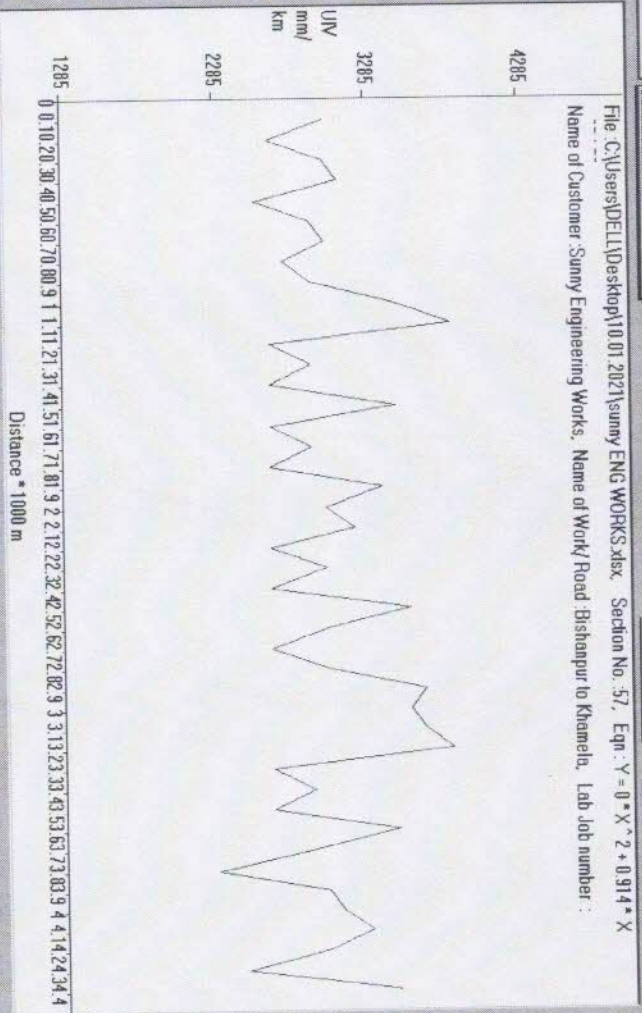

Handwritten signature
1/11/2021

Road Name:- BISHANPUR TO KHAJULA														
Date	Time	Section	Length	Bumps		Speed	OR		IRI, TEGORY	Latitude	Longitude	Event		
				No.	Rate		mm/km	ROAD						
10/1/21	15: 53: 13	57	0.10	300	10.1	3000	3016	G	25.9827	87.648265	Normal			
10/1/21	15: 53: 48	57	0.10	260	10.1	2600	2650	G	25.982002	87.64867	Curve			
10/1/21	15: 54: 0	57	0.10	300	20.2	3000	3016	G	25.981143	87.64848	Curve			
10/1/21	15: 54: 23	57	0.10	310	10.1	3100	3107	G	25.980248	87.648568	Curve			
10/1/21	15: 54: 23	57	0.10	250	20.2	2500	2559	G	25.97972	87.649325	Normal			
10/1/21	15: 55: 0	57	0.10	290	20.2	2900	2925	G	25.97965	87.650252	Normal			
10/1/21	15: 55: 34	57	0.10	300	20.2	3000	3016	G	25.979808	87.651295	Culvert			
10/1/21	15: 56: 0	57	0.10	270	10.1	2700	2742	G	25.97954	87.652205	Curve			
10/1/21	15: 56: 9	57	0.10	290	10.1	2900	2925	G	25.980292	87.652542	Curve			
10/1/21	15: 57: 20	57	0.10	350	20.2	3500	3473	G	25.980332	87.65348	Speed Breaker			
10/1/21	15: 57: 20	57	0.10	390	20.2	3900	3839	G	25.980507	87.65441	Speed Breaker			
10/1/21	15: 58: 30	57	0.10	260	30.3	2600	2650	G	25.980752	87.65537	Normal			
10/1/21	15: 58: 30	57	0.10	290	20.2	2900	2925	G	25.980735	87.656312	Normal			
10/1/21	15: 59: 6	57	0.10	260	30.3	2600	2650	G	25.980837	87.657205	Curve			
10/1/21	15: 59: 41	57	0.10	260	30.3	2600	2650	G	25.980813	87.658265	Curve			
10/1/21	16: 0: 16	57	0.10	350	20.2	3500	3473	G	25.98162	87.658652	Normal			
10/1/21	16: 0: 16	57	0.10	260	20.2	2600	2650	G	25.982282	87.659175	Normal			
10/1/21	16: 1: 0	57	0.10	290	20.2	2900	2925	G	25.982455	87.66012	Normal			
10/1/21	16: 1: 27	57	0.10	260	30.3	2600	2650	G	25.982518	87.66111	Curve			
10/1/21	16: 2: 2	57	0.10	340	10.1	3400	3382	G	25.98271	87.662103	Curve			
10/1/21	16: 2: 2	57	0.10	300	20.2	3000	3016	G	25.982907	87.663113	Culvert			
10/1/21	16: 2: 37	57	0.10	320	10.1	3200	3199	G	25.982958	87.66404	Culvert			
10/1/21	16: 3: 13	57	0.10	260	30.3	2600	2650	G	25.983128	87.664747	Curve			
10/1/21	16: 4: 0	57	0.10	300	20.2	3000	2650	G	25.982625	87.665337	Curve			
10/1/21	16: 4: 22	57	0.10	260	30.3	2600	2650	G	25.982532	87.665925	Normal			
10/1/21	16: 5: 0	57	0.10	360	20.2	3600	3564	G	25.982527	87.666935	Normal			
10/1/21	16: 5: 33	57	0.10	300	20.2	3000	3016	G	25.982412	87.667895	Normal			
10/1/21	16: 5: 33	57	0.10	260	20.2	2600	2650	G	25.981822	87.668248	Curve			
10/1/21	16: 6: 8	57	0.10	300	20.2	3000	3016	G	25.980973	87.667912	Normal			
10/1/21	16: 6: 43	57	0.10	370	10.1	3700	3656	G	25.980118	87.667878	Normal			
10/1/21	16: 7: 19	57	0.10	360	20.2	3600	3564	G	25.97924	87.66776	Normal			
10/1/21	16: 8: 0	57	0.10	370	20.2	3700	3656	G	25.97838	87.667473	Normal			
10/1/21	16: 8: 29	57	0.10	390	10.1	3900	3839	G	25.977515	87.667305	Culvert			
10/1/21	16: 9: 5	57	0.10	260	20.2	2600	2650	G	25.976615	87.667357	Normal			
10/1/21	16: 9: 40	57	0.10	290	10.1	2900	2925	G	25.975735	87.667255	Normal			
10/1/21	16: 10: 15	57	0.10	260	20.2	2600	2650	G	25.975735	87.667255	Normal			
10/1/21	16: 10: 15	57	0.10	350	20.2	3500	3473	G	25.974805	87.667188	Normal			
10/1/21	16: 10: 47	57	0.10	290	10.1	2900	2925	G	25.974603	87.667123	Normal			
10/1/21	16: 11: 0	57	0.10	220	20.2	2200	2285	G	25.97391	87.66707	Normal			
10/1/21	16: 11: 26	57	0.10	300	20.2	3000	3016	G	25.973002	87.667003	Normal			
Total			3.90			117400	117989							
Average						3010.26	3025.36							

$$Y = 0 * X^2 + 0.914 * X + 27$$

OFFICE OF THE EXECUTIVE ENGINEER R.W.D. REGIONAL
LABORATORY, PURNER, (BIHAR)
RESULT OF BITMEN CONTENT OF MIX SAMPLE

Name of work Maint of road Biskampur to Name of Division Ba'isi
Package no./ngt.no. MB/3054 Name of Agency M/S Sunny Engineering works
Sample Collected by A.E. RWA(W) Sub-Div. Ba'isi 4 NO. 07 dt. 04.01.2021
Location 1300M. Wt. of sample taken 1000gm.

Sl.No.	Sample No.	Identification No.	Wt. of sample b.c.	Wt. of sample a.c.	Loss wt.	Average	% of bitmen content
1.	M	B ₁	340	324	16.0		
2.	N	B ₂	287	273	14.0	15.0	5.05%
3.	P	B ₃	308	293	15.0		

Acceptable

Copy to Executive Engineer RWA(W) Sub-Div. Ba'isi

Suprntending Engineer

Chief Engineer Bihar Patna

LA
07/01/2021

A.E.
07/01/21

M-2
07/01/21

EXECUTIVE ENGINEER
RURAL WORKS DEPT.
REGIONAL LABORATORY
PURNER
