

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा।

पत्रांक...../2/.....

/ हिलसा, दिनांक.....13-01-21

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

सेवा में,


नोडल पदाधिकारी,
नई अनुरक्षण निति-2018 (3054),
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन की मांग।

महोदय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु संलग्न विवरणी के अनुसार रु० 135.36622 (रु० एक करोड़ पैंतीस लाख छत्तीस हजार छः सौ बाईस मात्र) रुपये का आवंटन उपलब्ध कराने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके।
अनुलग्नक :- विहित प्रपत्र में अधियाचना।

विश्वासभाजन


13-01-2021

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।



13/01/21

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :-Hilsa

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Agreement Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks			
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/NA/HIL/20/0001	Ekangarsarai parwalpur mukhya path se atramchak chora to rasilia tak path marammati	1281033307	5275/04.10.19	1.387	41.40	31.82427	12.90600	02/MBD/20-21	02.12.2020	25.11.2020	3387	25.02	5.18	19.09456	0.00	12.72971	
2	RM/NA/HIL/20/0001	Mushar rasilia road to chakdah	1281033309	5275/04.10.19	1.303	52.496	45.91463	12.00200	02/MBD/20-21	02.12.2020	23.11.2020	3456	25.02	5.17	27.54878	0.00	18.36585	
3	RM/NA/HIL/20/0001	Panchayat Jamuwan ke nischalganj Islampur road to rasilia gaon	1281033308	5275/04.10.19	1.332	54.546	48.22170	12.40900	02/MBD/20-21	02.12.2020	26.11.2020	3288	25.05	5.11	28.93302	0.00	19.28868	
4	RM/NA/HIL/20/0001	Diawan-Berthu Rd. to Pakari	10200802023	5275/04.10.19	1.219	41.162	33.15173	10.56200	02/MBD/20-21	02.12.2020	27.11.2020	3481	25.03	5.16	19.89104	0.00	13.26069	
5	RM/NA/HIL/20/0001	Islampur Nischalganj to Road to Bakaur via Rampur	1281033299	5275/04.10.19	2.574	90.073	75.67772	23.59300	02/MBD/20-21	02.12.2020	24.11.2020	3469	25.04	5.13	45.40663	0.00	30.27109	
6	RM/NA/HIL/20/0001	Panchayat Mandach ke lodipur khaddi gawn se radhli chikka	1281033290	5275/04.10.19	1.980	80.394	71.11154	18.17000	02/MBD/20-21	02.12.2020	26.11.2020	3217	25.03	5.13	42.66692	0.00	28.44462	
7	RM/NA/HIL/19/0006	Hilsa Chikhsaura main road to chamarbigha	1281033303	5275/04.10.19	0.415	32.53	32.51395	3.96021	01/MBD/20-21	02.12.2020	27.11.2020	3390	25.04	5.16	19.50837	0.00	13.00558	
TOTAL																		

- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- Up-to-date Physical Progress has been uploaded in MIS.


18/11/2021
18/11/21
Executive Engineer
RWD, Works Division,
Hilsa

Name of Customer : SUNNY ENGG WORKS
 Name of Work/ Road : MUSHAR BASISA ROAD 101
 Lab Job number :
 Date : 21-12-2020
 Section No. : 29

Test Date : 21-12-2020
 Machine No :
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : BASISA ROAD TO CHAKDAH
 Road Type : (R) RURAL ROAD
 Side :
 UHV Range : 2086 To 5000 m/ft
 Dist Range : 0 To 13 0.1 ~ 1000 m
 Equation : $Y = 0 \cdot X^2 + 0.338 \cdot X + 278.4$

Print Generate Report and Graph Radraw Graph Map View

File : C:\Users\ISHAZ\Desktop\13 DEC 2020\PAW DATA\29.xls. Section No. 29. Egn: $Y = 0 \cdot X^2 + 0.338 \cdot X + 278.4$
 Name of Customer: SUNNY ENGG WORKS, Name of Work/ Road: MUSHAR BASISA ROAD TO CHAKDAH1, Lab

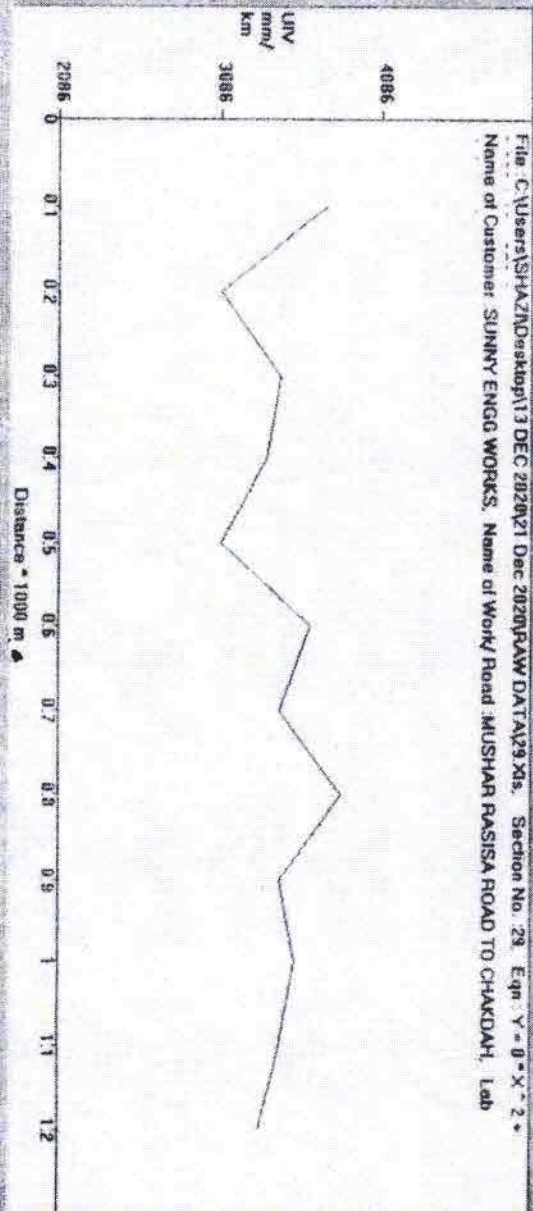

NAME OF THE ROAD : MUSHAR RASISA ROAD TO CHAKDAH

LENGTH OF THE ROAD : 1.903 KM

PACKAGE NO. : MR-N/19-20/HILSA/05

DIVISION : HILSA

BLOCK : EKANGARSARAI

CONTRACTOR : SUNNY ENGINEERING WORKS

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV mm/km	CATEGORY ROAD	IRI	Latitude	Longitude	Event			
21/12/20	13:34:24	29	0.1	370	0	3700	3741	G	4.9	25.20249	85.280168	Curve	$Y = 0 * X^2 + 0.936 * X + 278.4$		
21/12/20	13:35:0	29	0.1	300	20.2	3000	3086	G	4.13	25.202565	85.279242	Normal	X = 3318		
21/12/20	13:35:10	29	0.1	340	30.3	3400	3460	G	4.57	25.202702	85.278265	Normal	Y = 3320		
21/12/20	13:35:20	29	0.1	330	20.2	3300	3367	G	4.46	25.202957	85.277255	Normal			
21/12/20	13:35:35	29	0.1	300	20.2	3000	3086	G	4.13	25.202823	85.27643	Curve	(R) RURAL ROAD		
21/12/20	13:36:0	29	0.1	360	20.2	3600	3648	G	4.79	25.20268	85.275673	Normal	Good	Average	Poor
21/12/20	13:36:10	29	0.1	340	30.3	3400	3460	G	4.57	25.202945	85.274797	Normal	<4000	4001-5000	>5001
21/12/20	13:36:20	29	0.1	380	20.2	3800	3835	G	5.01	25.203118	85.273737	Normal			
21/12/20	13:36:30	29	0.1	340	20.2	3400	3460	G	4.57	25.20357	85.273047	Curve			
21/12/20	13:36:45	29	0.1	350	30.3	3500	3554	G	4.68	25.203643	85.27202	Normal			
21/12/20	13:37:0	29	0.1	340	30.3	3400	3460	G	4.57	25.203785	85.27101	Normal			
21/12/20	13:37:20	29	0.044	190	30.3	3318	3320	G	4.43	25.20383	85.270522	Normal			
TOTAL			1.144	3940	272.7	40818	41477		54.81	302.43711	1023.302166				
AVERAGE						3401.5	3486.417		4.5675						


 22.12.20
 S. S. S.

13/11

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Date 02/12/2020

Name of Project/Road :- Munhar Kasia Road to Chaddah

Bituminous mix

Name of Scheme :- 3554-MR

Name of Agency :- Sunny Engineering works

Nature of sample :- Bitumen content for SMC

Location :- 500M

Date of Collection/Received :- 01/12/2020

Date of Test :- 02/12/2020

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Kangar Sarsi vide letter No. 181 Dt. 28.10.2020

Agreement No / Package No. :- 02/MR0/2020-21

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	500.00	503.32	504.98	
2	Wt. of Dry chips after extraction (b)	473.60	477.88	478.79	
3	Percentage of bitumen (in the mix) [(a-b)*100] / a (%)	5.28	5.05	5.19	
4	Average % bitumen	5.17			

Ad
02.12.20
L.A

Regional Laboratory
R.W.D. Guljarbagh patna - 7

A.D

Regional Laboratory
R.W.D Guljarbagh patna - 7

Signature
A.E.

Regional Laboratory
R.W.D Guljarbagh patna - 7

Signature
E.E.

Regional Laboratory
R.W.D. Guljarbagh patna - 7
