

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा।

पत्रांक...../2/.....

/ हिलसा, दिनांक.....13-01-21

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

सेवा में,


नोडल पदाधिकारी,
नई अनुरक्षण निति-2018 (3054),
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन की मांग।

महोदय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु संलग्न विवरणी के अनुसार रु० 135.36622 (रु० एक करोड़ पैंतीस लाख छत्तीस हजार छः सौ बाईस मात्र) रुपये का आवंटन उपलब्ध कराने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके।
अनुलग्नक :- विहित प्रपत्र में अधियाचना।

विश्वासभाजन


13-01-2021

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।



13/01/21

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :-Hilsa

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Agreement Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks					
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19		
1	RM/NA/HIL/20/0001	Ekgarsarai parwalpur mukhya path se atramchak chora to rasilia tak path marammati	1281033307	5275/04.10.19	1.387	41.40	31.82427	12.90600	02/MBD/20-21	02.12.2020	25.11.2020	3387	25.02	5.18	19.09456	0.00	12.72971			
2	RM/NA/HIL/20/0001	Mushar rasilia road to chakdah	1281033309	5275/04.10.19	1.303	52.496	45.91463	12.00200	02/MBD/20-21	02.12.2020	23.11.2020	3456	25.02	5.17	27.54878	0.00	18.36585			
3	RM/NA/HIL/20/0001	Panchayat Jamuwan ke nischalganj Islampur road to rasilia gaon	1281033308	5275/04.10.19	1.332	54.546	48.22170	12.40900	02/MBD/20-21	02.12.2020	26.11.2020	3288	25.05	5.11	28.93302	0.00	19.28868			
4	RM/NA/HIL/20/0001	Diawan-Berthu Rd. to Pakari	10200802023	5275/04.10.19	1.219	41.162	33.15173	10.56200	02/MBD/20-21	02.12.2020	27.11.2020	3481	25.03	5.16	19.89104	0.00	13.26069			
5	RM/NA/HIL/20/0001	Islampur Nischalganj to Road to Bakaur via Rampur	1281033299	5275/04.10.19	2.574	90.073	75.67772	23.59300	02/MBD/20-21	02.12.2020	24.11.2020	3469	25.04	5.13	45.40663	0.00	30.27109			
6	RM/NA/HIL/20/0001	Panchayat Mandach ke lodipur khaddi gawn se radhli chikka	1281033290	5275/04.10.19	1.980	80.394	71.11154	18.17000	02/MBD/20-21	02.12.2020	26.11.2020	3217	25.03	5.13	42.66692	0.00	28.44462			
7	RM/NA/HIL/19/0006	Hilsa Chikhsaura main road to chamarbigha	1281033303	5275/04.10.19	0.415	32.53	32.51395	3.96021	01/MBD/20-21	02.12.2020	27.11.2020	3390	25.04	5.16	19.50837	0.00	13.00558			
TOTAL																				

- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- Up-to-date Physical Progress has been uploaded in MIS.

18/11/2021
18/11/21


Executive Engineer
RWD, Works Division,
Hilsa

Name of Customer: SUNNY ENGG WORKS
Name of Work: DIAYAN BERTHU RD TO PAJ
Road:
Lab Job number:
Date: 21-12-2020
Section No: 26

Test Date: 21-12-2020
Road Name: DIAYAN BERTHU RD TO PAJ
Machine No.:
Start S No.:
Start E No.:
Weather:
Start Location:
End Location:
Road Type: (R) RURAL ROAD
Side:
Interval:
UJV Range: 1892 To 5000
Dist Range: 0 To 114
Equation: $Y = 0.0002 \cdot X + 278.4$

Print Generate Report and Graph Redraw Graph Map View

File: C:\Users\Shahzad\Desktop\13 DEC 2020\PAJ DIAYAN BERTHU RD TO PAJ.xls Section No: 26 Eqn: $Y = 0.0002 \cdot X + 278.4$
Name of Customer: SUNNY ENGG WORKS Name of Work: Road DIAYAN BERTHU RD TO PAJ Lab Job

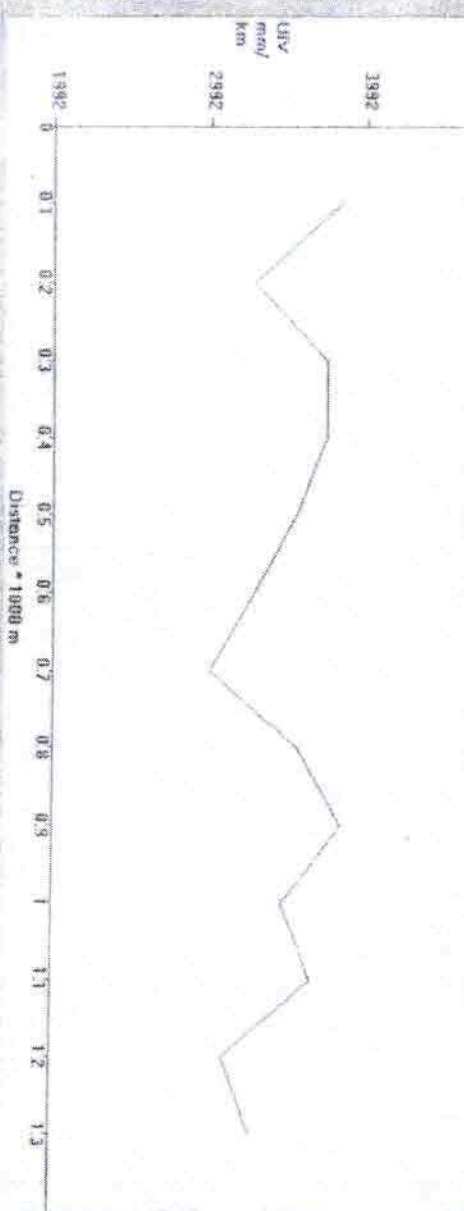

NAME OF THE ROAD : DIAMAN BERTHU ROAD TO PAKRI

LENGTH OF THE ROAD : 1.219 KM

PACKAGE NO. : MR-N/19-20/HILSA/05

DIVISION : HILSA

BLOCK : KARAIPARSURA

CONTRACTOR : SUNNY ENGINEERING WORKS

Date	Time	Section No.	Length (m km)	Bumps (m mm)	Speed Rate	OR (mm/km)	UIV (mm/km)	CATEGORY ROAD	IRI	Latitude	Longitude	Event			
21/12/20	10:54:51	26	0.1	380	0	3800	3835	G	5.01	25.366987	85.258535	Normal	$Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$		
21/12/20	10:55:0	26	0.1	320	20.2	3200	3273	G	4.35	25.36615	85.258315	Normal	$X = 3200$		
21/12/20	10:55:10	26	0.1	370	30.3	3700	3741	G	4.9	25.36531	85.25808	Normal	$Y = 3273$		
21/12/20	10:55:28	26	0.1	370	20.2	3700	3741	G	4.9	25.3644	85.25771	Curve			
21/12/20	10:55:38	26	0.1	350	20.2	3500	3554	G	4.68	25.364465	85.2568	Normal	(R) RURAL ROAD		
21/12/20	10:55:48	26	0.1	320	30.3	3200	3273	G	4.35	25.36453	85.25579	Normal	Good	Average	Poor
21/12/20	10:56:2	26	0.1	290	30.3	2900	2992	G	4.01	25.364635	85.254763	Curve	<4000	4001-5000	>5001
21/12/20	10:56:12	26	0.1	350	30.3	3500	3554	G	4.68	25.365107	85.25409	Normal			
21/12/20	10:56:22	26	0.1	380	30.3	3800	3835	G	5.01	25.36519	85.253163	Speed Breaker			
21/12/20	10:56:37	26	0.1	340	30.3	3400	3460	G	4.57	25.365242	85.252087	Normal			
21/12/20	10:56:57	26	0.1	360	20.2	3600	3648	G	4.79	25.365573	85.251312	Curve			
21/12/20	10:57:13	26	0.1	300	10.1	3000	3086	G	4.13	25.365978	85.25038	Normal			
21/12/20	10:57:33	26	0.019	210	20.2	3200	3273	G	4.35	25.365908	85.25037	Normal			
TOTAL			1.219	4340	292.9	44500	45265		59.73	329.74948	1108.311553				
AVERAGE						3423.077	3481.923		4.594615						


 20.12.20
 2 of 1000

OFFICE OF THE EXECUTIVE ENGINEER

REGIONAL LABORATORY, R. W. D., GULZARBAGH, PATNA - 7

Bituminous mix

Name of Project/Road :- Diawar - Beethu Road to Pakari

Name of Scheme :- 3054 - MR

Name of Agency :- Sany Engineering works

Nature of sample :- Bitumen content for SDR

Location :- 0.900 Km

Ref :- Material sent by E.E./A.E. R.W.D. WORKS Division/Sub Division Kany Parsuraj vide letter No. 76 Dt. 25.10.20

Agreement No / Package No. : 02/M30/2020-21

SL. NO.	SAMPLE NO.	1	2	3	REMARKS
1	Wt. of mix taken before extraction (a)	506.86	503.47	505.34	
2	Wt. of Dry chips after extraction (b)	480.93	478.09	478.65	
3	Percentage of bitumen (in the mix) [(a-b)*100] / a (%)	5.12	5.08	5.28	
4	Average % bitumen	5.16			

AE
02/12/2020
L.A.

A.E.

A.E.

E.E.

Regional Laboratory

Regional Laboratory

Regional Laboratory

R.W.D. Guljarbagh patna - 7

R.W.D. Guljarbagh patna - 7

R.W.D. Guljarbagh patna - 7

R.W.D. Guljarbagh patna - 7
