

कार्यपालक अभियंता का कार्यालय,

ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बायसी ।

पत्रांक:.....66.3130

बायसी / दिनांक:.....14/01/2021

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बायसी ।

सेवा में,

नोडल पदाधिकारी,
नई अनुरक्षण निति-2018 (3054),
ग्रामीण कार्य विभाग, बिहार, पटना ।

विषय- नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु आवंटन की मांग ।

महाशय,

उपर्युक्त विषय के संबंध में नई अनुरक्षण निति 2018 शीर्ष 3054 के अंतर्गत वित्तीय वर्ष 2020-21 में व्यय हेतु संलग्न विवरणी के अनुसार रु० 619.99900 (रु० छः करोड़ उन्नीस लाख निन्नानवे हजार नौ सौ मात्र) रुपये का आवंटन उपलब्ध कराने की कृपा की जाए ताकि किये गये कार्यों का भुगतान किया जा सके ।

अनुलग्नक :- विहित प्रपत्र में अधियाचना ।

विश्वासभाजन


14/01/21

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बायसी ।

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :-Baist.

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Length (in km)	Administrative Amount of (in Lakh)	Agreement Amount Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/PU/BAI/20/0001	Ganesh to Pothiya	21105202053	5271/04.10.19	2.170	135.716	119.054	26.32000	16/NMBD/2020-21	17.02.2021	04.01.2021	2987	25.03	5.06	0.000000	0.00	119.05400	
2	RM/PU/BAI/20/0001	Bishanpur to Khameela	21105202038	5271/04.10.19	4.330	224.712	185.14	54.02000	16/NMBD/2020-21	17.02.2021	05.01.2021	3031	25.02	5.05	0.000000	0.00	185.14000	
3	RM/PU/BAI/20/0001	Gurua to Manuware	21105202054	5271/04.10.19	3.450	229.935	198.72	45.33000	16/NMBD/2020-21	17.02.2021	04.01.2021	2993	25.03	5.05	0.000000	0.00	198.72000	
4	RM/PU/BAI/20/0001	T04 Approach Road to Barbatta	21105402004	5271/04.10.19	2.640	141.083	117.085	33.09800	16/NMBD/2020-21	17.02.2021	04.01.2021	3080	25.02	5.04	0.000000	0.00	117.08500	
TOTAL																	619.99900	

- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer
RWD, Works Division,
Baist

14/01/24

Name of Customer : Sunny Engineering Works
Name of Work : Gangail to Potheiya
Road :
Lab Job number :
Date : 10-01-2021
Section No. : 59


Test Date : 10-01-2021
Road Name : Gangail to Potheiya
Machine No. :
Road Type : (R) RURAL ROAD
Start S No. :
Side :
Start E No. :
Interval :
Weather :
UV Range : 828 To 5000 mm/km
Dist Range : 0 To 2.3 0.1 * 1000 m
Start Location :
End Location :
Equation : $Y = 0 * X^2 + 0.914 * X + 274.50$

Print Generate Report and Graph

Redraw Graph

Map View

File C:\Users\DELL\Desktop\10.01.2021\sunny ENG WORKS.xlsx Section No. 59. Egn : $Y = 0 * X^2 + 0.914 * X$
 Name of Customer : Sunny Engineering Works, Name of Work : Road : Gangail to Potheiya, Lab Job number :

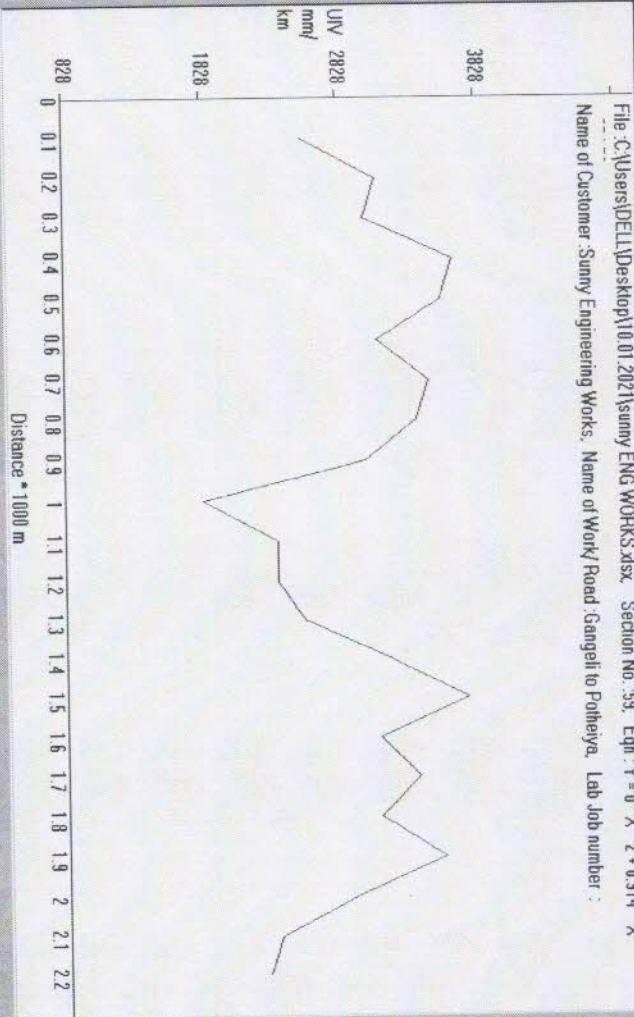

10/1/2021

Date	Time	Section	Length	Bumps	Speed	OR	IRI\TEGORY	Latitude	Longitude	Event	
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
10/1/21	17:26:0	59	0.1	250	10.1	2500	2559	G	26.207	87.635823	Normal
10/1/21	17:26:22	59	0.1	310	10.1	3100	3107	G	26.1577	87.636397	Normal
10/1/21	17:27:0	59	0.1	300	20.2	3000	3016	G	26.725	87.636262	Normal
10/1/21	17:28:0	59	0.1	370	20.2	3700	3656	G	26.12	87.636447	Curve
10/1/21	17:28:44	59	0.1	360	20.2	3600	3564	G	25.999598	87.637305	Curve
10/1/21	17:29:19	59	0.1	310	20.2	3100	3107	G	25.999332	87.638282	Normal
10/1/21	17:30:0	59	0.1	350	10.1	3500	3473	G	25.998898	87.638955	Culvert
10/1/21	17:31:5	59	0.1	340	10.1	3400	3382	G	25.998158	87.638518	Curve
10/1/21	17:31:40	59	0.1	300	20.2	3000	3016	G	25.997272	87.638585	Curve
10/1/21	17:32:50	59	0.1	170	20.2	1700	1828	G	25.996345	87.638518	Normal
10/1/21	17:34:0	59	0.1	230	10.1	2300	2376	G	25.99546	87.639175	Curve
10/1/21	17:34:35	59	0.1	230	10.1	2300	2376	G	25.994732	87.639175	Curve
10/1/21	17:35:11	59	0.1	250	10.1	2500	2559	G	25.994238	87.64	Normal
10/1/21	17:36:21	59	0.1	320	10.1	3200	3199	G	25.993508	87.640285	Curve
10/1/21	17:37:0	59	0.1	380	10.1	3800	3747	G	25.992643	87.64005	Speed Breaker
10/1/21	17:39:18	59	0.1	310	20.2	3100	3107	G	25.99201	87.639965	Normal
10/1/21	17:39:18	59	0.1	340	10.1	3400	3382	G	25.991957	87.639932	Speed Breaker
10/1/21	17:41:39	59	0.1	310	10.1	3100	3107	G	25.991628	87.639763	Normal
10/1/21	17:51:39	59	0.1	360	10.1	3600	3564	G	25.990845	87.639258	Normal
Total			1.9			57900	58125				
Average						3047.37	3059.21				

$$Y = 0 * X^2 + 0.914 * X + 274.50$$

OFFICE OF THE EXECUTIVE ENGINEER R.W.D. REGIONAL
LABORATORY, PURNER, (BIHAR)
RESULT OF BITMEN CONTENT OF MIX SAMPLE

Name of work Maint-7 road from Gangaoli Name of Division Baisi
to Pottiyar road.
Package no./ngt.no. MR/3054 Name of Agency M/S Sunny Engineering works
Sample Collected by A.E.RWA(W) sub-div. Anand LT NO. 04 dt-03/01/2021
Location 1500M. Wt. of sample taken 1000gm.

Sl.No.	Sample No.	Identification No.	Wt. of sample b.c.	Wt. of sample a.c.	Loss wt.	Average	% of bitmen content	Remarks
1.	P	G1	306	291	15.0			
2.	Q	G2	317	302	15.0	15.33	5.06%	
3.	R	G3	331	315	16.0			

Acceptable

Copy to Executive Engineer RWA(W) Div. Baisi

Suprntending Engineer

Chief Engineer Bihar Patna

K. Jyoti
LA 07/01/2021

[Signature]
07/01/21

AN-3
07/01/21
EXECUTIVE ENGINEER
RURAL WORKS DEPT.
REGIONAL LABORATORY
PURNERA
