

कार्यालय
कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, बिक्रमगंज (रोहतास)।

पत्रांक...1723/20...../बिक्रमगंज/दिनांक...27/11/2021

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।

सेवा में,

नोडल पदाधिकारी, (MR-3054)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के विरुद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति 2018 (MR-3054) योजनान्तर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अध्याचना विहित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनुलग्नक:-यथोक्त।

विश्वासभाजन

[Signature] 27/11/21


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, बिक्रमगंज।

[Signature]
27/11/21

Requisition Format for Scheme Head- MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)
Name of Works Division:- Bikramganj

Sl. No.	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter no. & DT.	Administrative Approval		Agreement Amount (in Lakhs)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakhs)	Up-to-Date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length	Amount of (in Lakhs)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 Bikramganj/02	Bikramganj Natarwar Road to Khirodhar Pur Road	10301001037	10301001037 139/2019-2065 DT.-04.07.2019	2.7	103.7477	60.80765	25.87756	54 MBD/2019-20 Date-13.02.2020	07.10.2020	-	2754.9	25	5.1	0.00	0.00	41.71495	BT Complete
2	MR-N/19-20 Bikramganj/02	Sasaram Bikramganj Road - Bensagar Village	10301002056	10301002056 139/2019-2065 DT.-04.07.2019	3.15	84.441	52.04483	18.35252	54 MBD/2019-20 Date-13.02.2020	07.10.2020	-	2715.61	25	5.1	31.22688	31.22688	20.81795	BT Complete
3	MR-N/19-20 Bikramganj/11	Badi Canal to Bageya Path	10301002051	10301002051 139/2019-2065 DT.-04.07.2019	1.40	53.609	31.92139	14.22985	66/MBD/2019-20 Date-20.03.2020	29.10.2020	-	2642.71	25	5.1	27.46000	27.46000	4.461	BT Complete
4	MR-N/19-20 Bikramganj/11	Natwar P.W.D. Path - Rauni Via Isralpura	10301302024	10301302024 139/2019-6282 DT.-02.12.19	2.10	98.025	72.37400	24.935	16MBD/2020-21 Dt.-30.06.2020	23.03.2021	-	2709.54	25	5.02	57.89920	57.89920	14.474	BT Complete

- 1 Signed Hard Copy and Soft Copy (in excel) of Recorded IRI is enclosed.
2 UP- to date Physical Progress has been Uploaded in MIS.


Executive Engineer
RWDD, Works Div. Bikramganj
27/01/21

Name of Customer: M/S Kaimur Developers Private
 Name of Work: Netwar PWD Road to Ravani via
 Road:
 Lab Job number: 63
 Date: 18-11-2020
 Section No. 63

Test Date: 18-11-2020 Road Name: Netwar PWD Road to Ravani via
 Machine No: 405 Road Type: (R) RURAL ROAD
 Start S No: 2328 Side: Bhromgarhi Interval
 Start E No: 2351
 Weather: Normal UV Range: 935 To 4000 mm/Km
 Start Location: 35 2328.841 Dist Range: 0 To 0.7 0.028 * 1000 m
 End Location: 35 21252.841 Equation: $Y = 0.0 * X^2 + 0.877 * X + 181.3$


Print Generate Report and Graph

Redraw Graph

Map View

File: C:\Users\BRRDA112\Desktop\sisco\181119\44.Ms. Section No. 63. Eqn: $Y = 0.0 * X^2 + 0.877 * X + 181.3$

Name of Customer: M/S Kaimur Developers Private Limited, Name of Work: Road: Netwar PWD Road to Ravani via

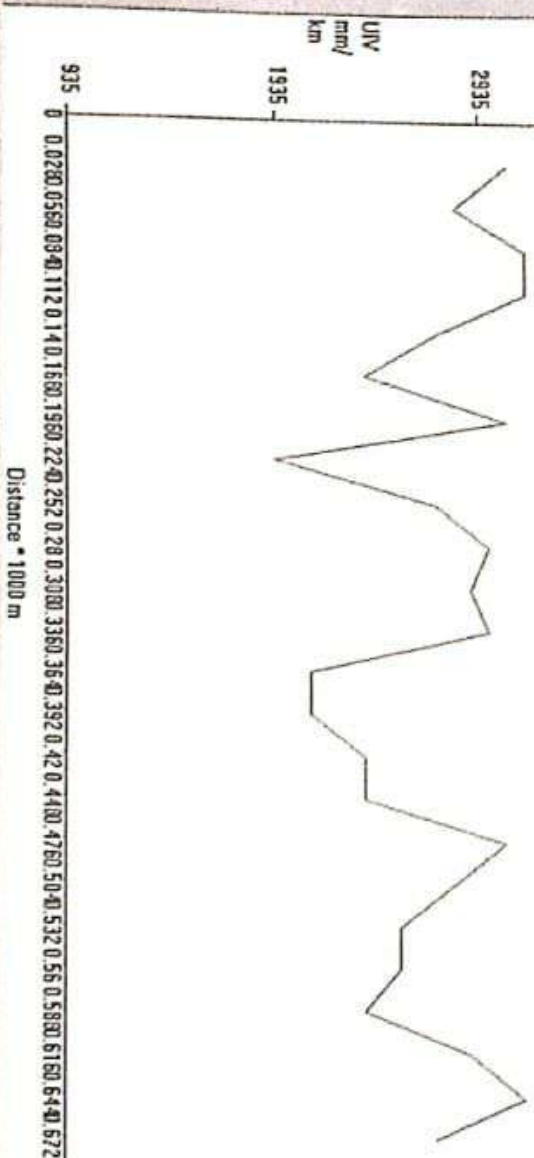

CP5
 23/11/20
 E.E

Name of Road- Natwar PWD Road to Ravani via Esaralpur

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEG ORY ROAD	Latitude	Longitude	Event
18/11/20	15:17:29	63	0.1	330	20.2	3300	3075	G	25.229257	84.180638	Normal
18/11/20	15:18:3	63	0.1	300	30.3	3000	2812	G	25.228295	84.180673	Normal
18/11/20	15:18:3	63	0.1	340	10.1	3400	3163	G	25.227297	84.180572	Normal
18/11/20	15:18:39	63	0.1	340	20.2	3400	3163	G	25.22648	84.180487	Normal
18/11/20	15:19:0	63	0.1	290	10.1	2900	2724	G	25.22557	84.18037	Normal
18/11/20	15:19:14	63	0.1	250	10.1	2500	2373	G	25.224593	84.180302	Normal
18/11/20	15:20:0	63	0.1	330	10.1	3300	3075	G	25.223637	84.180387	Normal
18/11/20	15:20:25	63	0.1	200	10.1	2000	1935	G	25.22287	84.180773	Speed Breaker
18/11/20	15:21:0	63	0.1	290	20.2	2900	2724	G	25.22209	84.181043	Normal
18/11/20	15:21:0	63	0.1	320	30.3	3200	2987	G	25.22118	84.181043	Normal
18/11/20	15:21:35	63	0.1	310	30.3	3100	2900	G	25.220232	84.180958	Curve
18/11/20	15:21:35	63	0.1	320	20.2	3200	2987	G	25.219798	84.181515	Normal
18/11/20	15:22:0	63	0.1	220	30.3	2200	2110	G	25.218873	84.181515	Normal
18/11/20	15:22:10	63	0.1	220	30.3	2200	2110	G	25.218002	84.181312	Normal
18/11/20	15:22:10	63	0.1	250	40.4	2500	2373	G	25.217185	84.180892	Normal
18/11/20	15:22:10	63	0.1	250	40.4	2500	2373	G	25.216477	84.180185	Curve
18/11/20	15:22:10	63	0.1	330	30.3	3300	3075	G	25.215598	84.180318	Normal
18/11/20	15:22:46	63	0.1	300	30.3	3000	2812	G	25.214773	84.18079	Normal
18/11/20	15:23:0	63	0.1	270	20.2	2700	2549	G	25.213975	84.181295	Normal
18/11/20	15:23:0	63	0.1	270	20.2	2700	2549	G	25.213153	84.18175	Normal
18/11/20	15:23:21	63	0.1	250	20.2	2500	2373	G	25.212953	84.182457	Normal
18/11/20	15:24:32	63	0.1	310	10.1	3100	2900	G	25.21278	84.18335	Normal
18/11/20	15:25:0	63	0.1	340	10.1	3400	3163	G	25.212653	84.184292	Normal
18/11/20	15:25:7	63	0.1	290	10.1	2900	2724	G	25.21252	84.184848	Normal
Total Length			2.40								

$$Y = 0 * X^2 + 0.877 * X + 181.3$$

$$X = 2900$$

$$Y = 2724$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

495

Redi
23/11/20
