

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, हिलसा (नालन्दा)।
Email:- ee.hilsa.rwd@gmail.com

पत्र संख्या 11866/217

हिलसा/दिनांक 27-7-2021

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

सेवा में,

नोडल पदाधिकारी,
MR 3054,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:-

नई अनुरक्षण निति 2018 शीर्ष के अंतर्गत वित्तीय वर्ष 2021-22 में व्यय हेतु
आवंटन की मांग।

महाशय,

उपर्युक्त विषयक नई अनुरक्षण निति 2018 शीर्ष के अंतर्गत वित्तीय वर्ष 2021-22 में
व्यय हेतु संलग्न विवरणी के अनुसार रू0 246.39846 (रू0 दो करोड़ छियालीस लाख उनचालीस
हजार आठ सौ छियालीस मात्र) रुपये का आवंटन उपलब्ध कराने की कृपा की जा ताकि किये
गये कार्यों का भुगतान किया जा सके।

अनु:- यथोक्त।

विश्वासभाजन

27/7/21

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, हिलसा।

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Hilsa

SI No.	Package No.	Name of Road	Project ID as per MIS	Administ rative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks	
					Length (In km)	Amount of (In Lakh)	Initial Rectificatio n with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
Mamurva																			
1	RM/NA/HIL /19/0002	Path to Shekhpura Rupaspur	NEA230002773	539/08- 02-2019	4.512	155.44800	98.73962	46.58258	25/MBD /2019-20	03.04.2020	18.07.21	2860	25.00	5.00	0.00	0.00	98.73962	Surface Work Complete	
2	RM/NA/HIL /19/0002	Ekangar Bihar PWD to Dhanbaba Road	NEA230002779	539/08- 02-2019	1.222	42.94300	27.63245	12.43379	25/MBD /2019-20	03.04.2020	18.07.21	3085	25.00	5.00	0.00	0.00	27.63245	Surface Work Complete	
3	RM/NA/HIL /19/0003	Hilsa fatuha road to gulani	10200802039	1826/24. 06.19	0.554	16.37570	9.43098	5.70937	05/MBD /2020-21	27.09.21	18.07.21	2747	25.00	5.00	0.00	0.00	9.43098	Complete	
4	RM/NA/HIL /19/0003	hilsa fatuha road to juniyar	10200802040	1826/24. 06.19	1.420	61.01000	41.28209	14.69668	05/MBD /2020-21	27.09.21	18.07.21	2641	25.00	5.00	0.00	0.00	41.28209	Complete	
5	RM/NA/HIL /19/0003	Teka bihar milki path to mahdumpur	10200901011	1826/24. 06.19	1.500	65.85900	44.16840	15.43384	05/MBD /2020-21	27.09.21	18.07.21	3203	25.00	5.00	0.00	0.00	44.16840	Complete	
6	RM/NA/HIL /19/0003	Hilsa harbanspur to kurseta	10200802041	1826/24. 06.19	0.890	37.88040	25.14492	9.17454	05/MBD /2020-21	27.09.21	18.07.21	2843	25.00	5.00	0.00	0.00	25.14492	Complete	
7	RM/NA/HIL /20/0005	Diawan-Berthu Rd. to Khokhana	10200802022	2775/19. 08.2020	0.450	22.99200	15.71172	4.67360	21/MBD/ 2020-21	26.12.21	27.07.21	2245	25.00	5.00	0.00	0.00	15.71172	Surface Work Complete	
TOTAL																		246.39846	

1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.


2 Up-to-date Physical Progress has been uploaded in MIS.

Executive Engineer

RWD, Works Division, Hilsa

Signature

File : F:\18071543.Xls, Section No. : 58, Egn : $Y = 0 * X^2 + 0.898 * X + 377.8$
Name of Customer : MS Global Solutions, Name of Work/ Road : Dhanawan Path to Shekhpura Rupaspur, Lab Job

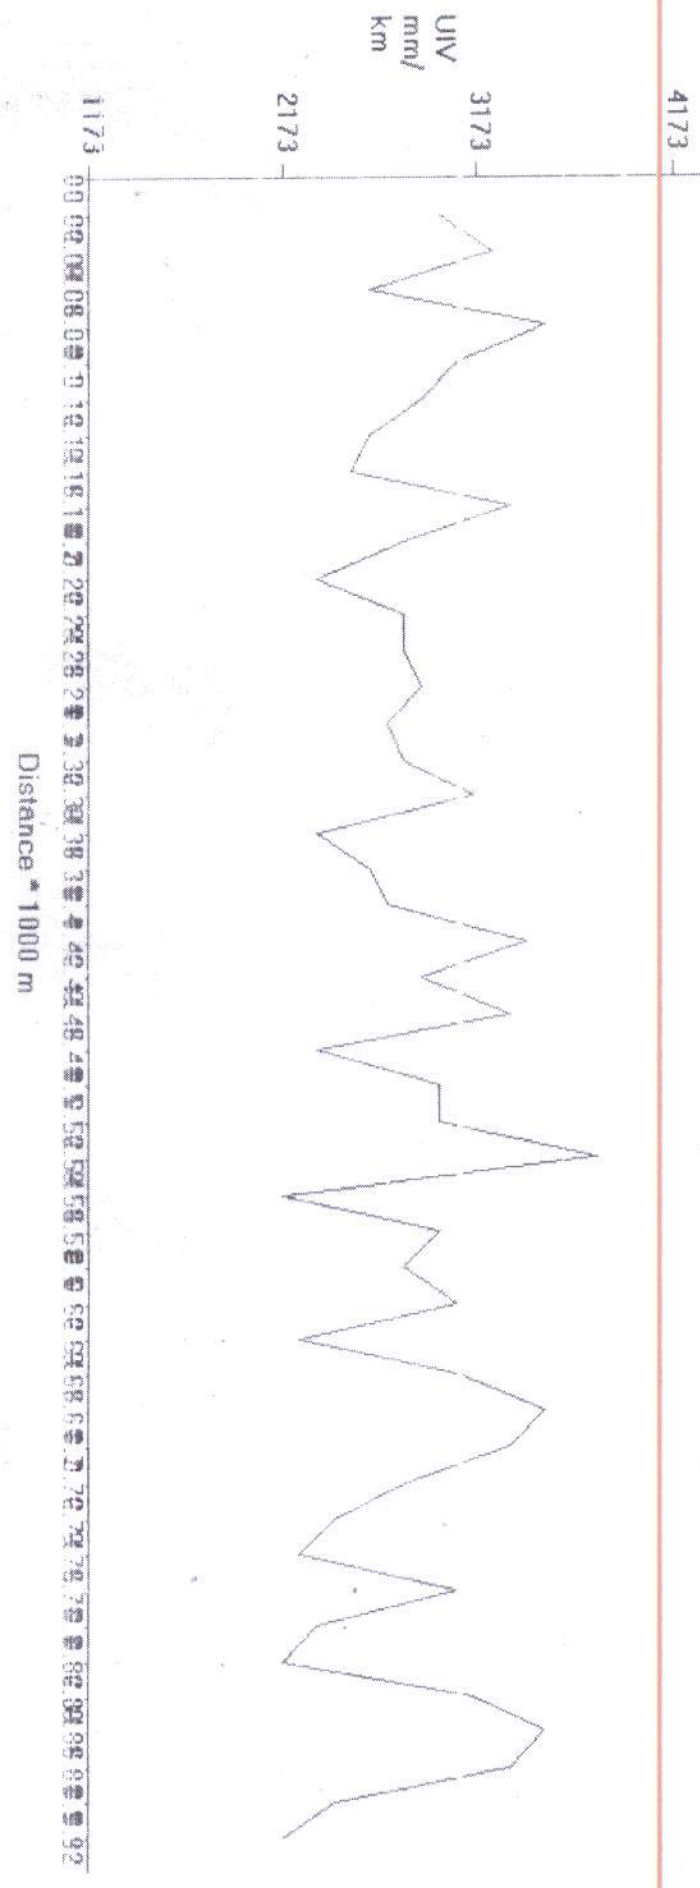

Signature
18/7/2021
J. S. Kumar

Signature
Executive Engineer
Rural Works Department
Works Division, Hissa

Name of Contractor:-MS Global Solutions

Name of Road:-Dhanawan Path to Shekhpura Rupasapur

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	IRI	Latitude	Longitude	Event
		No.										
18/7/21	15: 3: 33	58	0.1	290	0	2900	2982	G	4	25.23296	85.389882	Normal
18/7/21	15: 3: 33	58	0.1	320	20.2	3200	3251	G	4.32	25.23308	85.390823	Curve
18/7/21	15: 4: 8	58	0.1	250	30.3	2500	2622	G	3.57	25.23335	85.39177	Normal
18/7/21	15: 4: 8	58	0.1	350	20.2	3500	3520	G	4.64	25.23426	85.39182	Curve
18/7/21	15: 4: 8	58	0.1	300	20.2	3000	3071	G	4.11	25.23518	85.39178	Normal
18/7/21	15: 4: 44	58	0.1	280	20.2	2800	2892	G	3.89	25.23609	85.39177	Curve
18/7/21	15: 5: 0	58	0.1	250	30.3	2500	2622	G	3.57	25.23699	85.39173	Normal
18/7/21	15: 5: 0	58	0.1	240	30.3	2400	2533	G	3.46	25.23792	85.3918	Normal
18/7/21	15: 5: 19	58	0.1	330	10.1	3300	3341	G	4.43	25.23887	85.391835	Curve
18/7/21	15: 5: 19	58	0.1	270	20.2	2700	2802	G	3.79	25.23902	85.390908	Normal
18/7/21	15: 5: 54	58	0.1	220	30.3	2200	2353	G	3.24	25.23902	85.389982	Normal
18/7/21	15: 6: 0	58	0.1	270	30.3	2700	2802	G	3.79	25.23908	85.388888	Curve
18/7/21	15: 6: 0	58	0.1	270	20.2	2700	2802	G	3.79	25.23844	85.388332	Normal
18/7/21	15: 6: 29	58	0.1	280	30.3	2800	2892	G	3.89	25.23805	85.387542	Normal
18/7/21	15: 6: 29	58	0.1	260	20.2	2600	2712	G	3.68	25.23773	85.38668	Curve
18/7/21	15: 7: 0	58	0.1	270	20.2	2700	2802	G	3.79	25.23748	85.385823	Curve
18/7/21	15: 7: 5	58	0.1	310	20.2	3100	3161	G	4.22	25.23718	85.384865	Curve
18/7/21	15: 7: 5	58	0.1	220	30.3	2200	2353	G	3.24	25.23642	85.384697	Normal
18/7/21	15: 7: 5	58	0.1	250	30.3	2500	2622	G	3.57	25.23546	85.384848	Normal
18/7/21	15: 7: 40	58	0.1	260	20.2	2600	2712	G	3.68	25.23455	85.384763	Curve
18/7/21	15: 8: 15	58	0.1	340	10.1	3400	3431	G	4.54	25.23387	85.385	Curve
18/7/21	15: 8: 15	58	0.1	280	10.1	2800	2892	G	3.89	25.23311	85.385387	Normal
18/7/21	15: 8: 51	58	0.1	330	20.2	3300	3341	G	4.43	25.23259	85.386178	Normal
18/7/21	15: 9: 0	58	0.1	220	20.2	2200	2353	G	3.24	25.23243	85.387137	Normal

Y = 0 * X ^ 2 + 0.898 * X + 377.8		
X = 1.3636		
Y = 12622		
(R) RURAL ROAD		
Good	Average	Poor
<4000	4001-5000	>5001

Super 18/7/2021
sethupur

Executive Engineer
Rural Works Department
Works Division, HHSa

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY	IRI	Latitude	Longitude	Event
		No.						ROAD				
18/7/21	15: 9: 0	58	0.1	290	30.3	2900	2982	G	4	25.23234	85.388097	Normal
18/7/21	15: 9: 26	58	0.1	290	30.3	2900	2982	G	4	25.23231	85.389157	Normal
18/7/21	15: 9: 26	58	0.1	380	20.2	3800	3790	G	4.96	25.23162	85.389477	Curve
18/7/21	15: 10: 1	58	0.1	200	20.2	2000	2173	G	3.02	25.23085	85.388972	Normal
18/7/21	15: 10: 1	58	0.1	290	20.2	2900	2982	G	4	25.22999	85.389023	Curve
18/7/21	15: 10: 1	58	0.1	270	30.3	2700	2802	G	3.79	25.22914	85.388737	Normal
18/7/21	15: 10: 36	58	0.1	300	40.4	3000	3071	G	4.11	25.22829	85.38867	Normal
18/7/21	15: 10: 36	58	0.1	210	40.4	2100	2263	G	3.13	25.2274	85.388618	Normal
18/7/21	15: 10: 36	58	0.1	300	40.4	3000	3071	G	4.11	25.22643	85.388552	Normal
18/7/21	15: 11: 0	58	0.1	350	30.3	3500	3520	G	4.64	25.22543	85.38837	Curve
18/7/21	15: 11: 12	58	0.1	330	20.2	3300	3341	G	4.43	25.22533	85.387407	Curve
18/7/21	15: 11: 12	58	0.1	270	20.2	2700	2802	G	3.79	25.22456	85.387137	Normal
18/7/21	15: 11: 47	58	0.1	230	30.3	2300	2443	G	3.35	25.22369	85.387087	Normal
18/7/21	15: 11: 47	58	0.1	210	40.4	2100	2263	G	3.13	25.22275	85.38702	Normal
18/7/21	15: 12: 0	58	0.1	300	40.4	3000	3071	G	4.11	25.22189	85.386968	Normal
18/7/21	15: 12: 0	58	0.1	220	40.4	2200	2353	G	3.24	25.22091	85.386952	Normal
18/7/21	15: 12: 22	58	0.1	200	40.4	2000	2173	G	3.02	25.22	85.38702	Normal
18/7/21	15: 12: 22	58	0.1	310	20.2	3100	3161	G	4.22	25.21927	85.38744	Normal
18/7/21	15: 12: 22	58	0.1	350	20.2	3500	3520	G	4.64	25.21922	85.38838	Normal
18/7/21	15: 13: 0	58	0.1	330	20.2	3300	3341	G	4.43	25.21851	85.388872	Normal
18/7/21	15: 13: 0	58	0.1	230	20.2	2300	2443	G	3.35	25.21757	85.38872	Normal
18/7/21	15: 13: 33	58	0.012	200	30.3	2000	2173	G	3.02	25.21716	85.388635	Normal
Total			4.512	12720	1161.5	127200	131584		177.26			

by
18/7/2021
28/7/2021

Executive Engineer
Rural Works Department
Works Division, HWS
27/7/21
